




START HERE THURSDAY

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: 03H5J3 / 035B Size: 100 x 100 ft
 Date Started: 1-28-09
 Date Completed: 1-29-09

Work Order No.:
 UXO Supervisor: Lavchner, Clark
 UXO Technician(s): Adams, Larson
Remington

North
 Direction

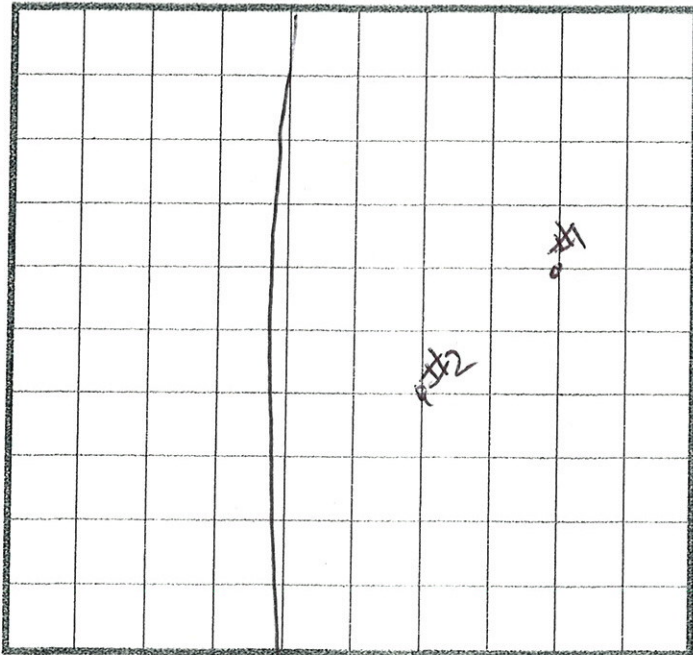

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
				1	6

MEC ID	NOMENCLATURE	DEPTH
1	SF signal illum ground M125 Series (empty)	3"
2	SF signal illum ground M125 Series (empty)	3"
1	signal illum ground M125 (mt)	3"
1		

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1-29-09	<i>[Signature]</i>	
Excavation Complete	1-29-09	<i>[Signature]</i>	
Quality Control Complete	2/4/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Work Order No.:

Grid No.: C24575 Size: 100 x 100 ft


UXO Supervisor: L. Avchner

Date Started: 1-28-09

UXO Technician(s): Larav Adams Remington

Date Completed: 1-28-09

North
Direction

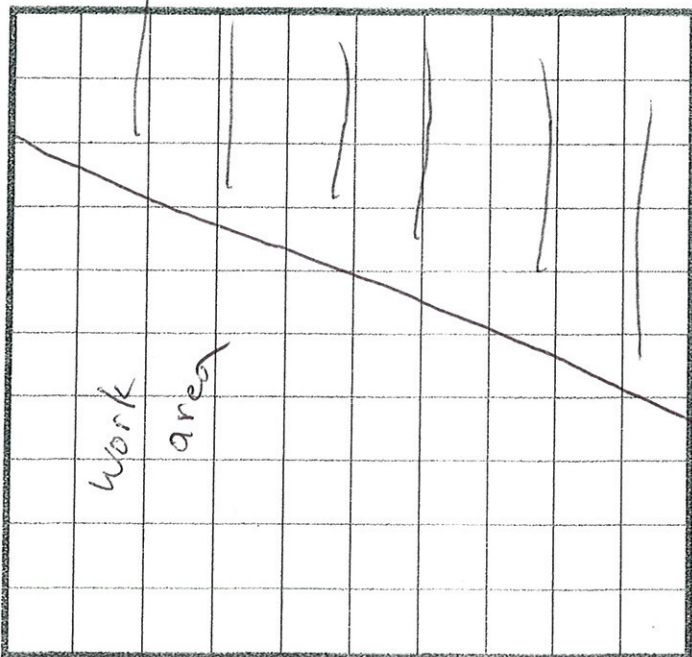

Total Anomalies	Total Excavations	Anomalies > ____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
106	106	-	-	-	2

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1-28-09	<i>[Signature]</i>	20090128-04-01
Excavation Complete	1/28/09	<i>[Signature]</i>	
Quality Control Complete	1/29/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Work Order No.:

Grid No.: C3H536 Size: 100 x 100 ft


UXO Supervisor: L. Avchner

Date Started: 1-28-09

UXO Technician(s): Adams, Larsen, Remington

Date Completed: 1-28-09

North
Direction

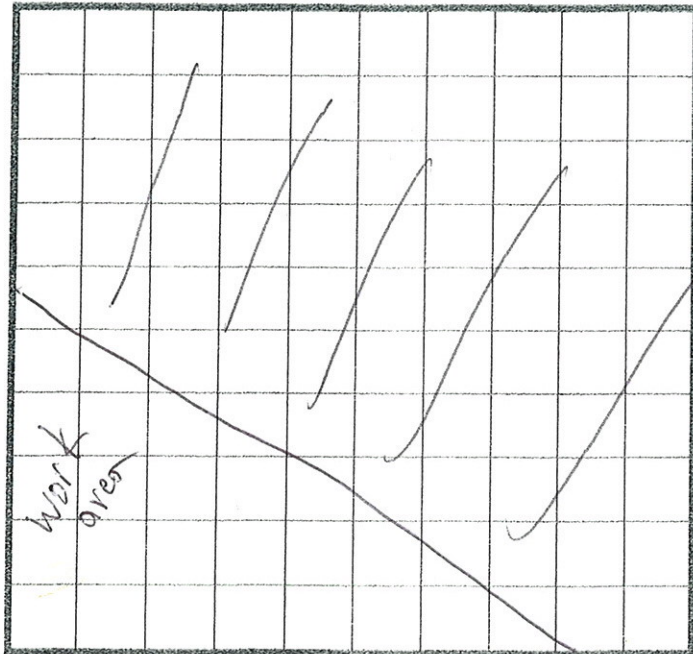

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
60	60	-	-	-	15

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1-26-09	<i>[Signature]</i>	20090128-02-01
Excavation Complete	1/28/09	<i>[Signature]</i>	
Quality Control Complete	1/29/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

4/24 SM




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C34534 Size: 100 x 100 ft
 Date Started: 1-28-09
 Date Completed: 1-28-09

Work Order No.: _____
 UXO Supervisor: LAuchner
 UXO Technician(s): Adams Lauer
Reminton

North
 Direction

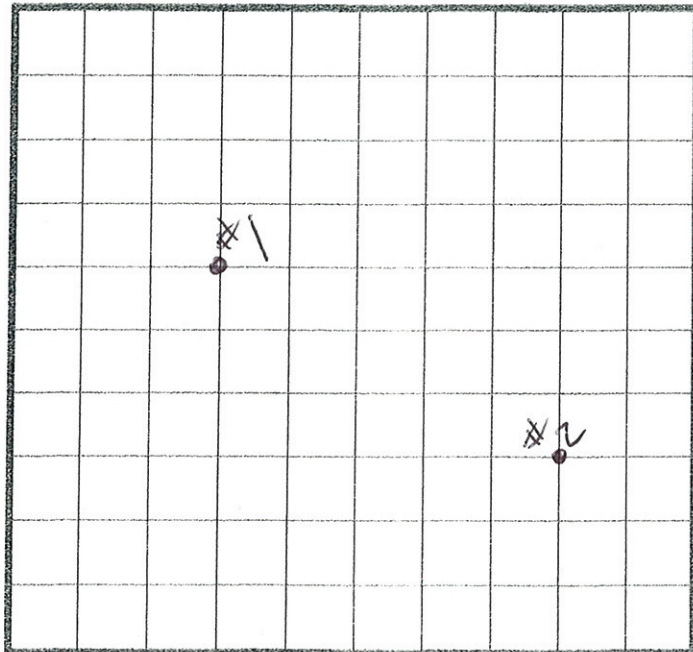

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
120	120	-	-	1	10

SCRAP		DEPTH
MEC	NOMENCLATURE	
# 1	grenade hand smoke M18 series	Empty
# 2	Signal @ illum ground M125 Series	Empty

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1-28-09	<i>[Signature]</i>	20090128-06-01 -07
Excavation Complete	1/28/09	<i>[Signature]</i>	
Quality Control Complete	1/29/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3 H5 D9 Size: 100 x 100 ft
 Date Started: 1/27/09
 Date Completed: 1/27/09

Work Order No.:
 UXO Supervisor: Kristensen
 UXO Technician(s): Caldwell, Clark
Gonzalez, Paz

North
 Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>50</u>	<u>50</u>			<u>1#</u>	<u>3#</u>

MEC	NOMENCLATURE	DEPTH
<u>MD</u>	<u>M49 FLARE SURFACE TRIP (PARTIAL)</u>	

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	<u>1/27/09</u>	<u>[Signature]</u>	<u>20090127_03</u>
Excavation Complete	<u>1/27/09</u>	<u>[Signature]</u>	
Quality Control Complete	<u>1/29/09</u>	<u>[Signature]</u>	
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3 H5 E0 Size: 100 x 100 ft
 Date Started: 1/27/09
 Date Completed: 1/27/09

North
Direction

Work Order No.: _____
 UXO Supervisor: Kristensen
 UXO Technician(s): Caldwell
Paz, GUNZALEZ

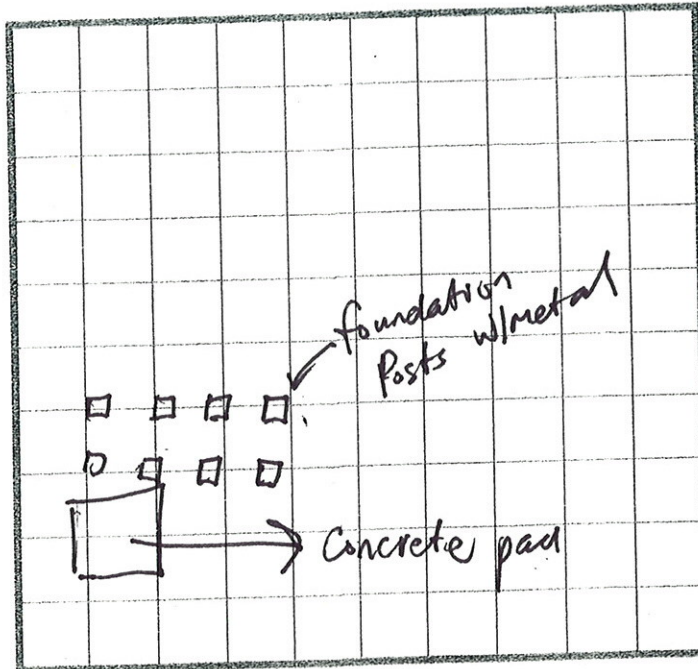

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>50</u>	<u>50</u>				<u>4#</u>

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	<u>1/27/09</u>		<u>20090127_01</u>
Excavation Complete	<u>1/27/09</u>		
Quality Control Complete	<u>1/27/09</u>		
Client Quality Assurance Complete			

1/28/09




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3 H5 C9 Size: 100 x 100 ft
 Date Started: 1/27/09
 Date Completed: 1/27/09

Work Order No.: _____
 UXO Supervisor: Kristenson
 UXO Technician(s): Caldwell
Paz, Gonzalez

North
Direction

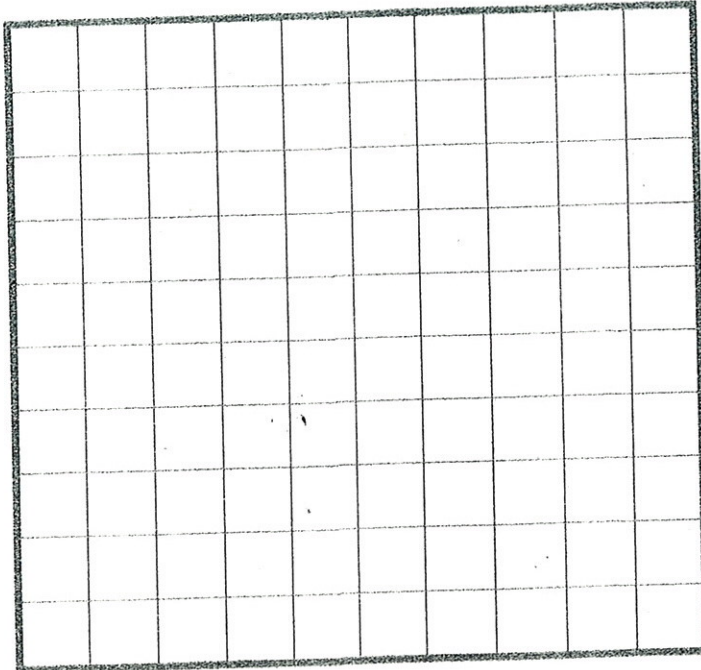

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > ____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
50	50			1#	4#

MEC	NOMENCLATURE	DEPTH
	(1) MRS signal, illum, ground	

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1/27/09		20090127-02
Excavation Complete	1/27/09		
Quality Control Complete	1/27/09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H6D5 Size: 100 x 100 ft
 Date Started: 1-26-09
 Date Completed: 1-27-09




Work Order No.:
 UXO Supervisor: Lauchner
 UXO Technician(s): adams Rensch Remington
Lauchner

North
 Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
105	105				4

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1-27-09		<u>20090127-02-01</u>
Excavation Complete	1/27/09		
Quality Control Complete	1/27/09		
Client Quality Assurance Complete			

4/24
SY



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3H6D4 Size: 100 x 100 ft

Date Started: 1-27-09

Date Completed: 1-27-09


Work Order No.:

UXO Supervisor: Lawchner

UXO Technician(s): Adams, Remington

North
Direction

Larue

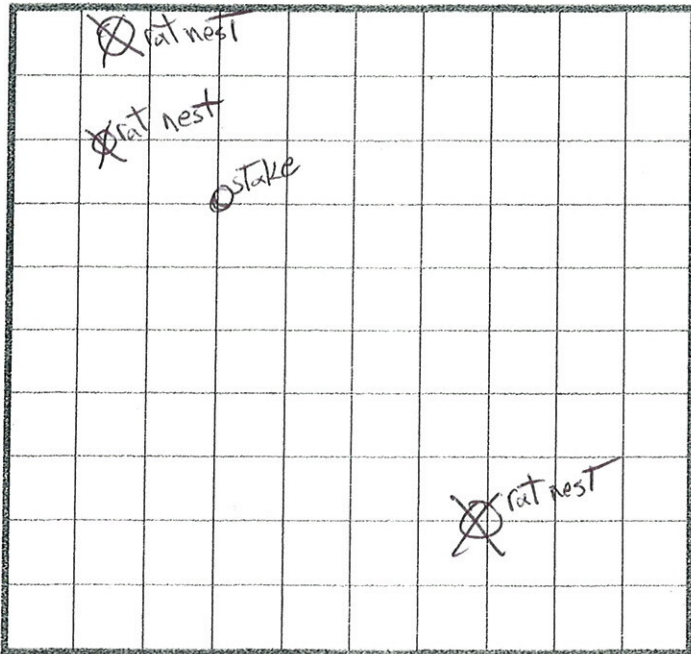

Total Anomalies	Total Excavations	Anomalies > ____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
120	120				5#

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1/27/09	[Signature]	20090127-03-01
Excavation Complete	1/27/09	[Signature]	
Quality Control Complete	1/27/09	[Signature]	METAL STAKE BURIED IN GRID.
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
Grid No.: C3H6E4 Size: 100 x 100 ft
Date Started: 1-27-09
Date Completed: 1-27-09

Work Order No.:
UXO Supervisor: L. Vachner
UXO Technician(s): Loren, Adams, Remington

North
Direction

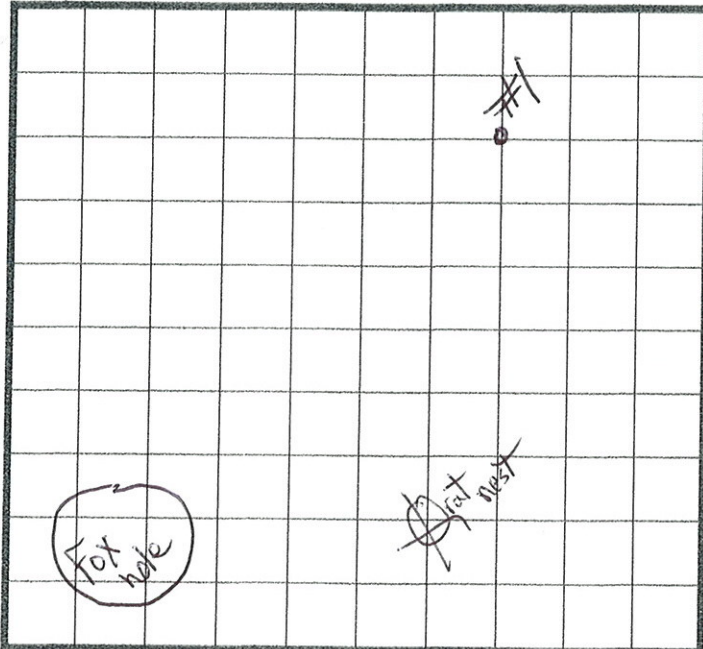

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
160	160			1/2	5

MEC #	NOMENCLATURE	DEPTH
#1	ground illum M125 sericts (empty) (1)	

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1-27-09	<i>[Signature]</i>	Fox hole need to remove oak To work in
Excavation Complete	12709	<i>[Signature]</i>	
Quality Control Complete	1/27/09	<i>[Signature]</i>	20090127-04
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
Grid No.: 5 C346 DØ Size: 100 x 100 ft
Date Started: 1/26/09
Date Completed: 1/26/09

North Direction

Work Order No.:
UXO Supervisor: Kristensen
UXO Technician(s): Caldwell
Paz, GONZALEZ

Total Anomalies	Total Excavations	Anomalies > ___ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>50</u>	<u>50</u>				<u>4#</u>

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	<u>1/26/09</u>	<u>[Signature]</u>	<u>2009 0126-02</u>
Excavation Complete	<u>1/26/09</u>	<u>[Signature]</u>	
Quality Control Complete	<u>1/26/09</u>	<u>[Signature]</u>	
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3 H6 E 1 Size: 100 x 100 ft
 Date Started: 1/26/09
 Date Completed: 1/26/09

North
Direction

Work Order No.:
 UXO Supervisor: Kristensen
 UXO Technician(s): Caldwell, Clark
Paz, Gonzalez, Hendrick

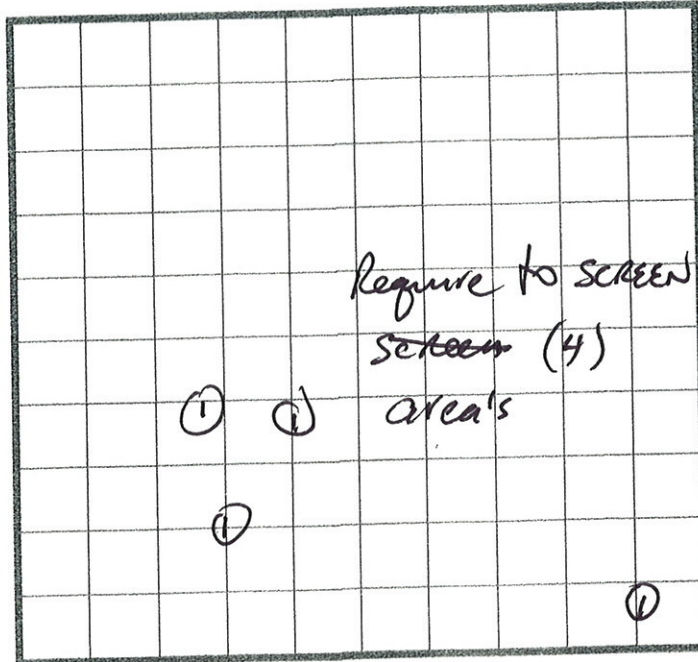

Total Anomalies	Total Excavations	Anomalies > ____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
50	50			2#	3#

MEC	NOMENCLATURE	DEPTH
MD	(1) Fragment MK II PRACTICE GRENADE	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1/26/09	<i>[Signature]</i>	2009 01 26 - 03 - 01
Excavation Complete	1/26/09	<i>[Signature]</i>	
Quality Control Complete	1/26/09	<i>[Signature]</i>	
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3H6E6 Size: 100 x 100 ft
 Date Started: 1-26-09
 Date Completed: 1-26-09

Work Order No.: _____
 UXO Supervisor: LAUHLNER
 UXO Technician(s): Remington Raasch
adams

North
 Direction

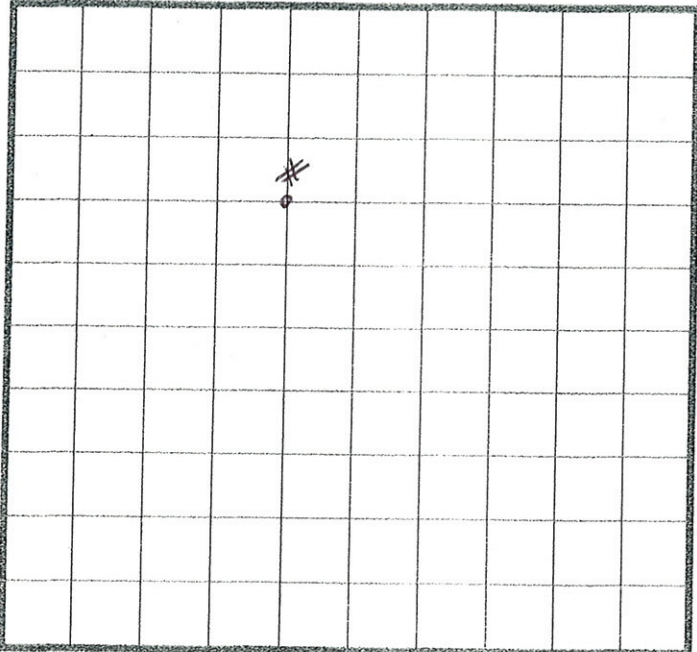

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
175	175	-	-	1/4 lb	10

Scrap		
MEC	NOMENCLATURE	DEPTH
#1	proj 40mm cluster white star m585/empty	

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1-26-09	<i>[Signature]</i>	20090126-09
Excavation Complete	1-26-09	<i>[Signature]</i>	
Quality Control Complete	1/26/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Work Order No.:

Grid No.: C3H6E5 Size: 100 x 100 ft

UXO Supervisor: L Avchner

Date Started: 1-26-09

UXO Technician(s): Adams Roach,

Date Completed: 1-26-09

North
Direction

Reminton

Rat nest

Rat nest

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
110	110	-	-	-	3lbs

MEC	NOMENCLATURE	DEPTH
-		

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1-26-09	<i>[Signature]</i>	Rat nests with rat anomalies
Excavation Complete	1/26/09	<i>[Signature]</i>	
Quality Control Complete	1/26/09	<i>[Signature]</i>	20090126-10
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Work Order No.:

Grid No.: C3 H6D6 Size: 100 x 100 ft

UXO Supervisor: L. Acker

Date Started: 1-26-09

UXO Technician(s): Reminton, Roach

Date Completed: 1-26-09

North
Direction

adams, Smith

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
210	210		-	-	25lbs

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1-26-09	<i>[Signature]</i>	20090126-06
Excavation Complete	1/26/09	<i>[Signature]</i>	
Quality Control Complete	1/26/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

A/24
SU



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3A6E7 Size: 100 x 100 ft

Date Started: 1-26-09

Date Completed: 1-26-09

Work Order No.:

UXO Supervisor: L. Lochner

UXO Technician(s): Adams, Remington

Rush

North
Direction

								#1	

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
				1/2	3/4

Scrap		
MEC #	NOMENCLATURE	DEPTH
#1	Signal illum ground MRS Series (empty)	

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1-26-09		20090126-12
Excavation Complete	1-26-09		
Quality Control Complete	1-26-09		
Client Quality Assurance Complete		1/27/09	



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H6F5 Size: 100 x 100 ft
 Date Started: 1-23-09
 Date Completed: 1-23-09

North
 Direction

Work Order No.:
 UXO Supervisor: T. Clark
 UXO Technician(s): J. LaPee
M. Pass, B. Adams

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>281</u>	<u>278</u>				<u>5</u>

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	<u>1-23-09</u>	<u>[Signature]</u>	<u>20090123_02</u>
Excavation Complete	<u>1-23-09</u>	<u>[Signature]</u>	
Quality Control Complete	<u>1/23/09</u>	<u>[Signature]</u>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Work Order No.:

Grid No: C3H6F7 Size: 100 x 100 ft

UXO Supervisor: T. Clark

Date Started: 1-23-09

UXO Technician(s): J. LaRoc

Date Completed: 1-23-09

North
Direction

M. Passz, B. Adams

Total Anomalies	Total Excavations	Anomalies > ____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
166	159			1	3

MEC	NOMENCLATURE	DEPTH
MO	2.62 Blanks	2"
MO	30 cal blanks	2"

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	1-23-09	<i>T. Clark</i>	20090123_04
Excavation Complete	1-23-09	<i>T. Clark</i>	
Quality Control Complete	1/23/09	<i>J. LaRoc</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3 H5 A8 Size 100 x 100 ft
 Date Started: 1/22/08 09
 Date Completed: 1/22/08 09

Work Order No.: _____
 UXO Supervisor: Kristensen
 UXO Technician(s): Remington
GONZALEZ, Hendrix

North
 Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
40	40				7#

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	1/22/09		20090122-03
Excavation Complete	1/22/09		< ORD3-12209-0001 >
Quality Control Complete	1/23/09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3 H6 D2 Size: 100 x 100 ft
 Date Started: 1/22/08
 Date Completed: 1/22/08

Work Order No.: _____
 UXO Supervisor: Kristensen
 UXO Technician(s): Smith, Hendrix
Remington, Gonzalez

North
Direction

Total Anomalies	Total Excavations	Anomalies > ____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>40</u>	<u>40</u>				<u>5#</u>

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	<u>1/22/09</u>	<i>[Signature]</i>	<u>NO Pict.</u>
Excavation Complete	<u>1/22/09</u>	<i>[Signature]</i>	
Quality Control Complete	<u>1/23/09</u>	<i>[Signature]</i>	
Client Quality Assurance Complete			

4/29 SU

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H4J7 Size 100 x 100 ft
 Date Started: 2-3-09
 Date Completed: 2-3-09

Work Order No.: _____
 UXO Supervisor: T. Clark
 UXO Technician(s): D. Caldwell
B. Smith, E. Gonzalez

North
 Direction

	Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
	2	2		0	0	0

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	2-3-09		
Excavation Complete	2-3-09		
Quality Control Complete	2/4/09		
Client Quality Assurance Complete			

4/24/09

Grid Sweep Log

Project Name/Fort Ord Remediation Program
Grid No: C3H4I5 Size 100 x 100 ft
Date Started: 2-3-09
Date Completed: 2-3-09

North
Direction

Work Order No: _____
UXO Supervisor: T. Clark
UXO Technician(s): D. Caldwell
B. Smith, E. Gonzalez

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>3</u>	<u>2</u>		<u>0</u>	<u>0</u>	<u>0</u>

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	<u>2-3-09</u>	<u>[Signature]</u>	
Excavation Complete	<u>2-3-09</u>	<u>[Signature]</u>	
Quality Control Complete	<u>2/4/09</u>	<u>[Signature]</u>	
Client Quality Assurance Complete			



C3H4I6

15

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H4I6 Size: 100 x 100 ft
 Date Started: 2-3-09
 Date Completed: 2-3-09

North
Direction

Work Order No.: _____
 UXO Supervisor: T. Clark
 UXO Technician(s): D. Caldwell
B. Smith, F. Gonzalez

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
88	86	.	193	6	8

MEC	NOMENCLATURE	DEPTH
185	30 cal Ball -	2"
8	30 cal Blank -	2"

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	2-3-09	<i>[Signature]</i>	<div style="font-size: 24px; font-weight: bold;">2009 0203-02</div> <div style="font-size: 24px; font-weight: bold;">2009 0203-01</div>
Excavation Complete	2-3-09	<i>[Signature]</i>	
Quality Control Complete	2/4/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3H4I7 Size: 100 x 100 ft

Date Started: 2-3-09

Date Completed: 2-3-09

North
Direction

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): D. Caldwell

B. Smith, F. Gonzales

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds Non-MEC Scrap	Pounds MEC Scrap
169	160		1	25	20

MEC	NOMENCLATURE	DEPTH
1-MD	ITLW, Signal ground M126 expended	0"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	2-3-09	<u>[Signature]</u>	20090203-03
Excavation Complete	2-3-09	<u>[Signature]</u>	
Quality Control Complete	2/4/09	<u>[Signature]</u>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H4T8 Size: 100 x 100 ft
 Date Started: 2-3-09
 Date Completed: 2-3-09

Work Order No.: _____
 UXO Supervisor: T. Clark
 UXO Technician(s): D. Caldwell
B. Smith, B. Raasch

North
 Direction

										Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
										189	184		0	0	9

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	2-3-09		20090203-04
Excavation Complete	2-3-09		
Quality Control Complete	2/4/09		
Client Quality Assurance Complete			

A124 SA

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H4I9 Size: 100 x 100 ft
 Date Started: 2-3-09
 Date Completed: 2-3-09

Work Order No.:
 UXO Supervisor: T. Clark
 UXO Technician(s): A. Caldwell
B. Smith, B. Rasch

North
 Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
99	99		15	.25	2

MEC	NOMENCLATURE	DEPTH
15/MO	30 cal Blanks - expended	3'

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	2-3-09	<i>[Signature]</i>	20090203_05
Excavation Complete	2-3-09	<i>[Signature]</i>	
Quality Control Complete	2/4/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H5D7 Size: 100 x 100 ft
 Date Started: 2-3-09
 Date Completed: 2-3-09

Work Order No.: _____
 UXO Supervisor: L. Auckner
 UXO Technician(s): Adams, Paz

North
 Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
160	160			4	8

MEC	NOMENCLATURE	DEPTH
#1	Signal Signal ground illum m125 Series	
#2	Signal ground illum m125 Series	

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	2-3-09	<i>[Signature]</i>	Rat nests + Large Oak areas
Excavation Complete	2-3-09	<i>[Signature]</i>	
Quality Control Complete	2/4/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

20090203 ~~07~~
-06

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H5E6 Size: 100 x 100 ft
 Date Started: 2-3-09
 Date Completed: 2-3-09


North
Direction

Work Order No.:
 UXO Supervisor: W. A. Archer
 UXO Technician(s): Adams, P. S.

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non- MEC Scrap
110	110		-	-	1.5

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	2-3-09		<p>20090203-05-01</p>
Excavation Complete	2-3-09		
Quality Control Complete	2/4/09		
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H5E7 Size: 100 x 100 ft
 Date Started: 2-3-09
 Date Completed: 2-3-09

Work Order No.:
 UXO Supervisor: L Avchener
 UXO Technician(s): Paz, Adams,
Reminton

North
 Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
160	160			1/2 lb	2 lbs

MEC #	NOMENCLATURE	DEPTH
# 1	Subground illum 125 series	

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	2-3-09	<i>[Signature]</i>	Lots of large oak areas 20090203-04-01 -03-01
Excavation Complete	23 09	<i>[Signature]</i>	
Quality Control Complete	2/4/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



CEHHE

ST

Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C3H4J8 Size: 100 x 100 ft

Date Started: 2-2-09

Date Completed: 2-2-09

North
Direction

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): D. Caldwell

B. Raasch, B. Adams

										Total Anomalies	Total Excavations	Anomalies > ____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non- MEC Scrap
										37	33		0	0	1
										MEC	NOMENCLATURE		DEPTH		

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	2-2-09	<i>[Signature]</i>	20090202-05
Excavation Complete	2-2-09	<i>[Signature]</i>	
Quality Control Complete	2/4/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

4/24/09



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3H4J9 Size: 100 x 100 ft

Date Started: 2-2-09

Date Completed: 2-2-09

North
Direction

Work Order No.

UXO Supervisor: T. Clark

UXO Technician(s): D. Caldwell

B. Raasch, B. Adams

Total Anomalies	Total Excavations	Anomalies > ____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
88	84		0	0	2

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	2-2-09	<u>[Signature]</u>	20090202-04
Excavation Complete	2-2-09	<u>[Signature]</u>	
Quality Control Complete	2/4/09	<u>[Signature]</u>	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C3H5J1 Size 100 x 100 ft

Date Started: 2-2-09

Date Completed: 2-2-09

North
Direction

Work Order No

UXO Supervisor: T. Clark

UXO Technician(s): D. Caldwell, B. Lensch

B. Adams

										Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
										137	135		0	.1	3
										MEC	NOMENCLATURE			DEPTH	
										MD	Signal Illum ground M126			3"	

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	2-2-09	<u>T. Clark</u>	20090202-02
Excavation Complete	2-2-09	<u>B. Adams</u>	
Quality Control Complete	2/4/09	<u>B. Adams</u>	
Client Quality Assurance Complete			

4/24/09




20090202

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C345J2 Size: 100 x 100 ft
 Date Started: 1-29-09
 Date Completed: 2-2-09

Work Order No.: _____
 UXO Supervisor: LAuchner, Clark
 UXO Technician(s): Reminton, Lamm
Aldwell, Rasch, Adams

North
 Direction

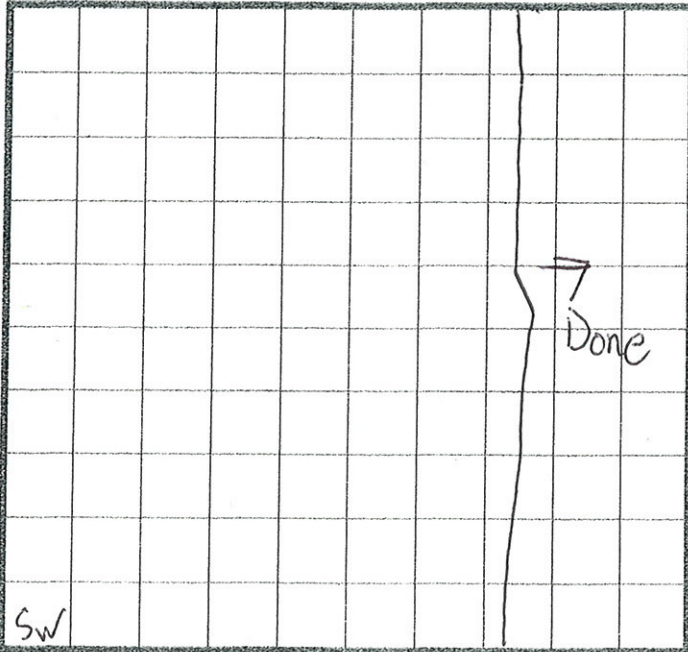

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
140	140		8	.1	12 lbs

MEC	NOMENCLATURE	DEPTH
8	7.62 Ball ammo	3"

Note: Gridlines spaced 10 x 10 ft


ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	2-2-09		20090202-01
Excavation Complete	2-2-09		
Quality Control Complete	2/4/09		
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H5E8 Size: 100 x 100 ft
 Date Started: 2-2-09
 Date Completed: 2-2-09

Work Order No.: _____
 UXO Supervisor: L Archer
 UXO Technician(s): Patz, Smith

North
 Direction

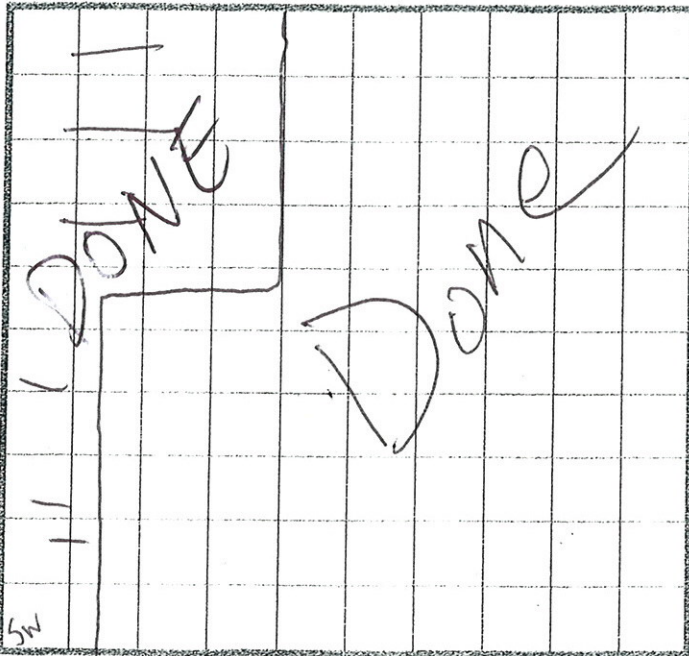

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
95	95				2

MEC	NOMENCLATURE	DEPTH
MD	NONE	

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	2-2-09	<i>[Signature]</i>	
Excavation Complete	2-2-09	<i>[Signature]</i>	
Quality Control Complete	2/4/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3H5E9 Size: 100 x 100 ft

Date Started: 2-2-09

Date Completed: 2-2-09


North
Direction

Work Order No:

UXO Supervisor: LAuckner

UXO Technician(s): Smith Remsten

PaZ

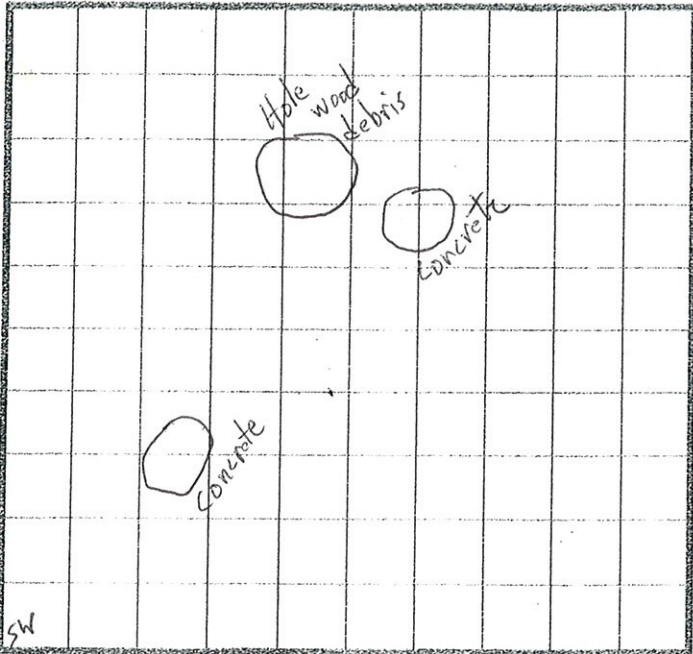

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
110	110				5

MEC	NOMENCLATURE	DEPTH
MD	NONCE	

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	2-2-09	<i>[Signature]</i>	
Excavation Complete	2-2-09	<i>[Signature]</i>	
Quality Control Complete	2/4/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

4/24/09

Grid Sweep Log

Project Name/For: Ord Remediation Program
Grid No: **C3H4G8** Size: 100 x 100 ft
Date Started: **3-23-09**
Date Completed: **3-23-09**

Work Order No.:

UXO Supervisor: *T. Tank*

UXO Technician(s): *B. Smith*

M. Adams

North Direction

Note: Guidelines speed 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
175	160		0	0	125

MEC	NOMENCLATURE	DEPTH

ACTION
Mag Sweep Complete
Excavation Complete
Quality Control Complete
Client Quality Assurance Complete

DATE
3-23-09
3-23-09
3/23/09

SIGNATURE
TRE
TRE
BA

REMARKS:

Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C3H4G7 Size: 100 x 100 ft

Date Started 3-23-09

Date Completed 3-23-09

Work Order No.

UXO Supervisor T. Clark

UXO Technician(s) B. Smith

M. Adams

North
Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>180</u>	<u>160</u>		<u>0</u>	<u>0</u>	<u>25</u>

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	<u>3-23-09</u>	<u>TRC</u>	
Excavation Complete	<u>3-23-09</u>	<u>TRC</u>	
Quality Control Complete	<u>3/23/09</u>	<u>JK</u>	
Client Quality Assurance Complete			

Grid Sweep Log

Project: Hanaford Old Remediation Program
 Grid No: **C3H4G5** Size: 100 x 100 ft
 Date Started: **3-20-09**
 Date Completed: **3-20-09**

Work Order No: _____
 UXO Supervisor: **[Signature]**
 UXO Technician(s): **S. Handrick**
B. Smith, E. Gowdars

North Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non MEC Scrap												
180	160	1		1.0	10												
<table border="1"> <thead> <tr> <th>MEC</th> <th>NOMENCLATURE</th> <th>DEPTH</th> </tr> </thead> <tbody> <tr> <td>MD</td> <td>Signal I/IIa Flare, M125 (1)</td> <td>3"</td> </tr> <tr> <td>MD</td> <td>Small Arms 7-2 30 cal (22)</td> <td>3"</td> </tr> <tr> <td>MD</td> <td>Small arms 5-56 (22)</td> <td>3"</td> </tr> </tbody> </table>						MEC	NOMENCLATURE	DEPTH	MD	Signal I/IIa Flare, M125 (1)	3"	MD	Small Arms 7-2 30 cal (22)	3"	MD	Small arms 5-56 (22)	3"
MEC	NOMENCLATURE	DEPTH															
MD	Signal I/IIa Flare, M125 (1)	3"															
MD	Small Arms 7-2 30 cal (22)	3"															
MD	Small arms 5-56 (22)	3"															

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	3-20-09	[Signature]	
Excavation Complete	3-20-09	[Signature]	
Quality Control Complete	3/20/09	[Signature]	
Client Quality Assessment Complete			

Grid Sweep Log

Project Name: Off Grid Remediation Program
 Grid No: **C3H4G6** Size: 100 x 100 ft
 Date Started: **3-20-09**
 Date Completed: **3-20-09**

Work Order No: _____
 UXO Supervisor: **T. Clark**
 UXO Technician(s): **S. Hendricks**
B. Smith, E. Gonzales

Bench Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non MEC Scrap
210	200		0	0	20
MEC					
NOMENCLATURE					
DEPTH					

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	3-20-09	<i>[Signature]</i>	
Excavation Complete	3-20-09	<i>[Signature]</i>	
Quality Control Complete	3/20/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/On Grid Remediation Program

Grid No. **C3HS H3** Size: 100 x 100 ft

Date Started: **3/20/09**

Date Completed: **3/20/09**

Work Order No.

UXO Supervisor: **Kristensen**

UXO Technician(s): **Matt Kelear, Adams Paz**

North Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non MEC Scrap
40	40			1#	15#
<p>MEC</p> <p>NOMENCLATURE</p> <p>(1) M125 expended signal illum ground</p>					
DEPTH					

ACTION: Mdg Sweep Complete
 Excavation Complete
 Quality Control Complete
 Client Quality Assurance Complete

DATE: 3/20/09
 3/20/09
 3/20/09

SIGNATURE: [Signatures]

REMARKS: Sink w/ 30' pipe

Grid Sweep Log

Project: Hanford/Off Grid Remediation Program

Grid No: C3H5M4H Size: 100 x 100 ft

Date Started: 3/20/09

Date Completed: 3/20/09

Work Order No:


Kristensen

UXO Supervisor

UXO Technician(s): Locklear Paz

Adams

North Direction

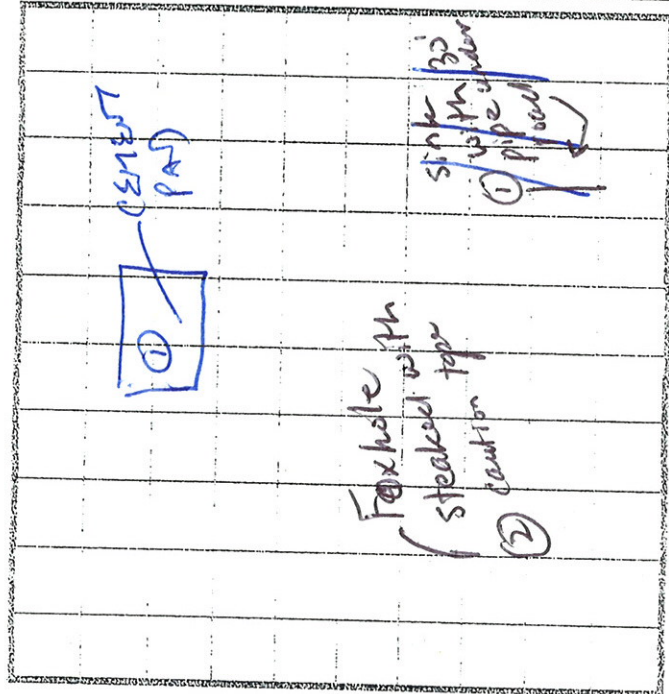

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
40	40			1#	5#

MEC	NOMENCLATURE	DEPTH
	(1) Expended M125 signal illum journal	0

ACTION	DATE	SIGNATURE	RE-MARKS
Mog Sweep Complete	3/20/09	[Signature]	Cement Pad
Excavation Complete	3/20/09	[Signature]	(1) Section of pipe in grid
Quality Control Complete	3/20/09	[Signature]	(1) Cement Pad (2) Foxhole
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. **C3H4G3**

Size 100 x 100 ft

Date Started: **3-20-09**

Date Completed: **3-20-09**


Work Order No.

UXO Supervisor: **T. Clark**

UXO Technician(s): **S. Hendricks**

B. Smith, E. Gonzalez

North
Direction

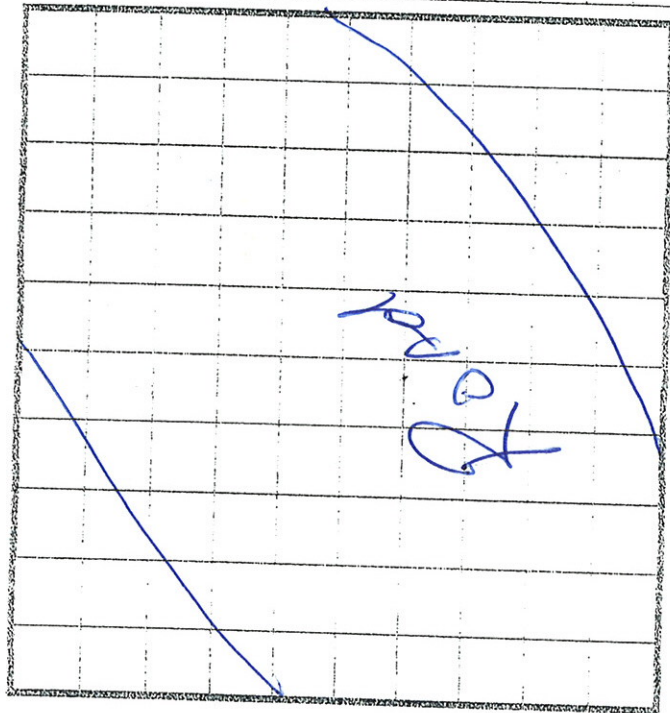

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
35	28		1	.5	.5

MEC	NOMENCLATURE	DEPTH
MD	Squad I/Item, Flare M105 (1)	3"
MD	Small Arms 7.62 (5)	3"
MD	Small Arms 5.56 (14)	3"

ACTION

Mag Sweep Complete

Excavation Complete

Quality Control Complete

Client Quality Assurance Complete

DATE

3-20-09

3-20-09

3/20/09

SIGNATURE

[Signature]

[Signature]

[Signature]

REMARKS

Grid Sweep Log

Project Name/Off Grid Remediation Program

Grid No. **C3H4G4** Size: 100 x 100 ft

Date Started: **3-20-09**

Date Completed: **3-20-09**

Work Order No.

UXO Supervisor: **T. Clark**

UXO Technicians:

S. Hendricks
B. Smith, E. Gonzalez

North Direction

<i>[Large handwritten scribble]</i>									

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
90	80		0	0	10
MEC					
NOMENCLATURE					
DEPTH					

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	3-20-09	<i>[Signature]</i>	
Excavation Complete	3-20-09	<i>[Signature]</i>	
Quality Control Complete	3/20/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

90101
 Old Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C3H5I4 Size 100 x 100 ft

Date Started 3-7-09

Date Completed 3-7-09

Work Order No.

UXO Supervisor Kristensen

UXO Technician(s) Faroe Smith

Remington

North Direction

Total Anomalies	Total Excavations	Anomalies > ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
40	40				5#
<p>MEC</p> <p>NOMENCLATURE</p> <p>DEPTH</p>					

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	RE-MARKS
Mag Sweep Complete	3/9/09	[Signature]	
Excavation Complete	3/9/09	[Signature]	
Quality Control Complete	3/9/09	[Signature]	
Client Quality Assurance Complete	3/9/09	[Signature]	

Grid Sweep Log

Project Handoff Grid Remediation Program

Grid No **C3 HS I3** Size 100 x 100 ft

Date Started **3-9-09**

Date Completed **3-9-09**


Work Order No

UXO Supervisor **Kristensen**

UXO Technician(s) **KAROE Smith**

Remington

North Direction

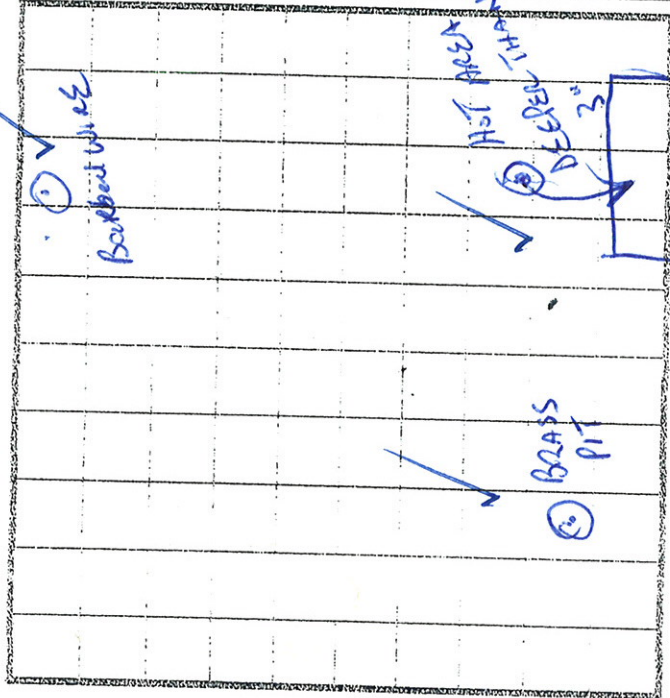

Total Anomalies	Total Excavations	Anomalies > ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
40	40				30#

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION

Mag Sweep Complete

Excavation Complete

Quality Control Complete

Client Quality Assurance Complete

DATE

3/9/09

3/9/09

3/9/09

SIGNATURE

[Signatures]

REMARKS

Barbed wire & fence posts

Grid Sweep Log

Project Name/Ford Old Remediation Program

Grid No C3.HS.HS Size 100 x 100 ft

Date Started 3/9/09

Date Completed 3/9/09

Work Order No

UXO Supervisor

UXO Technician(s)



Kristensen Smith
LALOE
Remington



North Direction

Note: Gridlines spaced 10 x 10 ft												

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>4/0</u>	<u>4/0</u>				<u>22#</u>

MEC	NOMENCLATURE	DEPTH

ACTION	SIGNATURE
Mag Sweep Complete	
Excavation Complete	
Quality Control Complete	
Client Gridline Assurance Complete	

DATE	SIGNATURE
<u>3/5/09</u>	
<u>3/9/09</u>	
<u>3/9/09</u>	


REMARKS
Fence posts

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H512 Size: 100 x 100 ft
 Date Started: 3-2-04
 Date Completed: 3-9-09

Work Order No. _____
 UXO Supervisor: LAUCHNER / KRISTENSEN
 UXO Technician(s): Loren Remington
LAROE, Remington, Smith

North
Direction

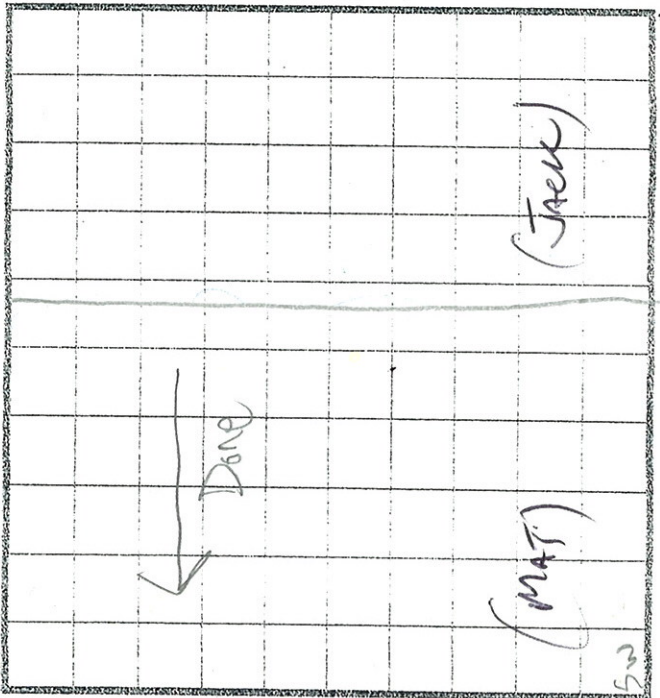

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
30	30				3#

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	3/9/09	<i>[Signature]</i>	
Excavation Complete	3/9/09	<i>[Signature]</i>	
Quality Control Complete	3/9/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H4 H9 Size: 100 x 100 ft
 Date Started: 3-9-09
 Date Completed: 3-9-09

Work Order No.: _____
 UXO Supervisor: T. Clark
 UXO Technician(s): B. Rasch
E. Gonzalez A. St. Louis

North
Direction

Total Anomalies	168
Total Excavations	150
Anomalies > _____ ft.	0
Total MEC Items	0
Pounds MEC Scrap	0
Pounds Non MEC Scrap	35

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE
Mag Sweep Complete	3-9-09	<u>[Signature]</u>
Excavation Complete	3-9-09	<u>[Signature]</u>
Quality Control Complete	3/9/09	<u>[Signature]</u>
Client Quality Assurance Complete		

REMARKS

Grid Sweep Log




Project Name/Fort Ord Remediation Program
 Grid No. C3H4H8 Size: 100 x 100 ft
 Date Started: 3-9-09
 Date Completed: 3-9-09

Work Order No.: _____
 UXO Supervisor: T. Clark
 UXO Technician(s): B. Baasch
E. Gonzalez Parttime

North
 Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>80</u>	<u>60</u>		<u>0</u>	<u>0</u>	<u>15</u>
MEC					DEPTH
NOMENCLATURE					

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	<u>3-9-09</u>		
Excavation Complete	<u>3-9-09</u>		
Quality Control Complete	<u>3/9/09</u>		
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3H4HS Size: 100 x 100 ft
 Date Started: 3-9-09
 Date Completed: 3-9-09

Work Order No.: _____
 UXO Supervisor: T. Clark
 UXO Technician(s): B. Rasch, F. Gonzales
P. Adams

North
 Direction

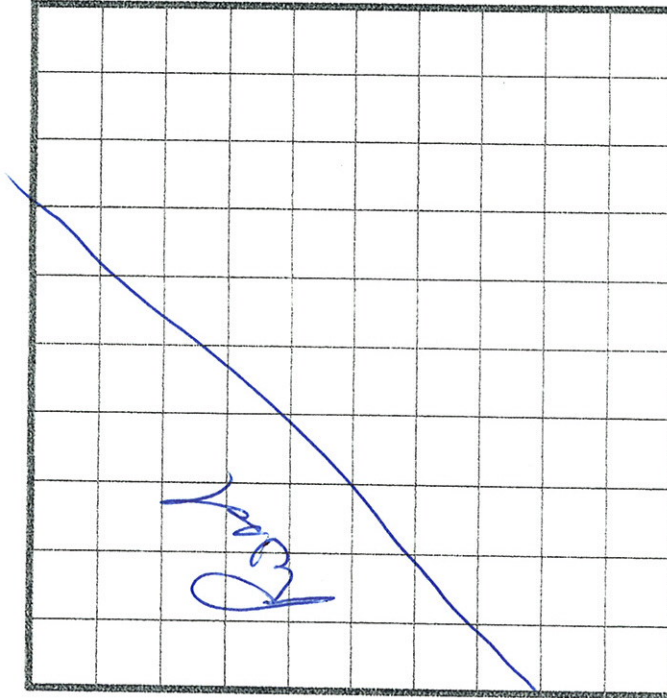

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
140	130		0	75	10

MEC	NOMENCLATURE	DEPTH
MD	Signal Illeg M/MS ③	2"

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	3-9-09	<i>[Signature]</i>	
Excavation Complete	3-9-09	<i>[Signature]</i>	
Quality Control Complete	3/9/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Work Order No.: _____
 UXO Supervisor: T. Clark
 UXO Technician(s): B. Raasch, F. Gonzales
Passive site

Project Name/Fort Ord Remediation Program
 Grid No: C3H4H7 Size: 100 x 100 ft
 Date Started: 3-9-09
 Date Completed: 3-9-09

North
 Direction

X - Anchor Cable

Total Anomalies	Total Excavations	Anomalies > ____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
120	100		0	0	5

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	3-9-09	<u>[Signature]</u>	
Excavation Complete	3-9-09	<u>[Signature]</u>	
Quality Control Complete	3/9/09	<u>[Signature]</u>	
Client Quality Assurance Complete			
			- 1 Anchor for T. Raasch



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3H4 H6 Size: 100 x 100 ft
 Date Started: 3-9-09
 Date Completed: 3-9-09

Work Order No.: _____
 UXO Supervisor: T. Clark
 UXO Technician(s): B. Raasch, E. Gruzicko
RASZ, M. Adams

North
Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>111</u>	<u>95</u>		<u>0</u>	<u>0</u>	<u>3</u>

MEC	NOMENCLATURE	DEPTH
<u>RSP</u>		<u>24</u>

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	<u>3-9-09</u>	<u>[Signature]</u>	
Excavation Complete	<u>3-9-09</u>	<u>[Signature]</u>	
Quality Control Complete	<u>3/9/09</u>	<u>[Signature]</u>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3H4H4 Size: 100 x 100 ft

Date Started: 3-9-09

Date Completed: 3-9-09


Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): B. Rausch, T. Gonzalez

ASS, M. Adams

North
Direction

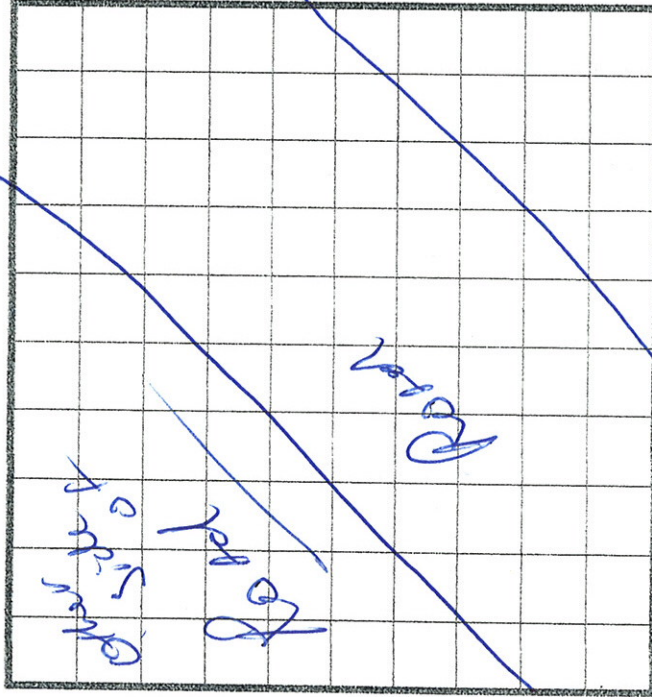

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>1</u>	<u>1</u>		<u>0</u>	<u>0</u>	<u>1</u>

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	<u>3-9-09</u>	<u>T. Clark</u>	
Excavation Complete	<u>3-9-09</u>	<u>T. Clark</u>	
Quality Control Complete	<u>3/9/09</u>	<u>MR</u>	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name: Fort Ord Remediation Program
 Grid No: **C3 H5 15** Size: 100 x 100 ft
 Date Started: **3/9/09**
 Date Completed: **3/9/09**

Work Order No:
 UXO Supervisor: **Kristensen**
 UXO Technician(s): **LAROE Smith**
Remington

North Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
2/0	4/0				12#
MEC					
NOMENCLATURE					
DEPTH					

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	RE-MARKS
Mag Sweep Complete	3/9/09	<i>[Signature]</i>	
Excavation Complete	3/9/09	<i>[Signature]</i>	
Quality Control Complete	3/9/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3H5C7 Size: 100 x 100 ft

Date Started: 3-2-09

Date Completed: 3-2-09

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): B. Smith

B. Raasch

North Direction

x → Anchor.
pounds

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
224	219		2	1	35

MEC	NOMENCLATURE	DEPTH
MD	Signs (Illum. Flame M26 - (2))	2"

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	3-2-09	[Signature]	
Excavation Complete	3-2-09	[Signature]	
Quality Control Complete	4/29/09	[Signature]	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Ford Grid Remediation Program

Grid No. C3H5B7

Size 100 x 100 ft

Date Started 3-2-09

Date Completed 3-2-09

Work Order No.

UXO Supervisor J. T. [Signature]

UXO Technician(s) B. Smith

B. Pasch

North Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
164	150		7	1	8

MEC	NOMENCLATURE	DEPTH
MD	30 gal black - Lin	1"
MD	Signal ILLUM Flare M125 (1)	1"

Note: Guidelines speed 10 x 10 ft

ACTION

Mag Sweep Complete

Excavation Complete

Quality Control Complete

Client Quality Assurance Complete

DATE

3-2-09

3-2-09

4/29/09

SIGNATURE

[Signature]

[Signature]

[Signature]

REMARKS

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No. C3G5E9 Size: 100 x 100 ft

Date Started: 3/2/09
 Date Completed: 3/2/09

Work Order No. _____
 UXO Supervisor: Kristensen
 UXO Technician(s): Caldwell, Hendricks
Paz




North
 Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
50	50			2#	10#

WT
 0.75
 .5

MEC	NOMENCLATURE	DEPTH
MD	(2) EXTENDED MISS SIGNAL ITEM	3"

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	3/2/09		
Excavation Complete	3/2/09		
Quality Control Complete	4/14/09		
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C365C9 Size: 100 x 100 ft

Date Started: 3/2/09

Date Completed: 3/2/09

North Direction

Work Order No:

UXO Supervisor: Kristensen

UXO Technician(s): Caldwell Hendricks

PAZ




Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
30	30			4#	5#

--	--	--	--	--	--	--	--	--	--	--	--

Note: Gridlines spaced 10 x 10 ft

MEC	NOMENCLATURE	DEPTH
MD	(4) Expanded M125 Signch illum	

WT
L#

ACTION	DATE	SIGNATURE
Mag Sweep Complete	3/2/09	
Excavation Complete	3/2/09	
Quality Control Complete	4/14/09	
Client Quality Assurance Complete		

REMARKS:

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No. C365FB Size: 100 x 100 ft
 Date Started: 3/2/09
 Date Completed: 3/2/09

Work Order No.:
 UXO Supervisor: Kristensen
 UXO Technician(s): Caldwell, Hendrick
Paz

North
 Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
50	50			2#	10#
MEC MD NOMENCLATURE (2) Expended 40mm Parachute Star M662 DEPTH					

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	3/2/09		
Excavation Complete	3/2/09		
Quality Control Complete	4/14/09		
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3G5H7 Size: 100 x 100 ft
 Date Started: 3-2-09
 Date Completed: 3-2-09

Work Order No.:
 UXO Supervisor: T. Clark
 UXO Technician(s): B. Smith
B. Raasch

North Direction

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
310	285		0	0.25	60

MEC	NOMENCLATURE	DEPTH
MD	Signal Film Frame M26 (7)	1"

Note: Gridlines spaced 10 x 10 ft


ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	3-2-09	[Signature]	
Excavation Complete	3-2-09	[Signature]	
Quality Control Complete	3/4/09	[Signature]	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: 63#512 Size: 100 x 100 ft
 Date Started: 3-2-09
 Date Completed: 3-2-09

Work Order No.:
 UXO Supervisor: Labachere
 UXO Technician(s): Lesovic, Remington

North
 Direction

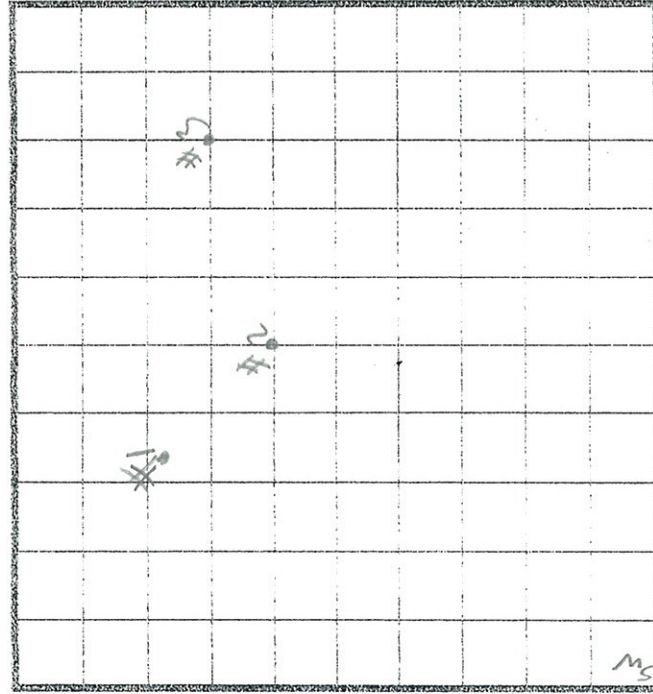

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
165	165		—	8	20

	NOMENCLATURE	DEPTH	WT
Scrap			
#1	Mine AT, Proc MI (1)	SuL	10
#2	Signal illum ground M125 series (1)	SuL	25
#3	Signal illum ground M25 series (1)	SuL	25

Note: Gridlines spaced 10 x10 ft

ACTION	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	3-2-09		
Excavation Complete	3-2-09		
Quality Control Complete	3-2-09		
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C34410 Size: 100 x 100 ft

Date Started: 3-2-09

Date Completed: 3-2-09

Work Order No:

UXO Supervisor: L. Archer

UXO Technician(s): La Dae Remington

North
Direction

1															
---	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
00	00	-	-	1/2	20

Sweep

MEC

#1

NOMENCLATURE

Sigapillium spore MEC5 series

DEPTH

2"

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	3-2-09	<i>[Signature]</i>	
Excavation Complete	3-2-09	<i>[Signature]</i>	
Quality Control Complete	3/9/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Entered
4/15/09

Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No C3H5 F1 Size 100 x 100 ft

Date Started 4/15/09

Date Completed 4/15/09

Work Order No. _____

UXO Supervisor Kristensen

UXO Technician(s) Hendricks

North
Direction

--	--	--	--	--	--	--	--	--	--

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
50	50		0	3#	5#

MEC	NOMENCLATURE	DEPTH
	(1) expended rocket 2.36" practice M7	3"
	(2) expended Signal Illum flashed round M125	3"

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4/15/09		
Excavation Complete	4/15/09		
Quality Control Complete	4-20-09		
Client Quality Assurance Complete			

4/17/09




Entered
4/15

Grid Sweep Log

Project Name: *Fort Camp Remediation Program*
 Site No: *C395B9* Size: *100 x 100 ft*
 Date Started: *4-15-09*
 Date Completed: *4-15-09*

Work Order No:
 Site Supervisor: *T. Clark*
 Field Technicians:
B. Raasch
J. Remington

Grids:
Direction:

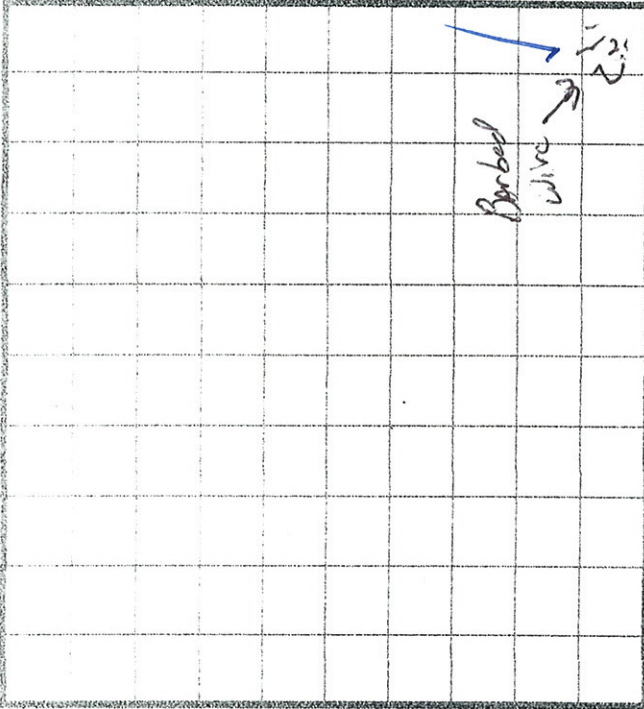

Note: Gridlines spaced 10 N10 ft

Total Anomalies	Total Excavations	Anomalies per ft	Total MFC Items	Pounds MFC Scrap	Pounds Non MFC Scrap
225	210		0	1.5	8.5

ITEM	NOMENCLATURE	DEPTH
MD	Signal I (low grid - M125 (2))	3"
MD	Future green head M10 (1)	3"

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-15-09	[Signature]	
Excavation Complete	4-15-09	[Signature]	
Quality Control Complete	4/24/09	[Signature]	
Client Quality Assurance Complete			

4/17 sy



Entered
4/15

Grid Sweep Log

Project Name: Grid Remediation Program

Site No: C39588 Size: 100' x 100'

Date Started: 4-15-09

Date Completed: 4-15-09


Work Order No.

Site Supervisor:

Site Technician:

T. Clark
B. Raasch
J. Remington

Depth:
Direction:

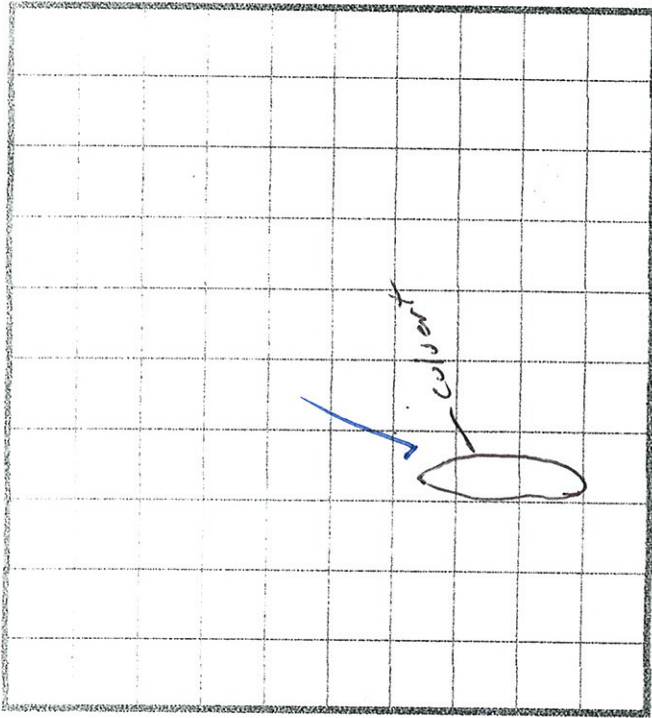

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies per ft	Total MFC Items	Pounds MFC Scrap	Pounds Non-MFC Scrap
160	150		0	2.0	100
NOMENCLATURE					
MFC					DEPTH
MD	- Sig Ellen grid		M125-	(1)	3"
MD	Small mass blanks		(75)		3"

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-15-09	<i>[Signature]</i>	
Excavation Complete	4-15-09	<i>[Signature]</i>	
Quality Control Complete	4/24/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C365AO Size 100 x 100 ft

Date Started 4-14-09

Date Completed 4-14-09


Work Order No. _____

UXO Supervisor CLARK

UXO Technician(s) B. Raasch

E. Gonzalez

North Direction

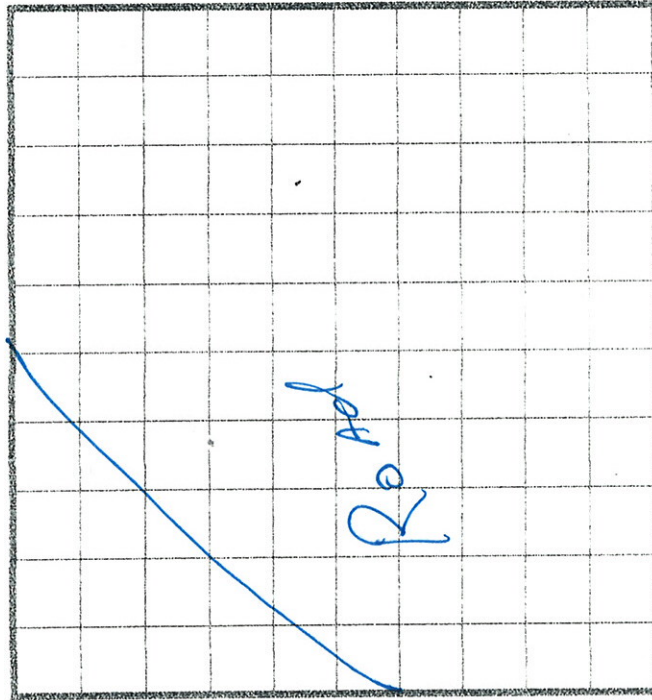

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
6	6		0	0	.5

MEC	NOMENCLATURE	DEPTH

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-14-09	<i>[Signature]</i>	
Excavation Complete	4-14-09	<i>[Signature]</i>	
Quality Control Complete	4/14/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

Ent. 4/17 sy.



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C365A9 Size 100 x 100 ft

Date Started 4-14-09

Date Completed 4-14-09


Work Order No. _____

UXO Supervisor Clark

UXO Technician(s) B. Raasch

E. Gonzalez

North Direction _____

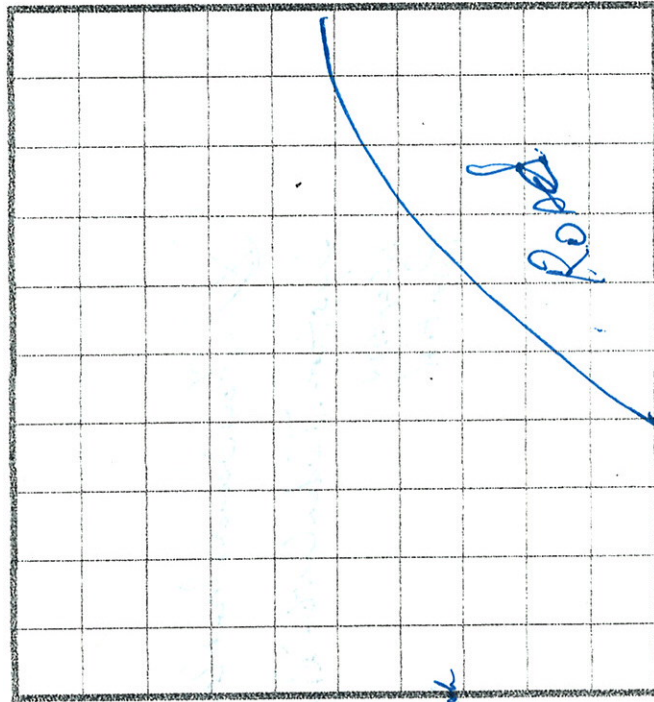

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
250	220		0	.1	20

MEC	NOMENCLATURE	DEPTH
MD	Face-Gravel Area MZOS	3"

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-14-09	[Signature]	
Excavation Complete	4-14-09	[Signature]	
Quality Control Complete	4/14/09	[Signature]	
Client Quality Assurance Complete			

Est. 4/17 sy.




Grid Sweep Log

Project Name/Ford Remediation Program
 Grid No. C3G5B0 Size 100 x 100 ft
 Date Started 4-14-09
 Date Completed 4-14-09

Work Order No.:
 UXO Supervisor Clark
 UXO Technician(s) B. Rorsch
E. Gumbel

North
Direction

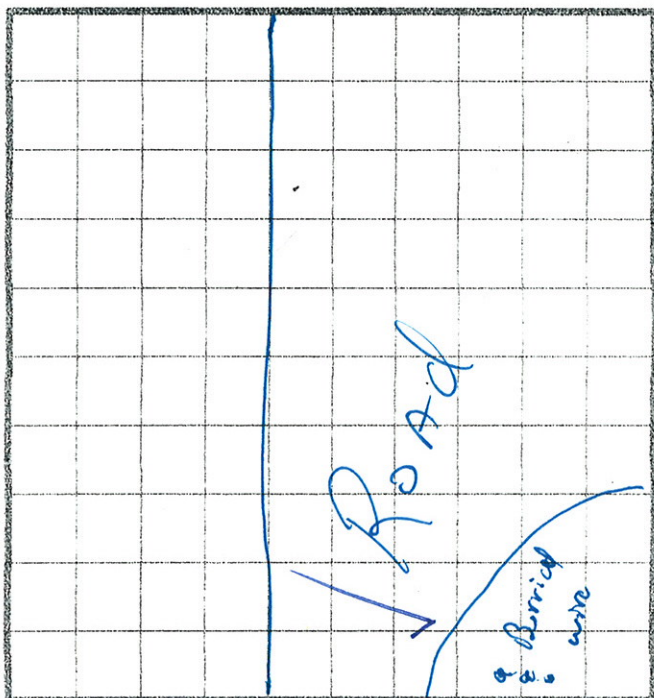

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
200	190		0	0	5

MEC	NOMENCLATURE	DEPTH

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-14-09	<i>[Signature]</i>	
Excavation Complete	4-14-09	<i>[Signature]</i>	
Quality Control Complete	4/24/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

Ext. 4/17 sy.



Grid Sweep Log

Project Name: Fast Grid Remediation Program

Grid No. **C3 F5J7** Size: 100 x 100 ft

Date Started: **4-14-09**

Date Completed: **4-14-09**

Work Order No.

Work Order Desc.


Work Order Date

Inspector: **E. Gantales**

Site Manager: **T. Clark**

Site Supervisor: **B. Rasch**

Grid Direction

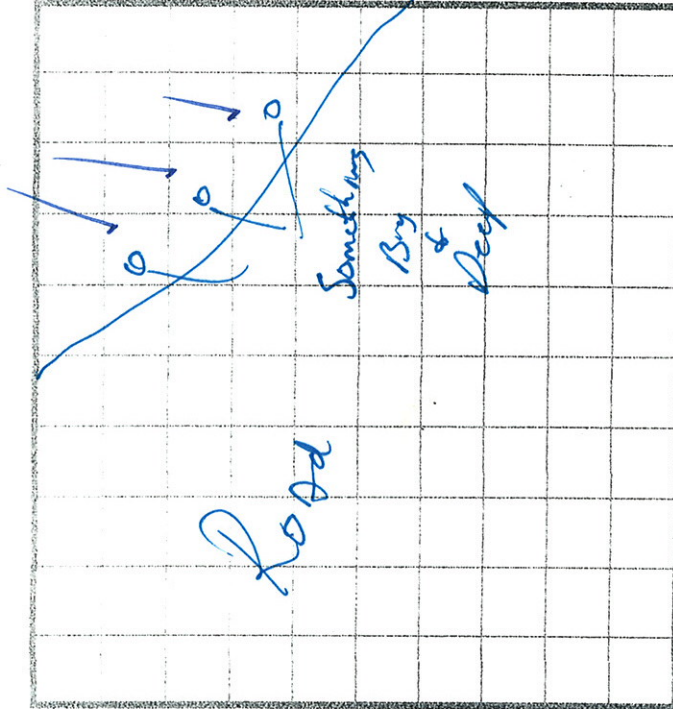

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies Found	Total MFR Items	Pounds MEC Scrap	Pounds Non MEC Scrap
6	6		0	0	1.0
MEC			NOMENCLATURE		DEPTH

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-14-09	[Signature]	
Excavation Complete	4-14-09	[Signature]	
Quality Control Complete	4-14-09	[Signature]	
Client Quality Assurance Complete			

cont. 4/17 sy.



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No **C3F5J8** Size 100 x 100 ft

Date Started **4-14-09**

Date Completed **4-14-09**


Work Order No:

UXO Supervisor **T. Clark**

UXO Technician(s) **B. Raasch**

E. Gouzales

North
Direction

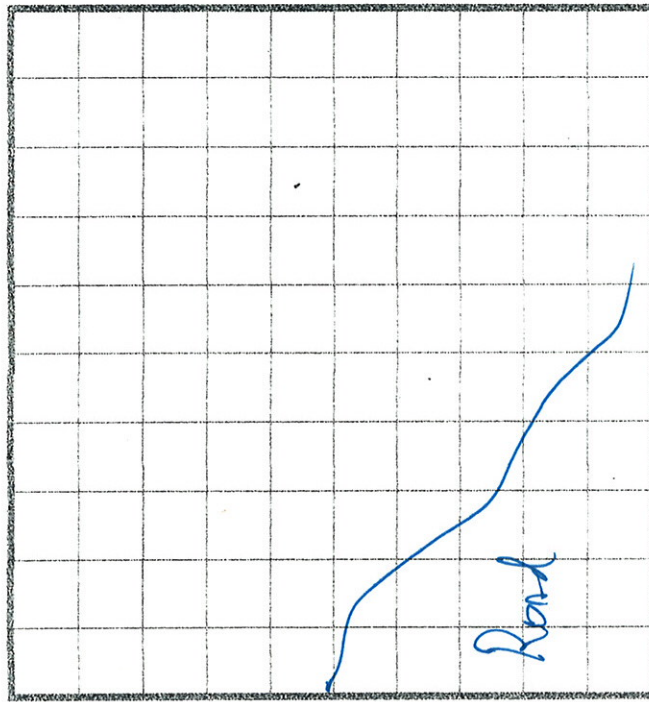

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
200	175		0	3	5

MEC	NOMENCLATURE	DEPTH
MD	Blanks - Small ones (25)	3"
MD	Small Ilium MDS (1)	3"

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-14-09	[Signature]	
Excavation Complete	4-14-09	[Signature]	
Quality Control Complete	4/14/09	[Signature]	
Client Quality Assurance Complete			

Est. 4/17 sy.



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: **C3H4CB** Size: 100 x 100 ft

Date Started: **4-14-09**


Date Completed: **4-14-09**

Work Order No.:

UXO Supervisor: **Lauchner**

UXO Technician(s): **LaPore Adams**

North Direction

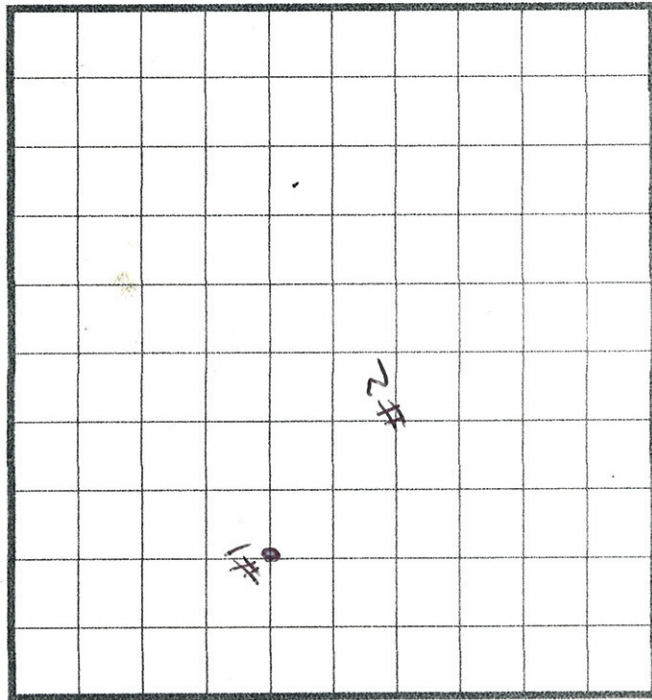

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
200	200	-	1	1	2.5

MEC	NOMENCLATURE	DEPTH
#1	DMM flare surface Trip M49 (1)	
#2	sig illum grad M125 (1)	

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-14-09	<i>[Signature]</i>	
Excavation Complete	4/14/09	<i>[Signature]</i>	
Quality Control Complete	4/21/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

OK - data ent. 4/15



Grid Sweep Log

Project Name/Est/Ord Remediation Program

Job No. **C3H5F2** Size **100' x 100' ±**

Date Started **4-8-09**

Date Completed **4-9-09**

Job Order No.

Job Supervisor

Project Location

T. Clark
B. Smith
L. Gonzalez, J. Reardon

Date
 Location

Note: Gridlines spaced 10' N10' E

Total Anomalies	Total Excavations	Approaches	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
450	400		0	2	25

MEC	NOMENCLATURE	DEPTH
MD	Small arm (100')	3"
DDM	Flare, Surface n.p. M49	3"

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-9-09	<i>[Signature]</i>	
Excavation Complete	4-9-09	<i>[Signature]</i>	
Quality Control Complete	4/20/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name: Grid Remediation Program

Site No: C375 J9 Size: 100 x 100 ft

Date Started: 4-9-09

Date Completed: 4-9-09

Work Order No:

Contract No:

Client Name:

Site Location:

T. Clark

B. Smith

E. Gonzalez

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies per ft	Total MFL Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
2	1		0	0	1

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-9-09	<i>TRE</i>	
Excavation Complete	4-9-09	<i>TRE</i>	
Quality Control Complete	4/14/09	<i>EK</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name: Grid Remediation Program

Site ID: C3G5A8 Size: 100 x 100 ft

Date: 4-9-09

Date: 4-9-09

Client: Weston

Project No: 09-00050


Site No: 09-00050

Site Name: F. Gonzales

T. Clark

B. Smith

Grid Location

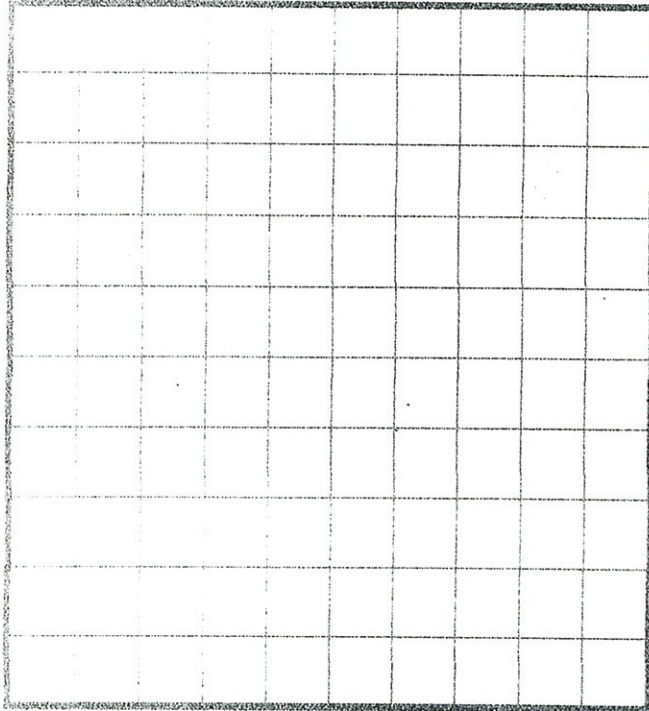

Total Anomalies	Total Excavations	Anomalies	Total MFC Items	Pounds MEC Scrap	Pounds Non MEC Scrap
120	100		0	4	5

MFC	NOMENCLATURE	DEPTH
MD	Small Arms Blank (55)	3"
MD	Grease, Hard Spots M18 (3)	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-9-09	[Signature]	
Excavation Complete	4-9-09	[Signature]	
Quality Control Complete	4/14/09	[Signature]	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name: Fort Ord Remediation Program

Grid No. C3H5 F3 Size 100 x 100 ft

Date Started: 4-8-09

Date Completed: 4-8-09

Work Order No. _____

UXO Supervisor T. Park

UXO Technician(s) B. Smith

E. Gortals

North Direction

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
450	430		0	1.5	150

MEG	NOMENCLATURE	DEPTH
MO	Small Arms (100)	3"

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-8-09		
Excavation Complete	4-8-09		
Quality Control Complete	4/20/09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3H5F4 Size: 100 x 100 ft
 Date Started: 4-7-09
 Date Completed: 4-8-09

Work Order No.: _____
 UXO Supervisor: T. Clark
 UXO Technician(s): B. Smith
E. Gonzalez

North
Direction

<input checked="" type="checkbox"/> Pit

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
400	380		0	2.0	8.5

MEC	NOMENCLATURE	DEPTH
MP	Small Arms - Blanks (88)	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-8-09		
Excavation Complete	4-8-09		
Quality Control Complete	4/20/09		
Client Quality Assurance Complete			

Grid Sweep Log

Project Name: C3 H5A5 Size: 100 x 100 ft
 Date Started: 4/8/09
 Date Completed: 4/8/09

Work Order No: _____
 UXO Supervisor: Kristensen
 UXO Technicians: Caldwell, Rasch

Berth
 Direction

(B) Metal Post											

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total Misc Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
0	0	>	0	1	5

MEC	NOMENCLATURE	DEPTH
0	(1) Expended M125 ground illumination flare	3"

Note: Gridlines spaced 10 x 10 ft

ACTION: Mag Sweep Complete
 Excavation Complete
 Quality Control Complete
 Client Quality Assurance Complete

DATE	SIGNATURE
4/8/09	
4/8/09	
4/28/09	

RE-MARKS



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3H4H Size: 100 x 100 ft

Date Started: 4-8-09

Date Completed: 4-8-09

Work Order No: _____
 UXO Supervisor: Lauchner
 UXO Technician(s): Adams, Remington

North
Direction

#1																				
----	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
150	150	-	-	1	15

MEC	NOMENCLATURE	DEPTH
#1	grenad smoke MIS	

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-8-09		lots of wood chip
Excavation Complete	4-8-09		Very high mounds.
Quality Control Complete	4/14/09		
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C3 H4A 5 Size: 100 x 100 ft
 Date Started: 4-8-09
 Date Completed: 4-8-09

Work Order No.:
 UXO Supervisor: Launched
 UXO Technician(s): Adams Reminton

North
 Direction

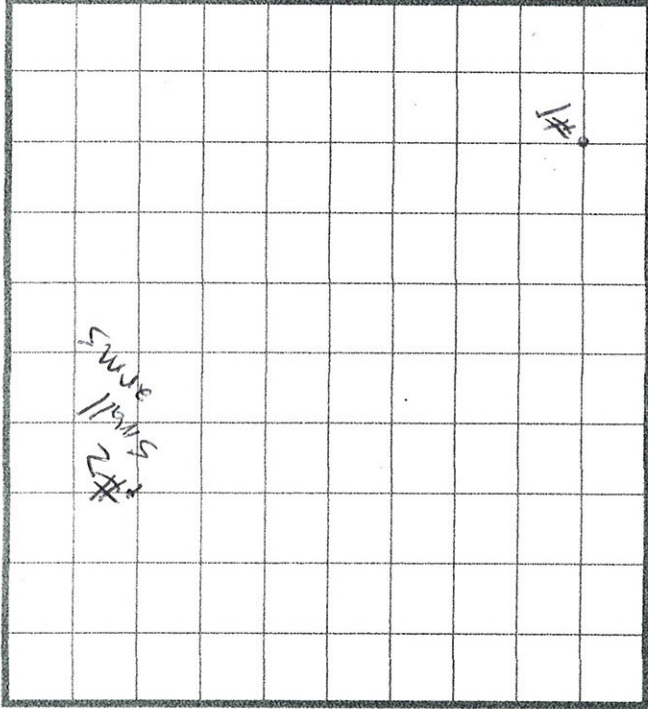

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
180	180	---	---	2	10

MEC	NOMENCLATURE	DEPTH
#1	grenade hand frag MXTI (1)	3
#2	Blank Ammunition (6 Field Dig)	3

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-8-09	<i>[Signature]</i>	
Excavation Complete	4-8-09	<i>[Signature]</i>	
Quality Control Complete	4/14/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

