



# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C3H5G5 Size: 100 x 100 ft  
 Date Started: 4-7-09  
 Date Completed: 4-7-09

Work Order No.: \_\_\_\_\_  
 UXO Supervisor: T. Turk  
 UXO Technician(s): B. Smith  
E. Gonzales

North  
 Direction

Gridlines spaced 10 x 10 ft Grounding Rod post ✓ X ✓									

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
350	320		0	4.1	5

MEC	NOMENCLATURE	DEPTH
MP	Small arms blanks (65)	3"
MP	5/16" ILLUM Grenad MBS (2)	3"
MD	1/2" Grenad (hand mag) (1)	3"
OMM	Squibs, electric or model # 426 (5)	.1

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-7-09	[Signature]	
Excavation Complete	4-7-09	[Signature]	
Quality Control Complete	4-7-09	[Signature]	
Client Quality Assurance Complete			






# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C3/H5 G2 Size: 100 x 100 ft  
 Date Started: 4-6-09  
 Date Completed: 4-7-09

Work Order No.:  
 UXO Supervisor: T. Clark  
 UXO Technician(s): B. Smith  
E. Gonzalez

North  
 Direction

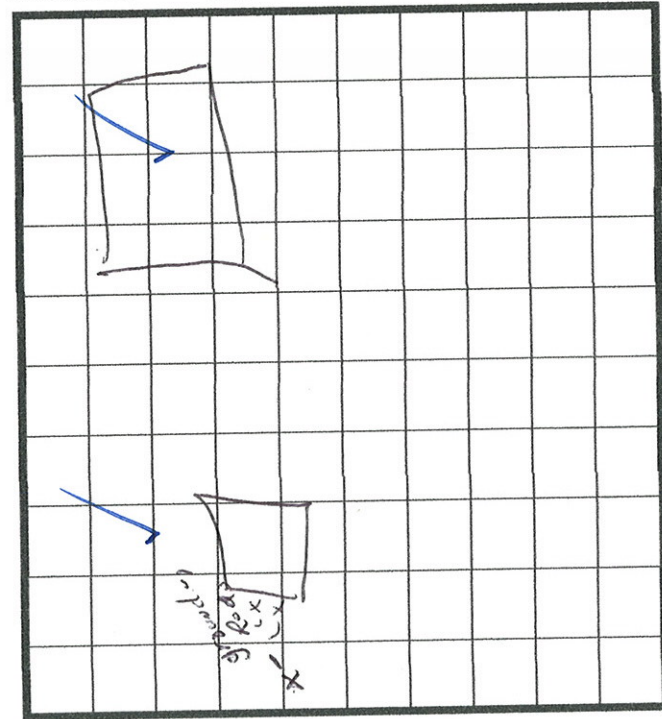

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
500	450		0	30	30

MEC	NOMENCLATURE	DEPTH
MO	Small brass Bunks (500)	3"
MO	rust, ground hard pine (4)	3"

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-7-09	[Signature]	
Excavation Complete	4-7-09	[Signature]	
Quality Control Complete	4-7-09	[Signature]	
Client Quality Assurance Complete			







# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No: C3H4C7 Size: 100 x 100 ft  
 Date Started: 4-7-09  
 Date Completed: 4-7-09

Work Order No.:  
 UXO Supervisor: Lavhner  
 UXO Technician(s): Adams, Beniston

North Direction

#1											

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
-	-	-	-	1 1/2	1
MEC	NOMENCLATURE			DEPTH	
#1	Sig illum ground MISS			SUR	

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-7-09	<i>[Signature]</i>	
Excavation Complete	4-7-09	<i>[Signature]</i>	
Quality Control Complete			
Client Quality Assurance Complete			





# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C3H5G3 Size: 100 x 100 ft  
 Date Started: 4-6-09  
 Date Completed: 4-6-09

Work Order No.: \_\_\_\_\_  
 UXO Supervisor: I. Clark  
 UXO Technician(s): B. Smith  
E. Gonzalez

North  
Direction

* - Grounding Rod									

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
350	330		0	3	16

MEC	NOMENCLATURE	DEPTH
MD	Small metal blanks (129)	3"
MD	Fluxy surface trip M49 (1)	3"
MD	ground, hand spike M18 (1)	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-6-09	<i>[Signature]</i>	
Excavation Complete	4-6-09	<i>[Signature]</i>	
Quality Control Complete	4-7-09	<i>[Signature]</i>	
Client Quality Assurance Complete			





**Grid Sweep Log**

Project Name/Fort Ord Remediation Program

Grid No.: C3H5H1 Size: 100 x 100 ft

Date Started: 4-6-09

Date Completed: 4-6-09

Work Order No.:

UXO Supervisor: [Signature]

UXO Technician(s): B. Smith

E. Gonzales

North Direction


✓  
Ground  
X Rad

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
400	350			30	40

MEG	NOMENCLATURE	DEPTH
MD	Gravel, base fine MK2 (1)	3"
MD	Signal, Ellin M2579A2 (1)	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-6-09	[Signature]	
Excavation Complete	4-6-09	[Signature]	
Quality Control Complete	4/8/09	[Signature]	
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C3H4H0      Size: 100 x 100 ft  
 Date Started: 4-6-09  
 Date Completed: 4-6-09

Work Order No.: \_\_\_\_\_  
 UXO Supervisor: T. Clark  
 UXO Technician(s): B. Smith  
E. Gonzalez

North \_\_\_\_\_  
 Direction \_\_\_\_\_


Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
420	380		0	4	20

	NOMENCLATURE	DEPTH
MEC		
MD	Gravelly Hard Sinks M18 (2)	3 1/2"
MD	Small pieces blanks (67)	3"

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-6-09	[Signature]	
Excavation Complete	4-6-09	[Signature]	
Quality Control Complete	4/8/09	[Signature]	
Client Quality Assurance Complete			

# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3H4B6 Size: 100 x 100 ft

Date Started: 4-6-09

Date Completed: 4-6-09

Work Order No.:

UXO Supervisor: Laucher

UXO Technician(s): Remington, Adams



North

Direction


Total Anomalies	Total Excavations	Anomalies > <u>    </u> ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
-	-	-	-	-	10

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-6-09		
Excavation Complete	4-6-09		
Quality Control Complete	4-7-09		
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3H4D5 Size: 100 x 100 ft

Date Started: 4-6-09


Date Completed: 4-6-09

Work Order No.:

UXO Supervisor: L. Kuchner

UXO Technician(s): Remington Adams

North Direction

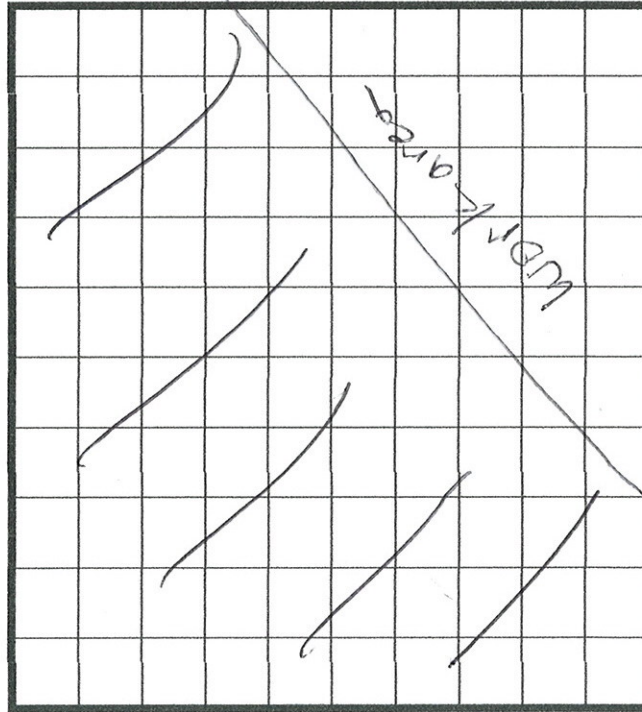

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
1	-	-	-	-	1/4

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-6-09	[Signature]	
Excavation Complete	4-6-09	[Signature]	
Quality Control Complete	4-7-09	[Signature]	
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Work Order No.:

Grid No.: C34465 Size: 100 x 100 ft


UXO Supervisor: L. Kuchner

Date Started: 4-6-09

UXO Technician(s): Remington Adams

Date Completed: 4-6-09

North  
Direction

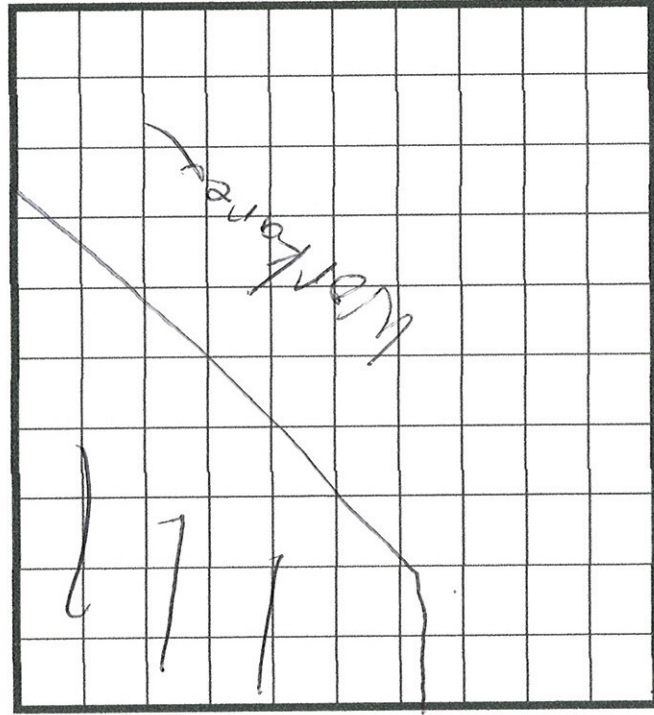

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
0	0	0	0	0	3

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-6-09	[Signature]	
Excavation Complete	4-6-09	[Signature]	
Quality Control Complete	4-7-09	[Signature]	
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C3H4C6 Size: 100 x 100 ft

Date Started: 4-6-09


Date Completed: 4-6-09

Work Order No.:

UXO Supervisor: Lauchner

UXO Technician(s): Adams, Remington

North  
Direction

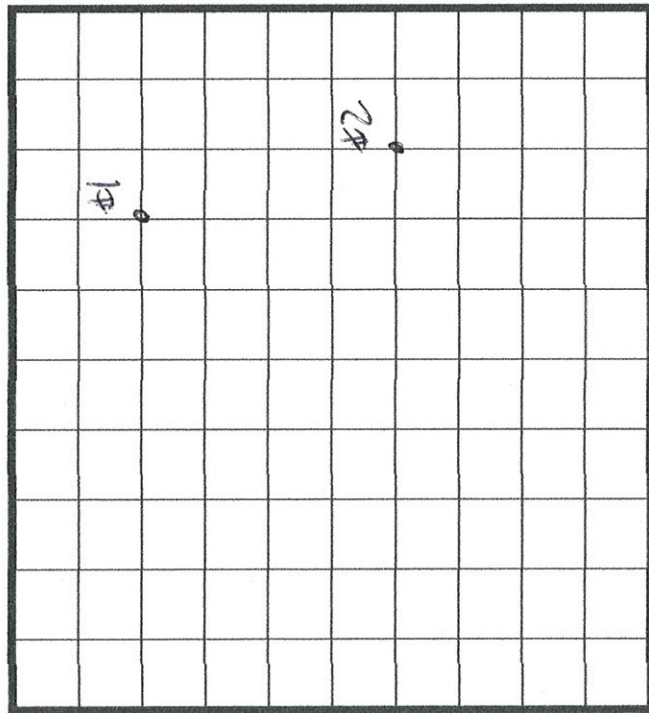

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
110	110			200	20

Scrap

	NOMENCLATURE	DEPTH
# 1	gravel hand proc MK11	
# 1	Signal illum ground M125-series	

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-6-09	[Signature]	
Excavation Complete	4-6-09	[Signature]	
Quality Control Complete	4-7-09	[Signature]	
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: S3H460 Size: 100 x 100 ft

Date Started: 4-3-09

Date Completed: 4-3-09

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): F. Gonziak  
M. Adams

North  
Direction


Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > <u>    </u> ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
380	360		0	.5	30

MEC	NOMENCLATURE	DEPTH
MO	Small items (15)	3"

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-3-09	<u>[Signature]</u>	
Excavation Complete	4-3-09	<u>[Signature]</u>	dry grass stowed sweep
Quality Control Complete	4/8/09	<u>[Signature]</u>	
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C3H5G1 Size: 100 x 100 ft  
 Date Started: 4-3-09  
 Date Completed: 4-3-09

Work Order No.: \_\_\_\_\_  
 UXO Supervisor: T. Clark  
 UXO Technician(s): E. Guzman  
M. Adams, B. Smith

North  
Direction


Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
450	422		0	2.5	20

MEC	NOMENCLATURE	DEPTH
MO	Small items - Blanks (30)	3"
MO	Greenady Hard Proc (M19 (1))	3"
MO	Sig Filler gnd M125 (2)	3"

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-3-09	<i>[Signature]</i>	long grass started sweep
Excavation Complete	4-3-09	<i>[Signature]</i>	
Quality Control Complete	4/8/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name: Grid Remediation Program

Grid No: C3H499 Size: 100 x 100 ft

Date Started: 4-2-09

Date Completed: 4-2-09

Work Order No:

UXO Supervisor: T. Clark

UXO Technician(s): M. Adams

M. Paszta/Invee

Bench Direction:

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non MEC Scrap
390	380		0	2	25

MEC	NOMENCLATURE	DEPTH
MO	(2) 5g 7.6mm graud M125	3"
MO	(1) fuse graud M10	3"
MO	(64) Black Ammo	3"

Note: Grid has exposed to M10 ft

ACTION

Mag Sweep Complete

Excavation Complete

Quality Control Complete

Client Quality Assurance Complete

DATE

4-2-09

4-2-09

4/8/09

SIGNATURE

*[Signature]*

*[Signature]*

*[Signature]*

REMARKS















# Grid Sweep Log

Project Name/Off Grid Remediation Program  
 Grid No. **C3H4A0** Size: 100 x 100 ft  
 Date Started **4-20-09**  
 Date Completed **4-20-09**

Work Order No.  
 UXO Supervisor **T. Clark**  
 UXO Technician(s) **J. Headricks**  
**B. Adams**

North Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MFC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
220	200		0	1.0	35.0
<p><b>MFC</b></p> <p><b>MO</b> Sig. ILLUM ground M125 (2)</p> <p>NOMENCLATURE</p> <p>DEPTH 3"</p>					

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-20-09	<i>[Signature]</i>	
Excavation Complete	4-20-09	<i>[Signature]</i>	
Quality Control Complete	4-23-09	<i>[Signature]</i>	
Client Quality Assurance Complete			












# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No. C3H4R5 Size 100 x 100 ft  
 Date Started 4/20/09  
 Date Completed 4/20/09

Work Order No.:  
 UXO Supervisor: Kristensen  
 UXO Technician(s): Smith  
GONZALEZ

North  
 Direction

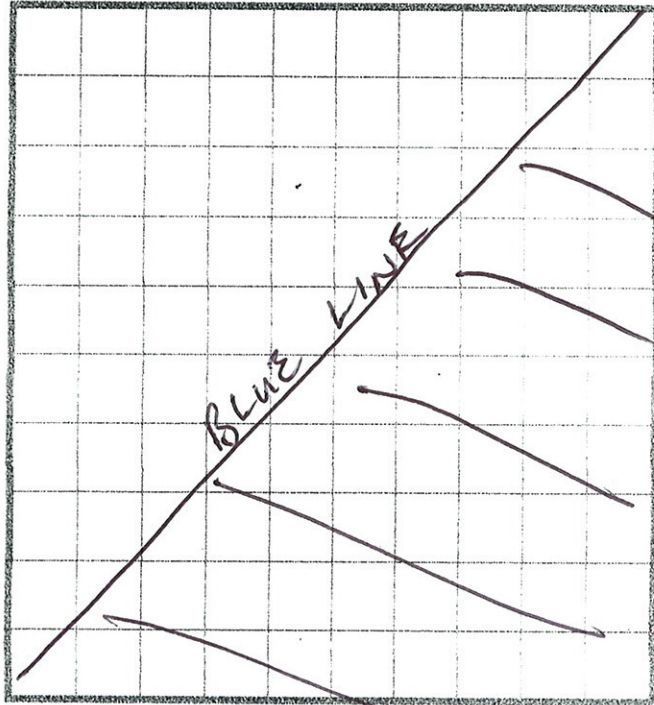

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
30	30				15#

MEC	NOMENCLATURE	DEPTH

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4/20/09	<i>[Signature]</i>	
Excavation Complete	4/20/09	<i>[Signature]</i>	
Quality Control Complete	4-21-09	<i>[Signature]</i>	
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No C3H4E6 Size 100 x 100 ft

Date Started 4/20/09

Date Completed 4/20/09

Work Order No.

UXO Supervisor Kristensen

UXO Technician(s) Smith

GONZALEZ

North Direction

Not area deeper than 3"

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
45	45				15#

MEC	NOMENCLATURE	DEPTH

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4/20/09		
Excavation Complete	4/20/09		
Quality Control Complete	4-21-09		
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3 H5C1 Size: 100 x 100 ft

Date Started: 4-20-09


Date Completed: \_\_\_\_\_

Work Order No.:

UXO Supervisor: L. Auchner

UXO Technician(s): \_\_\_\_\_

North  
Direction

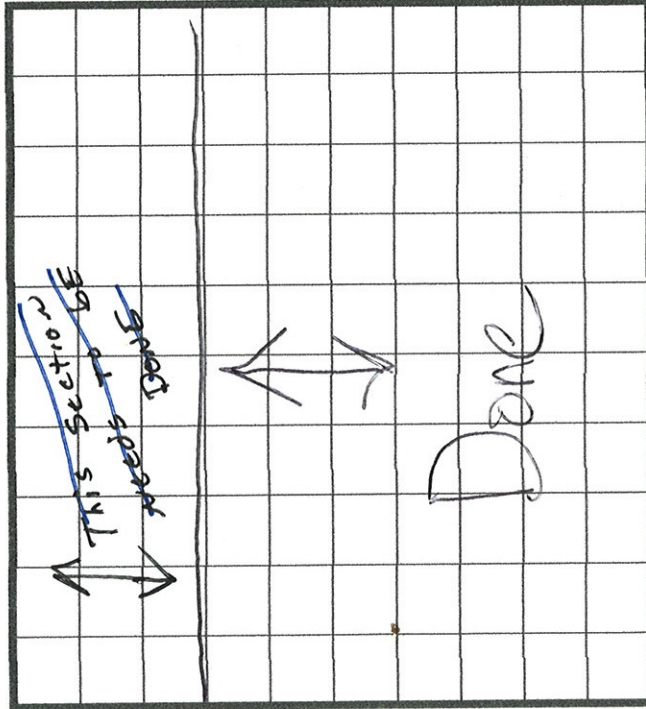

Note: Gridlines spaced 10 x 10 ft.

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
				<u>20#</u>	<u>125</u>

MEC	NOMENCLATURE	DEPTH
	<u>3 Ammo Cans Full .556 Blank</u>	<u>3"</u>
	<u>Expanded H+8 Fuzze Grenade Smoke</u>	<u>2"</u>

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	<u>4/21/09</u>	<u>[Signature]</u>	
Excavation Complete	<u>4/21/09</u>	<u>[Signature]</u>	
Quality Control Complete	<u>4-21-09</u>	<u>[Signature]</u>	
Client Quality Assurance Complete			



Printed ✓

# Grid Sweep Log



Project Name: Grid Remediation Program  
 Grid No: C3-H4-F5      Size: 100 x 100 ft  
 Date Started: 4/16/09  
 Date Completed: 4/16/09

Work Order No: \_\_\_\_\_  
 UXO Supervisor: Kristensen  
 UXO Technicians: Hendricks  
Remington

North  
 Direction


Total Anomalies	Total Excavations	Anomalies > 100 ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
70	10				14

MEC	NOMENCLATURE	DEPTH

WELDON

AC TID: \_\_\_\_\_  
 Map Sweep Complete: 4/16/09  
 Excavation Complete: 4/16/09  
 Quality Control Complete: 4/20/09  
 Client Quality Assurance Complete

DATE: \_\_\_\_\_  
 SIGNATURE:   
 SIGNATURE:

data re-entered 4/20/09







**Grid Sweep Log**

Project Name: Fort Ord Remediation Program

Grid No: C3H4E7 Size 100 x 100 ft

Date Started: 4/16/09

Date Completed: 4/16/09

North Direction

Work Order No

LXO Supervisor Kristensen

LXO Technician(s) Hendricks

Remington


Total Anomalies	Total Excavations	Anomalies > 1 ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>45</u>	<u>45</u>				<u>10#</u>

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft.

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	<u>4/16/09</u>		
Excavation Complete	<u>4/16/09</u>		
Quality Control Complete	<u>4-21-09</u>		
Client Quality Assurance Complete			

4/20/09



# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No **C3 H4 F7** Size 100 x 100 ft  
 Date Started **4-16-07**  
 Date Completed **4-16-07**

Work Order No \_\_\_\_\_  
 UXO Supervisor \_\_\_\_\_  
 UXO Technician(s) \_\_\_\_\_

North  
 Direction

<p>Smell pockets of          link &amp; brass  </p>									
---	--	--	--	--	--	--	--	--	--

Note Gridlines spaced 10' x 10'

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
60	60				10#

MEC	NOMENCLATURE	DEPTH

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-16-07		
Excavation Complete	4-16-07		
Quality Control Complete	4-20-07		
Client Quality Assurance Complete			

4/20/07



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: 13 H4 F8 Size: 100 x 100 ft

Date Started: 4/16/09

Date Completed: 4/16/09

Work Order No.:

UXO Supervisor: Kristensen

UXO Technician(s): Hendrix

Remington

North  
Direction


Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
60	60				44

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 MTO ft.

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4/16/09		
Excavation Complete	4/16/09		
Quality Control Complete	4-20-09		
Client Quality Assurance Complete			

4/20/09



Project Name: Fort Ord Remediation Program

Site No: **C395B7** Size: 135 x 100 ft

Date Started: **4-16-09**

Date Completed: **4-16-09**

North Direction

Entered 4/16


Grid Sweep Log

Work Order No:

MEC Supervisor:

MEC Inspector:

*T. Clark*  
*B. Smith*

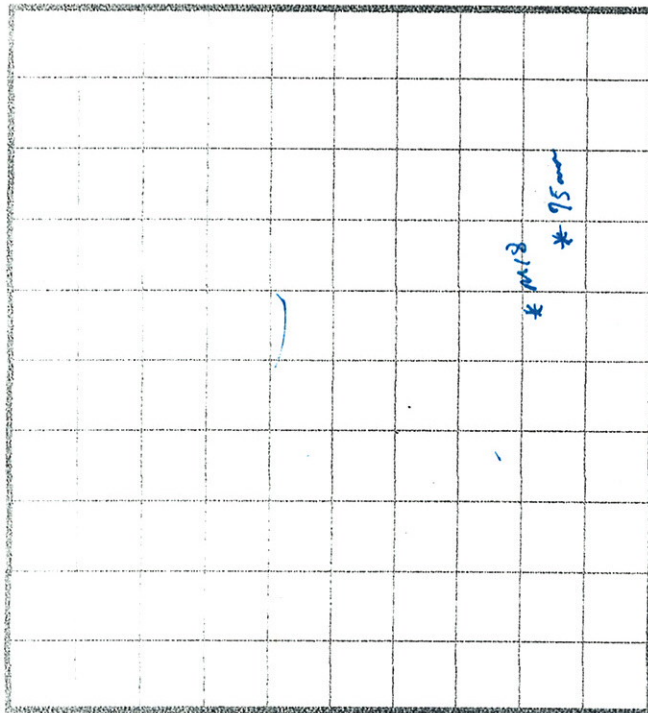

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies by Category	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
150	140		1	7	8.5
MEC		NOMENCLATURE			DEPTH
DMM	Green, hard,	Smoke M18 (1)			3"
MD	Small Arms	Blank Ammo (84)			3"
MD	Sig I Item	grid M125 (3)			3"
MD	Pepi, 75mm,	Shrapnel, MK1 (1)			3"
MD	fuzze,	green, hnd M10 (2)			3"

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-16-09	[Signature]	
Excavation Complete	4-16-09	[Signature]	
Quality Control Complete	4-24-09	[Signature]	
Client Quality Assurance Complete			

*de ALP GMS*




# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No: **C3H4B4** Size: 100 x 100 ft  
 Date Started: **4-16-09**  
 Date Completed: **4-16-09**

Work Order No.:  
 UXO Supervisor: **Lawcher**  
 UXO Technician(s): **LAROC Adams**

North  
 Direction

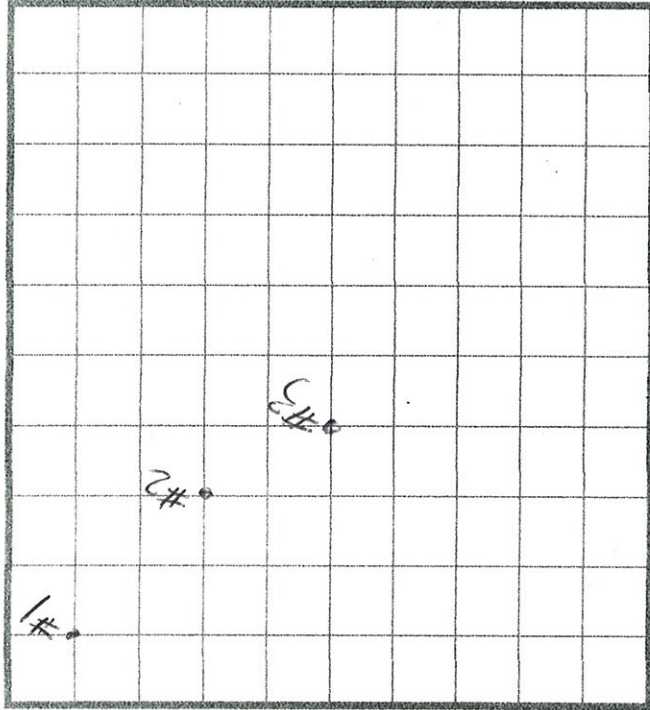

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
100	100	-	-	2	4

MEC	NOMENCLATURE	DEPTH
#1	grenade hand scribe M18 Series (1)	
#2	Signal illum ground parachute rifle M19 Series (1)	
#3	Signal illum ground M125 Series	

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-16-09	[Signature]	
Excavation Complete	4/16/09	[Signature]	
Quality Control Complete	5/12/09	[Signature]	
Client Quality Assurance Complete			

4/20/09



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C3H4C9 Size: 100 x 100 ft

Date Started 4-16-09


Date Completed 4-16-09

Work Order No. \_\_\_\_\_

UXO Supervisor: L. A. Luchner

UXO Technician(s): Ken Ray Adams

North Direction

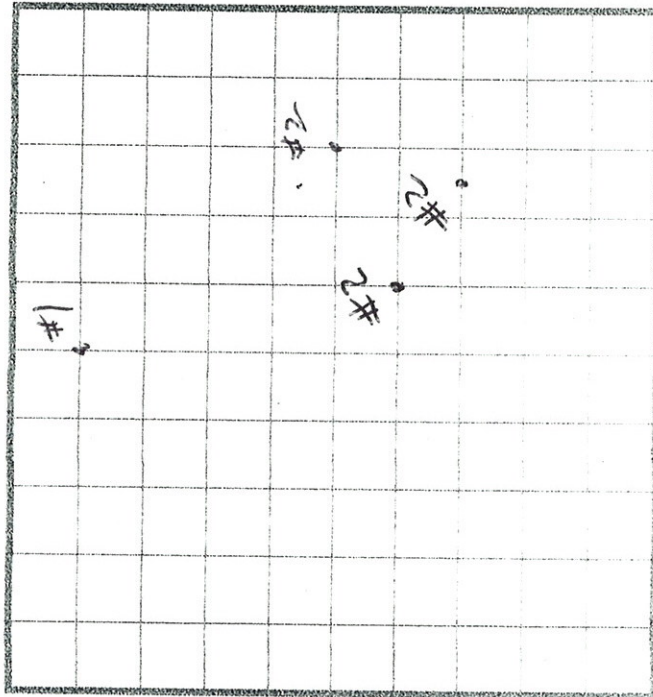

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
120	120	-	-	2.5	5165

MEC	NOMENCLATURE	DEPTH
#1	Flare surface Trip M49	(1)
#2	Sig illum ground M125	(3)

Scale: Gridlines spaced 10x10ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-16-09		
Excavations Complete	4-16-09		
Quality Control Complete	4-21-09		
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C34424 Size 100 x 100 ft

Date Started 4-16-09

Date Completed 4-16-09


Work Order No: \_\_\_\_\_  
UXO Supervisor: L. Huchner  
UXO Technician(s): L. R. Adams

North  
Direction


Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>109</u>	<u>109</u>	<u>-</u>	<u>-</u>	<u>-</u>	<u>10</u>

MEC	NOMENCLATURE	DEPTH

Notes: Gridlines spaced 100 ft apart

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	<u>4-16-09</u>		
Excavation Complete	<u>4-16-09</u>		
Quality Control Complete	<u>5/12/09</u>		
Client Quality Assurance Complete			





Project Name/Fort Ord Remediation Program

Grid No. C3H4A7 Size 100 x 100 ft

Date Started 4-16-09

Date Completed 4-16-09

North Direction

Work Order No. \_\_\_\_\_

UXO Supervisor: LAUCHNER

UXO Technician(s): LA ROE ADAMS

# Grid Sweep Log


Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
130	130	~	-	-	5

MEC	NOMENCLATURE	DEPTH

Notes: Gridlines per 100 ft

AG FIOH:

Grid Sweep Complete

Excavation Complete

Quality Control Complete

Final Quality Assurance Complete

SIGNATURE

*Matt Lauchner*  
*[Signature]*

DATE

4-16-09  
4-16-09  
4-23-09

REMARKS

ok ✓



# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C344B Size: 100 x 100 ft  
 Date Started: 4-24-09  
 Date Completed: 4-25-09

Work Order No.:  
 UXO Supervisor: L. Fischer  
 UXO Technician(s): Lois Adams

North  
 Direction


Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
200	200	-	-	15	-

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-24-09		
Excavation Complete	4-24-09		
Quality Control Complete	4-29-09		
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No C3H4D0 Size: 100 x 100 ft

Date Started 4/24/09


Date Completed 4/24/09

Work Order No:

UXO Supervisor: J. Kristensen

UXO Technician(s): Smith Remington

North Direction:

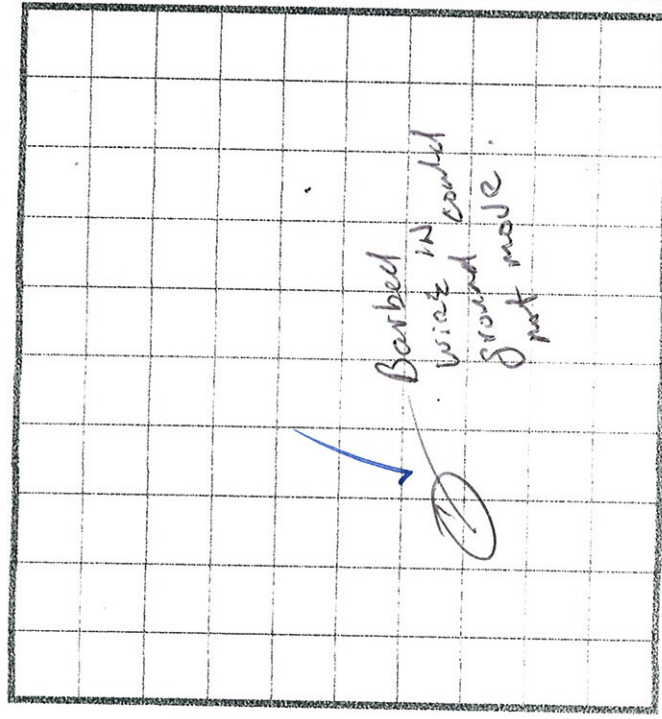

Note: Gridlines spaced 10 x 10 ft.

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
30	50				7#

MEC	NOMENCLATURE	DEPTH

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4/24/09		
Excavation Complete	4/24/09		
Quality Control Complete	4/28/09		
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: **G3G5A6** Size: 100 x 100 ft

Date Started: **4-24-09**

Date Completed: **4-24-09**

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): J. Hewdicks

E. Gonzalez

North  
Direction

--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

Total Anomalies	Total Excavations	Anomalies > ____ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
100	80		0	2.0	5.0

MEC	NOMENCLATURE	DEPTH
Small Arms	Blanks (50)	3"
MD	Gravel, Sand, Smoke MIB (1)	3"
MD	Sig. ground E/line M125 (1)	3"

Note: Gridlines spaced 10 M10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-24-09	<u>[Signature]</u>	
Excavation Complete	4-24-09	<u>[Signature]</u>	
Quality Control Complete	4/28/09	<u>[Signature]</u>	
Client Quality Assurance Complete			





# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C3F5J6 Size: 100 x 100 ft  
 Date Started: 4-24-09  
 Date Completed: 4-24-09

Work Order No.:  
 UXO Supervisor: T. Clark  
 UXO Technician(s): S. Hendricks  
E. Gonzales

North Direction


Total Anomalies	Total Excavations	Anomalies > ____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
220	210		0	1.5	30

MEC	NOMENCLATURE	DEPTH
Smallarms	Blinks - (80)	3''

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-24-09	<i>[Signature]</i>	
Excavation Complete	4-24-09	<i>[Signature]</i>	
Quality Control Complete	4-24-09	<i>[Signature]</i>	
Client Quality Assurance Complete			

# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C365B6 Size: 100 x 100 ft

Date Started: 4-24-09

Date Completed: 4-24-09

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): S. Hendricks

L. Gonzalez

North  
Direction


Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
140	120		0	1.5	3.5

	MEG	NOMENCLATURE	DEPTH
	MD	Sign. Thin sand Mass (2)	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-24-09	<i>[Signature]</i>	
Excavation Complete	4-24-09	<i>[Signature]</i>	
Quality Control Complete	4-28-09	<i>[Signature]</i>	
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3H4B9 Size: 100 x 100 ft

Date Started: 4-24-09

Date Completed: 4-24-09

Work Order No.:

UXO Supervisor: LAUCHNER

UXO Technician(s): Larve Adams

North Direction

3 Booth at N. end							#1A		
			#4						

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
150	150	-	1	5.5lbs	5

MEC	NOMENCLATURE	DEPTH
#1 A,B,C	Signal ground <del>illum</del> 0125 (8)	
#2	Small arms 30 cal (2lbs)	
#3	hand grenade practice mk1 (1)	
#4	hand grenade practice MK69 (1)	

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-24-09		
Excavation Complete	4-24-09		
Quality Control Complete	4-29-09		
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 SMO No **C3H5D1** Size 100 x 100 ft  
 Date Started **4/24/09**  
 Date Completed **4/24/09**

Work Order No \_\_\_\_\_  
 UXO Supervisor **Kristen Seem**  
 UXO Technician(s) **Smith Remington**

North Direction


Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
90	60			2#	5#

MEC	NOMENCLATURE	DEPTH
	(2) MH# expended MRS signed 1 Mar 2008	3"

ACT On: **4/24/09**  
 Dig Sweep Complete  
 Operator Complete  
 Quality Control Complete  
 Client Quality Assurance Complete

DATE: **4/24/09**  
 SIGNATURE: *[Signature]*  
 REMARKS:



# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: CSH4A8 Size: 100 x 100 ft  
 Date Started: 4/23/09  
 Date Completed: 4/23/09

Work Order No.: \_\_\_\_\_  
 UXO Supervisor: LAROE  
 UXO Technician(s): Adams, Par

North  
Direction


Total Anomalies	Total Excavations	Anomalies > <u>     </u> ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
52	52	NA	NA	#	3#

MEC	NOMENCLATURE	DEPTH
1	MCS Extended Signal ground 11/1/17	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4/23/09	[Signature]	
Excavation Complete	4/23/09	[Signature]	
Quality Control Complete	4/23/09	[Signature]	
Client Quality Assurance Complete			

4/23/09



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3H4D6 Size: 100 x 100 ft

Date Started: 4/23/09

Date Completed: 4/23/09

Work Order No.:

UXO Supervisor: Kristensen

UXO Technician(s): Smith

Remington

North  
Direction


Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
45	45			1#	5#

MEC	NOMENCLATURE	DEPTH
	Expanded <del>MEC</del> Grenade Fuze	3"
	M10	

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4/23/09		
Excavation Complete	4/23/09		
Quality Control Complete	4/23/09		
Client Quality Assurance Complete			

A/29 WJ





# Grid Sweep Log


Project Name/Fort Ord Remediation Program

Grid No. C344DB Size: 100 x 100 ft  
Date Started 4/23/09  
Date Completed 4/23/09

Work Order No.

UXO Supervisor: Kristensen  
UXO Technician(s): Smith  
Remington

North Direction

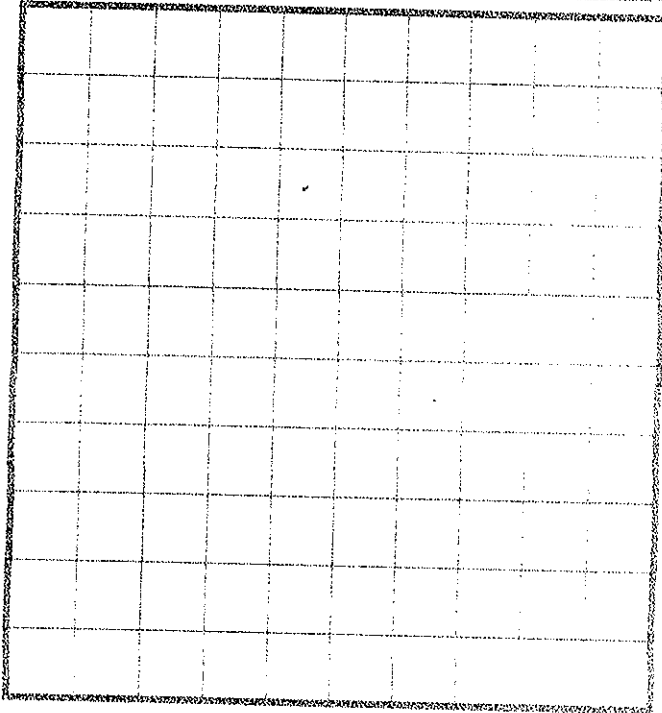

Total Anomalies	Total Excavations	Anomalies > ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
90	90			4#	10#

MEC	NOMENCLATURE	DEPTH
MD	25ea fire grenade (M205)	3"
	1ea expended MK II grenade hand proc	3"
	2ea expended M175 Signal ground illum	3"

Grid Sweep Log

DATE	SIGNATURE	REMARKS
4/23/09	[Signature]	
4/23/09	[Signature]	
4/28/09	[Signature]	

- Map Sweep Complete
- Excavation Complete
- Quality Control Complete
- Client Quality Assurance Complete





# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3H4A9 Size: 100 x 100 ft

Date Started: 4/23/09

Date Completed: 4/23/09

Work Order No.:

UXO Supervisor: LAROE

UXO Technician(s): Adams, PAZ

North  
Direction


Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<del>100</del> 100	<del>75</del> 75			2 #	<del>30 #</del> 30 #

MEC	NOMENCLATURE	DEPTH
2	M125 Expanded Sigad Ground Illum	3"
1	Hand Grenade size EXPANDED (M165)	2"

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4/23/09		
Excavation Complete	4/23/09		
Quality Control Complete	4/23/09		
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C344B8 Size: 100 x 100 ft  
 Date Started: 4/23/09  
 Date Completed: 4/23/09

Work Order No.:  
 UXO Supervisor: LAROE  
 UXO Technician(s): Adams, PAZ

North  
 Direction


line  
 presence  
 2-5  
 ⓧ

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non- MEC Scrap
35	35			2.5 #	5 #

MEC	NOMENCLATURE	DEPTH
M0	gren, hand, proc, MCI (live fire)	3"
1	M125 Extended Signal Ground Illum	3"
1	smoke, rifle grenade tail boom	3"

\* Bruce, I couldn't find smoke rifle grenade in PDA so it is not entered in PDA

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4/23/09	[Signature]	
Excavation Complete	4/23/09	[Signature]	
Quality Control Complete	4/29/09	[Signature]	
Client Quality Assurance Complete			





# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3F5F5 Size: 100 x 100 ft

Date Started: 4-23-09

Date Completed: 4-23-09


Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): S. Hendricks

E. Goates

North  
Direction

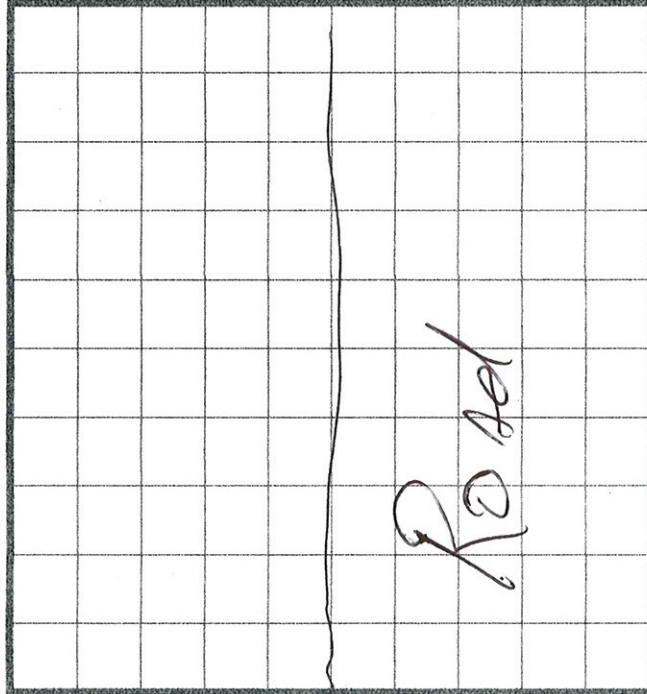

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
50	40		0	0	1.5

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-23-09	<u>[Signature]</u>	
Excavation Complete	4-23-09	<u>[Signature]</u>	
Quality Control Complete	4-24-09	<u>[Signature]</u>	
Client Quality Assurance Complete			



**Grid Sweep Log**

Project Name/Fort Ord Remediation Program

Grid No: C3F5G5 Size: 100 x 100 ft

Date Started: 4-23-09

Date Completed: 4-23-09

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): S. Henderson

F. Gonzales




North  
Direction

--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
180	170		0	0	70

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-23-09		
Excavation Complete	4-23-09		
Quality Control Complete	4/24/09		
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3F5G6 Size: 100 x 100 ft

Date Started: 4-23-09

Date Completed: 4-23-09


Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): S. Henderson

F. Gonzalez

North  
Direction

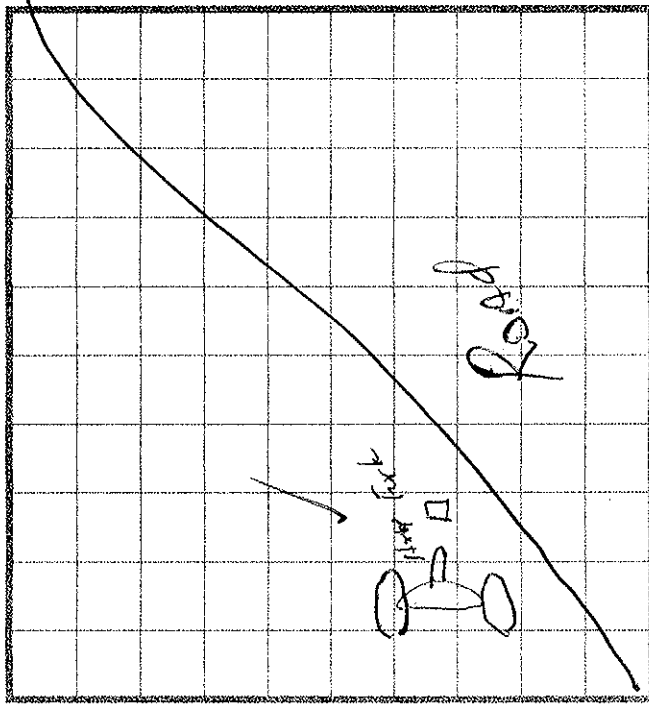

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
100	95		0	0	8.5

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-23-09	<u>T. Clark</u>	
Excavation Complete	4-23-09	<u>T. Clark</u>	
Quality Control Complete	4/24/09	<u>F. Gonzalez</u>	
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C3F5H6 Size: 100 x 100 ft  
 Date Started: 4-23-09  
 Date Completed: 4-23-09

Work Order No.:  
 UXO Supervisor: T. Clark  
 UXO Technician(s): J. Handricks  
E. Gonzalez

North  
 Direction


Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
220	200		0	3.0	10.0

MES	NOMENCLATURE	DEPTH
Smellwars	Blunks - 7.62 (100)	3"
MO	Big Illum gated - M125 (1)	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-23-09	<i>[Signature]</i>	
Excavation Complete	4-23-09	<i>[Signature]</i>	
Quality Control Complete	4/24/09	<i>[Signature]</i>	
Client Quality Assurance Complete			




# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C3F5H7 Size: 100 x 100 ft  
 Date Started: 4-23-09  
 Date Completed: 4-23-09

Work Order No.: \_\_\_\_\_  
 UXO Supervisor: T. Clark  
 UXO Technician(s): S. Hendricks  
E. Gonzalez

North  
 Direction

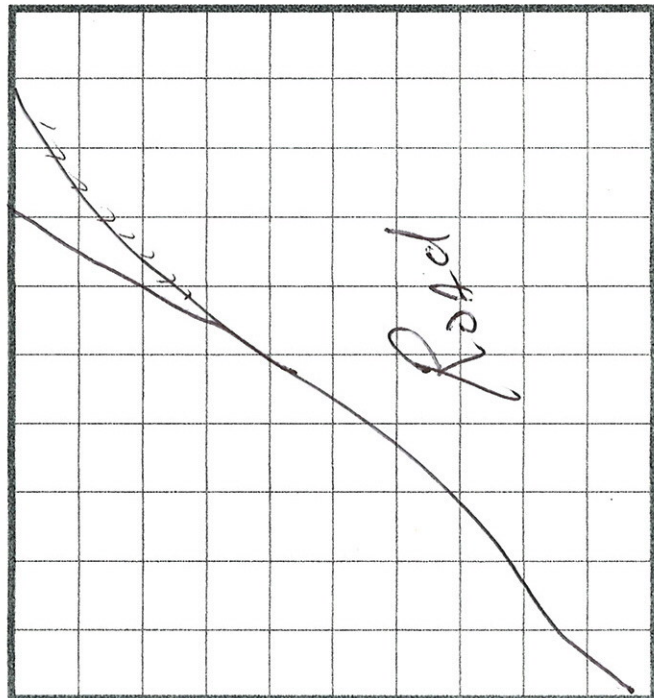

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
60	50		0	0	5

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-23-09	[Signature]	
Excavation Complete	4-23-09	[Signature]	
Quality Control Complete	4/24/09	[Signature]	
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ops Remediation Program

Grid No.: C3H5I8 Size: 100 x 100 ft

Date Started: 4-23-09

Date Completed: 4-23-09


Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): S. Hendricks

E. Gonzalez

North  
Direction

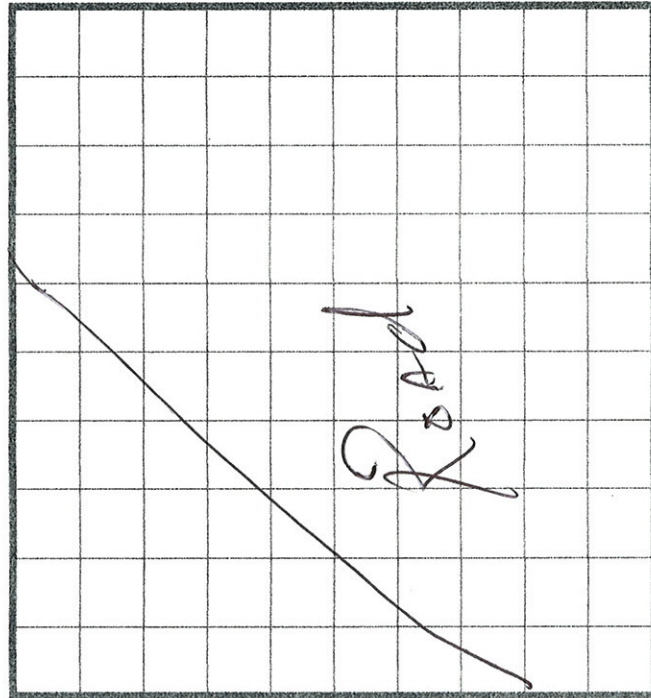

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
20	17		0	0	1.5

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-23-09	<i>[Signature]</i>	
Excavation Complete	4-23-09	<i>[Signature]</i>	
Quality Control Complete	4/24/09	<i>[Signature]</i>	
Client Quality Assurance Complete			




# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C3F5I7 Size: 100 x 100 ft  
 Date Started: 4-23-09  
 Date Completed: 4-23-09

Work Order No.: \_\_\_\_\_  
 UXO Supervisor: T. Clark  
 UXO Technician(s): S. Hendricks  
E. Gonzales

North  
 Direction

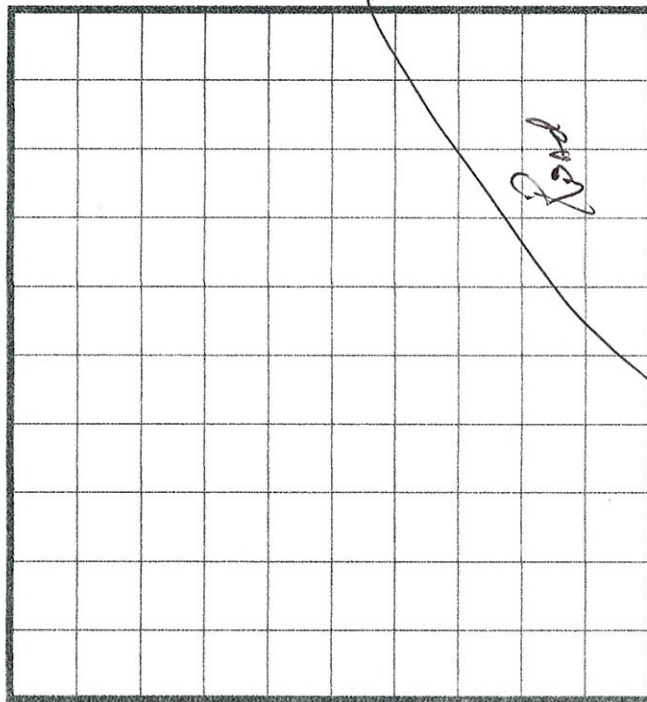

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
160	155		0	1.0	5.5

MEC	NOMENCLATURE	DEPTH
Small Arms	Bullets - 2.62 in (30)	3"

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-23-09	[Signature]	
Excavation Complete	4-23-09	[Signature]	
Quality Control Complete	4/24/09	[Signature]	
Client Quality Assurance Complete			




# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No. C3H5E2 Size 100 x 100 ft  
 Date Started 4/20/09  
 Date Completed 4/21/09

Work Order No.  
 UXO Supervisor Kristensen  
 UXO Technician(s) Smith, Laroe  
GONZALEZ

North  
 Direction

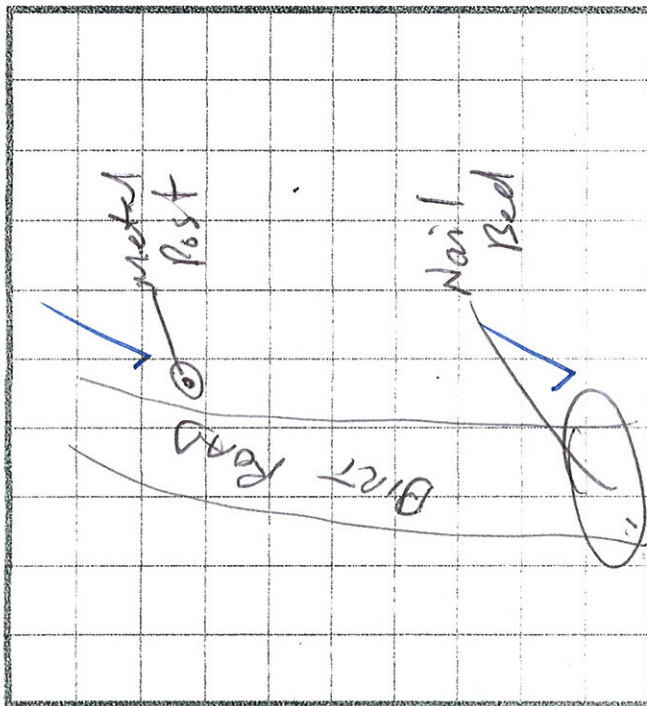

Note: Gridlines spaced 10'x10'

Total Anomalies	Total Excavations	Anomalies > <u>      </u> ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>80</u>	<u>80</u>				<u>5#</u>

MEC	NOMENCLATURE	DEPTH

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	<u>4/21/09</u>	<i>[Signature]</i>	
Excavation Complete	<u>4/21/09</u>	<i>[Signature]</i>	
Quality Control Complete	<u>4/21/09</u>	<i>[Signature]</i>	
Client Quality Assurance Complete			





# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No C3H5E3 Size 100 x 100 ft  
 Date Started 4/21/09  
 Date Completed 4/21/09

Work Order No. \_\_\_\_\_  
 UXO Supervisor Kristensen  
 UXO Technician(s) Smith, Laroe  
Gonzalez

North Direction \_\_\_\_\_


Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
100	80			2#	3#

MEC	NOMENCLATURE	DEPTH
1 ea	Expanded M118 Grenade Smoke	3'
2 ea	Expanded M125 Signal Illum	3'

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4/21/09		
Excavation Complete	4/21/09		
Quality Control Complete	4/22/09		
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C3 H5 E1 Size 100 x 100 ft

Date Started 4/21/09


Date Completed 4/21/09

North Direction

Work Order No. \_\_\_\_\_

UXO Supervisor: Kristensen

UXO Technician(s) Smith, LAROE  
GONZALEZ

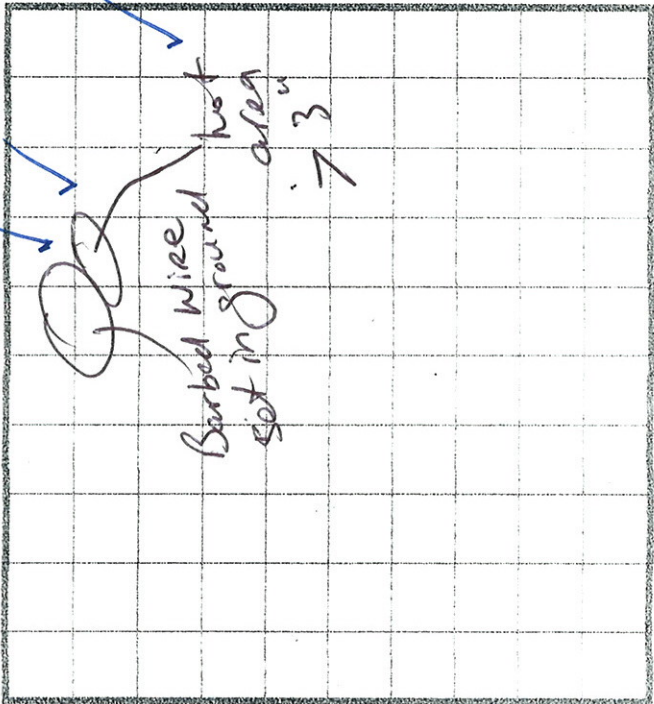

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
80	80			7#	7#

MEC	NOMENCLATURE	DEPTH
3EA	Expanded MKII Grenade Band	3"
1EA	Expanded <del>MEC</del> Fuze, Grenade, <del>Sensate</del>	3"
	MID	

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4/21/09		
Excavation Complete	4/21/09		
Quality Control Complete	4-21-09		
Client Quality Assurance Complete			

4/21/09




# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C345 E4 Size: 100 x 100 ft  
 Date Started: 4/21/09  
 Date Completed: 4/21/09

Work Order No.:  
 UXO Supervisor: Kristensen  
 UXO Technician(s): Smith, Lane  
 Gonzalez

North  
Direction

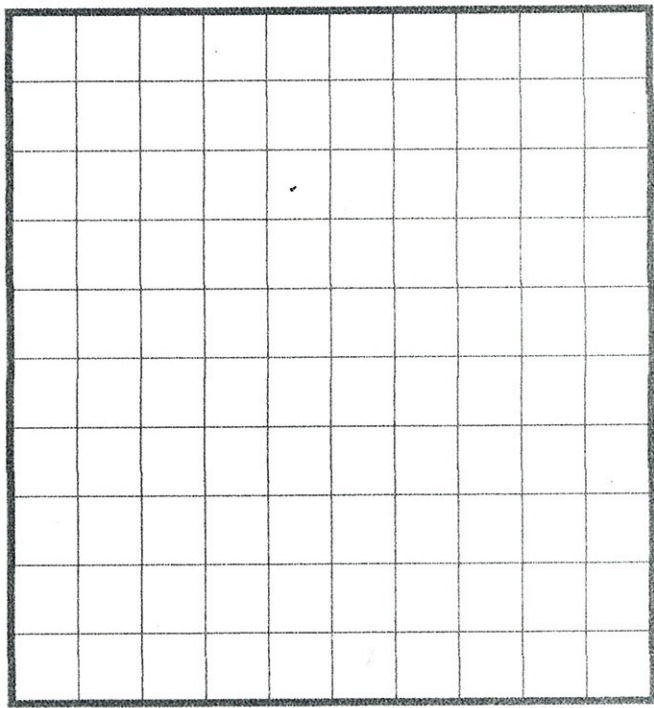

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
0	0			7#	2#

MEC	NOMENCLATURE	DEPTH
	(2) Expanded MILS signal, illum	3'
	5' + 5.86 m Blank small arms	3'

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4/21/09		
Excavation Complete	4/21/09		
Quality Control Complete	4/23/09		
Client Quality Assurance Complete			




# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: 345ES Size: 100 x 100 ft  
 Date Started: 4/27/09  
 Date Completed: 4/28/09

Work Order No.:  
 UXO Supervisor: Kristensen  
 UXO Technician(s): Rausch, Gonzalez

North  
 Direction

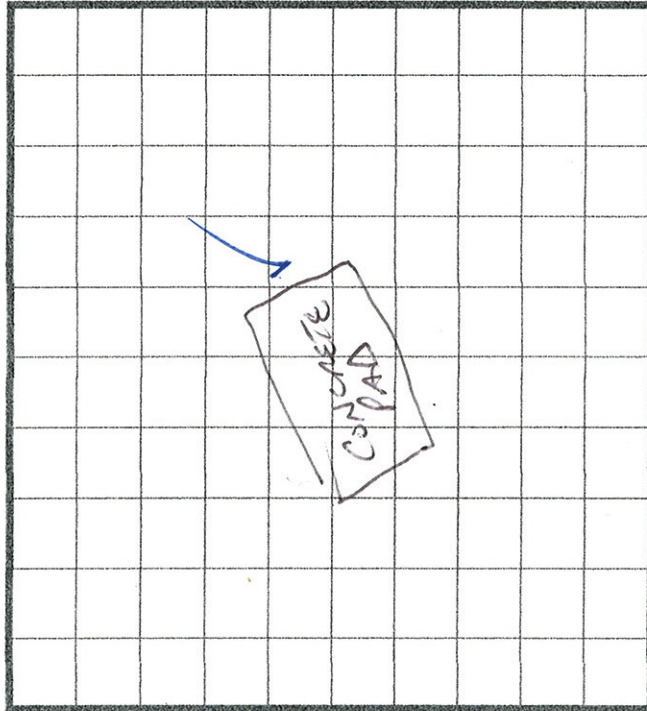

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap	
60	60		30 #		2 #	
MEC	NOMENCLATURE					DEPTH
MEC (2ea)	10lb. Smoke HC screening MI					3"
MEC (5ea)	grenade, rifle, smoke OE#-(399)					3"
MEC (1ea)	grenade M18 OE# (142)					3"
MEC (200+)	small arms 5.56 blank					3"
MEC (5ea)	3.0 cal rounds					3"

OE# (207)

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4/28/09	[Signature]	
Excavation Complete	4/28/09	[Signature]	
Quality Control Complete	4-29-09	[Signature]	
Client Quality Assurance Complete			





# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C3H5C2 Size: 100 x 100 ft  
 Date Started: 4/28/09  
 Date Completed: 4/28/09

Work Order No.: \_\_\_\_\_  
 UXO Supervisor: Wistensen  
 UXO Technician(s): Ransch Gonzalez

North  
 Direction


Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
45	45				3#

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4/28/09	<i>[Signature]</i>	
Excavation Complete	4/28/09	<i>[Signature]</i>	
Quality Control Complete	4-29-09	<i>[Signature]</i>	
Client Quality Assurance Complete			















# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No C3F515 Size: 100 x 100 ft

Date Started 4-28-09


Date Completed 4-28-09

Work Order No.:

UXO Supervisor L. Fuhrer

UXO Technician(s) Adams P. Z. Hendrix

North Direction

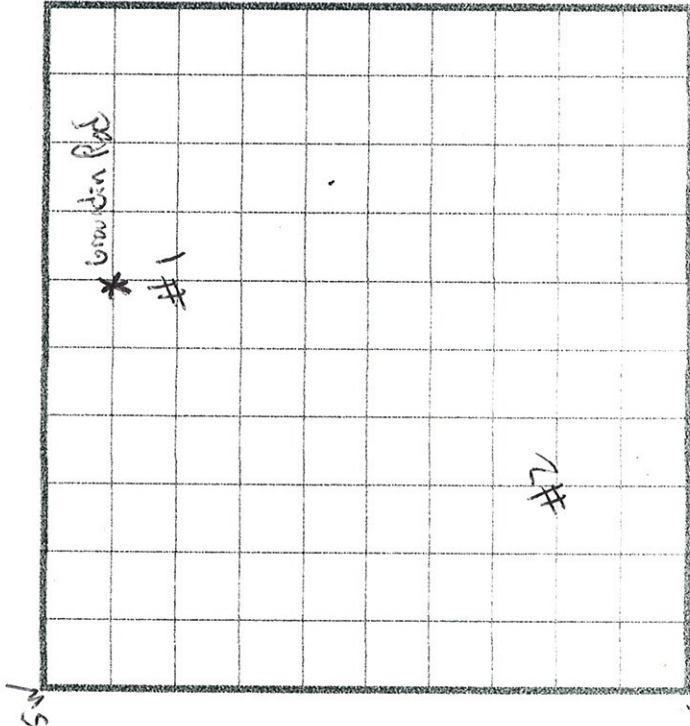

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
160	160			2.5	15

MEC	NOMENCLATURE	DEPTH
#1	Small arms (Blank 2lbs)	
#2	Signal illum ground MRS (1)	

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4/28/09	[Signature]	* Grounding Rod
Excavation Complete	4/28/09	[Signature]	
Quality Control Complete	4/28/09	[Signature]	
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3511 Size: 100 x 100 ft

Date Started: 4-28-09


Date Completed: 4-28-09

Work Order No.:

UXO Supervisor: Lauchner

UXO Technician(s): Patz Adams Hendrix

North  
Direction

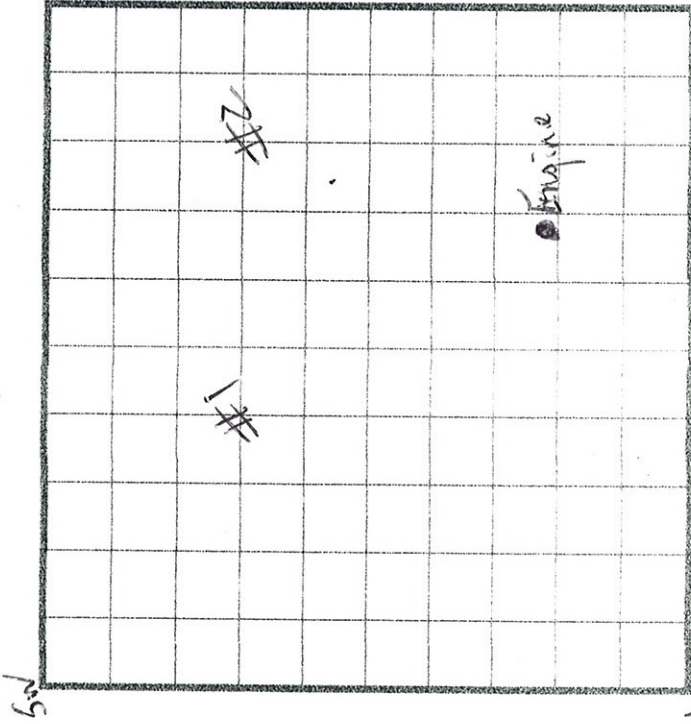

Total Anomalies	Total Excavations	Anomalies > ___ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
120	120			165	10

MEC	NOMENCLATURE	DEPTH
#1	Signal illum ground	12.5 (1)
#2	" "	" (1)

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-28-09		
Excavation Complete	4-28-09		● Engine in Grid
Quality Control Complete	4/28/09		
Client Quality Assurance Complete			






# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No: C3F5PH Size: 100 x 100 ft  
 Date Started: 4-28-09  
 Date Completed: 4-28-09

Work Order No.:  
 UXO Supervisor: L. Avehner  
 UXO Technician(s): Adams Wender

North Direction

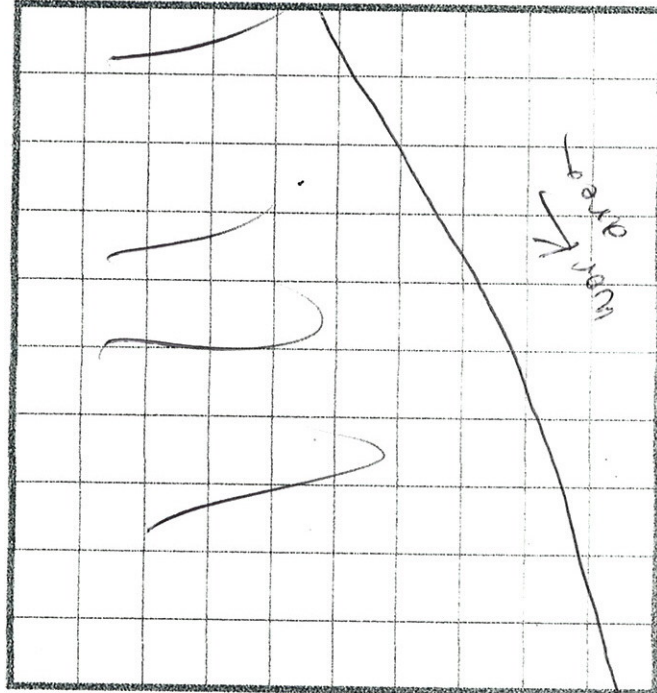

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
20	20	-	-	-	1

MEC	NOMENCLATURE	DEPTH

SW Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-28-09	[Signature]	
Excavation Complete	4-28-09	[Signature]	
Quality Control Complete	4-28-09	[Signature]	
Client Quality Assurance Complete	4-28-09	[Signature]	



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3F5P3 Size: 100 x 100 ft

Date Started: 4-28-09


Date Completed: 4-28-09

Work Order No.:

UXO Supervisor: LAVACHER

UXO Technician(s): Hendrix Adams

North Direction

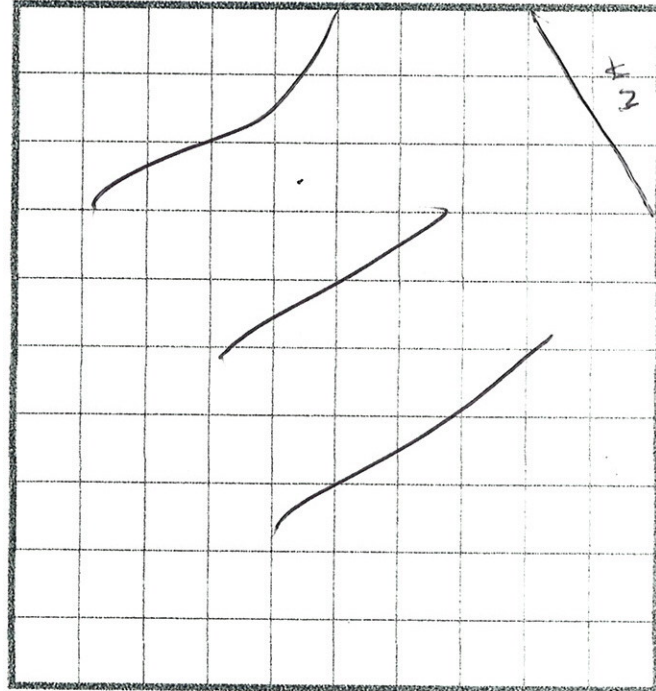

SUNCO Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
5	5		1	1	15

MEC	NOMENCLATURE	DEPTH
1		

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-28-09	[Signature]	
Excavation Complete	4-28-09	[Signature]	
Quality Control Complete	4-30-09	[Signature]	
Client Quality Assurance Complete			





# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No: CXF 5 H 5 Size: 100 x 100 ft  
 Date Started: 4-28-09  
 Date Completed: 4-28-09

Work Order No.:  
 UXO Supervisor: L. Auchner  
 UXO Technician(s): Adams Hendrix Paez

North  
 Direction

#1										
----	--	--	--	--	--	--	--	--	--	--

Total Anomalies	Total Excavations	Anomalies > <u>    </u> ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
160	160				30

MEC	NOMENCLATURE	DEPTH
#1	Grenade hand practice mfg (1)	

52000 Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-28-09	<i>[Signature]</i>	
Excavation Complete	4-28-09	<i>[Signature]</i>	
Quality Control Complete	4-30-09	<i>[Signature]</i>	
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program  
Grid No.: D3 3H5D3 Size: 100 x 100 ft  
Date Started: 4/27/09  
Date Completed: 4/27/09

Work Order No.: \_\_\_\_\_  
UXO Supervisor: Kristensen  
UXO Technician(s): Raash, Gonzalez

North Direction

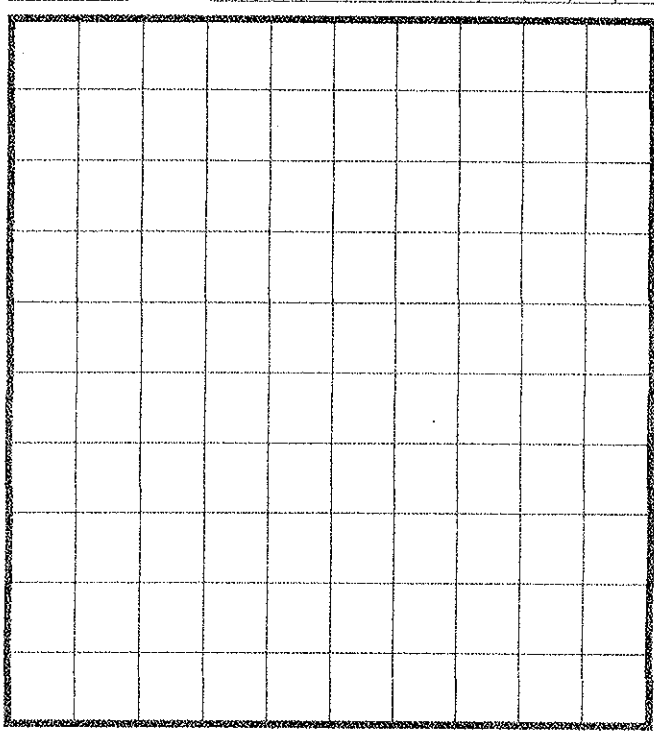

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
60	60		1#	3#	4#
<b>MEC</b>		<b>NOMENCLATURE</b>			<b>DEPTH</b>
	(1)	MIDS expended signed items			3"
	(2)	expended MEC @ place hand grenade			3"
	(3)	perforated Glass M49, surface trip			3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4/27/09	[Signature]	
Excavation Complete	4/27/09	[Signature]	
Quality Control Complete	4/28/09	[Signature]	
Client Quality Assurance Complete			

4/27/09



# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C34518 Size: 100 x 100 ft  
 Date Started: 4-27-09  
 Date Completed: 4-27-09

Work Order No.: \_\_\_\_\_  
 UXO Supervisor: T. Clark  
 UXO Technician(s): B. Smith  
J. Reiningford

North Direction  
 \_\_\_\_\_


Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
180	170		0	4.0	8.0

MEC	NOMENCLATURE	DEPTH
MD	Sig Illum grid M/25 (4)	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-27-09	<i>[Signature]</i>	
Excavation Complete	4-27-09	<i>[Signature]</i>	
Quality Control Complete	4-29-09	<i>[Signature]</i>	
Client Quality Assurance Complete			







Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C395E7 Size: 100 x 100 ft  
 Date Started: 4-27-09  
 Date Completed: 4-27-09

Work Order No.:  
 UXO Supervisor: T. Clark  
 UXO Technician(s): B. Smith  
J. Remington

North  
 Direction


Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > <u>    </u> ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
200	190		0	3.0	10.0
MEC	NOMENCLATURE				DEPTH
MD	Sig. IIR gas		M125	(3)	3"

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-27-09	TRB	
Excavation Complete	4-27-09	TRB	
Quality Control Complete	4-29-09	[Signature]	
Client Quality Assurance Complete			

4/29/09  
 JKR



# Grid Sweep Log

Project Name: Fort Ord Remediation Program

Grid No.: C39508 Size: 100 x 100 ft

Date Started: 4-27-09

Date Completed: 4-27-09

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): B. Smith

J. Reayton

North  
Direction


Note: Gridlines spaced 10' x 10'

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
100	85		0	2.0	3.5

MESG	NOMENCLATURE	DEPTH
	Sig I (low grade) M125 (1)	3"
	M48 Gravel, hard smoky, M48 (1)	3"

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-27-09	<i>[Signature]</i>	
Excavation Complete	4-27-09	<i>[Signature]</i>	
Quality Control Complete	4-29-09	<i>[Signature]</i>	
Client Quality Assurance Complete			



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C365E8 Size: 100 x 100 ft

Date Started: 4-27-09

Date Completed: 4-27-09

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): B. Smith

J. Reed

North  
Direction


Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
180	175		0	2.0	10.0

MEC	NOMENCLATURE	DEPTH
MD	Sig I item grid M125 (2)	3"
MD	Etag, Ground, had smoke (1)	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-27-09	[Signature]	
Excavation Complete	4-27-09	[Signature]	
Quality Control Complete	4-29-09	[Signature]	
Client Quality Assurance Complete			

4/29/09





# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C345D2 Size: 100 x 100 ft

Date Started: 4/24/09

Date Completed: 4/27/09

Work Order No.:

UXO Supervisor: Kristensen

UXO Technician(s): Smith, Rensch  
Gonzalez

North  
Direction


*Hot area over 3"*

*Hot area over 3"*

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
70	70			1#	10#

MEC	NOMENCLATURE	DEPTH
	(1) Expended miss signal ground item	

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4/27/09	<i>[Signature]</i>	
Excavation Complete	4/27/09	<i>[Signature]</i>	
Quality Control Complete	4-28-09	<i>[Signature]</i>	
Client Quality Assurance Complete			

*4/27/09*



# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3HS 05 Size: 100 x 100 ft

Date Started: 4/27/09

Date Completed: 4/27/09

Work Order No.:

UXO Supervisor: Kristensen

UXO Technician(s): Rausch, GENZLEE

North  
Direction

✓ Marked stake	
① POTS IN REMOVED	
by 10 DEEP TO	
GROUND	

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
30	30				3#

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4/27/09	[Signature]	
Excavation Complete	4/27/09	[Signature]	
Quality Control Complete	4-28-09	[Signature]	
Client Quality Assurance Complete			







# Grid Sweep Log

Project Name/Fort Ord Remediation Program  
 Grid No.: C3H5B2 Size: 100 x 100 ft  
 Date Started: 4-27-09  
 Date Completed: 4-27-09

Work Order No.: \_\_\_\_\_  
 UXO Supervisor: L. AUCHINCLOSS  
 UXO Technician(s): PAZ

North  
 Direction

A 10x10 grid representing the sweep area. Handwritten markers indicate the locations of anomalies: a circle with '#2' in the top-left quadrant and a circle with '#1' in the top-right quadrant.

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
175	175			1	15

MEC	NOMENCLATURE	DEPTH
#1	Flare above ground MISS (1)	
#2	U C (1 JUST FINS)	

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-27-09	[Signature]	
Excavation Complete	4-27-09	[Signature]	
Quality Control Complete	4-29-09	[Signature]	
Client Quality Assurance Complete			





WASTEWATER

# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3H5C6 Size: 100 x 100 ft

Date Started: 4/30/09


Date Completed: 4/30/09

Work Order No.:

UXO Supervisor: Kristensen

UXO Technician(s): Raasch, Hendrik GONZALEZ

North Direction

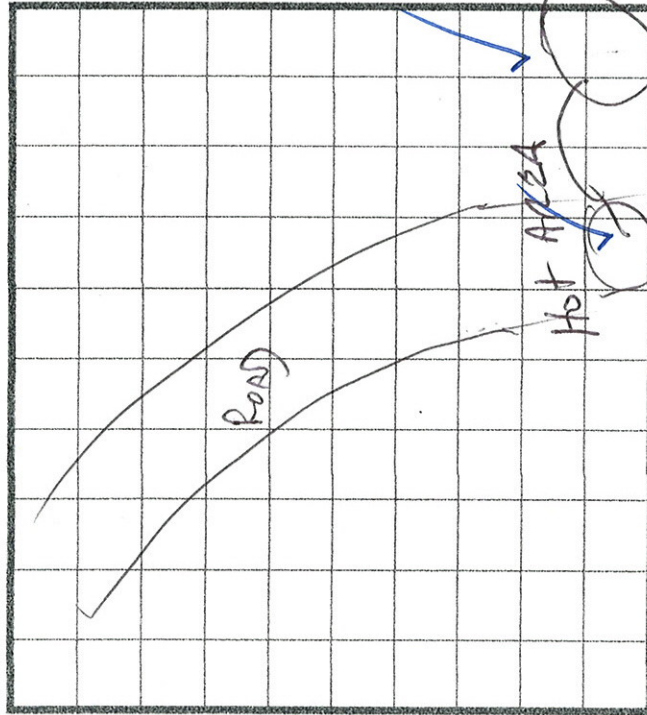

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
60	30				3#

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4/30/09		
Excavation Complete	4/30/09		
Quality Control Complete	4/30/09		
Client Quality Assurance Complete			

5/1/09







# Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C364D Size: 100 x 100 ft

Date Started: 4/30/09

Date Completed: 4/30/09


Work Order No.:

UXO Supervisor: Kristensen

UXO Technician(s): Rausch

Hendrix, Gonzalez

North  
Direction

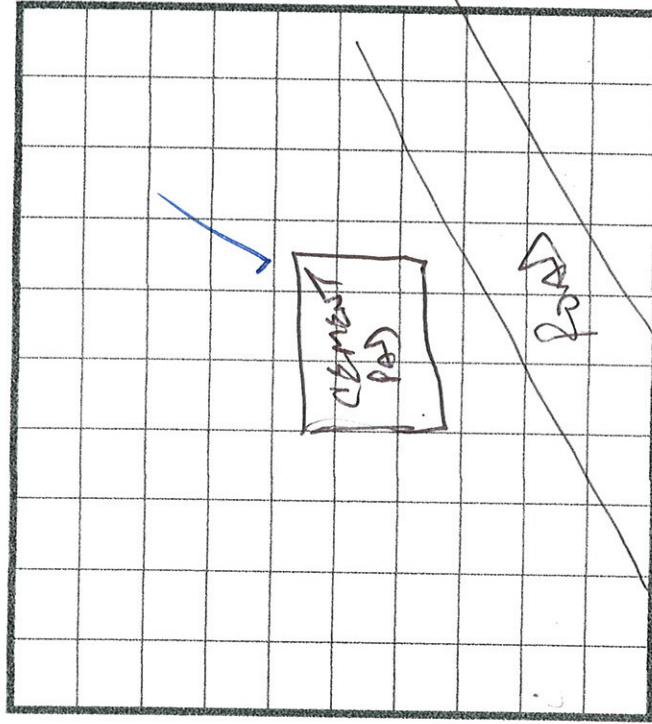

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
40	15				2#

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4/30/09	[Signature]	
Excavation Complete	4/30/09	[Signature]	
Quality Control Complete	5-4-09	[Signature]	
Client Quality Assurance Complete			





