



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3 G5B1 Size: 100 x 100 ft

Date Started: 4-30-09

Date Completed: 4-30-09

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): B. Smith

J. Remington

North
Direction

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	150
Total Excavations	142
Anomalies > ___ ft	
Total MEC Items	0
Pounds MEC Scrap	1.0
Pounds Non-MEC Scrap	5.5

MEG	NOMENCLATURE	DEPTH
MRP	Sig Item grnd M125 (1)	3"

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-30-09	[Signature]	
Excavation Complete	4-30-09	[Signature]	
Quality Control Complete	5-4-09	[Signature]	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C395B2 Size 100 x 100 ft

Date Started 4-30-09

Date Completed 4-30-09


North Direction

Work Order No.:

UXO Supervisor

UXO Technician(s)

T. Clark
B. Smith
J. Remington

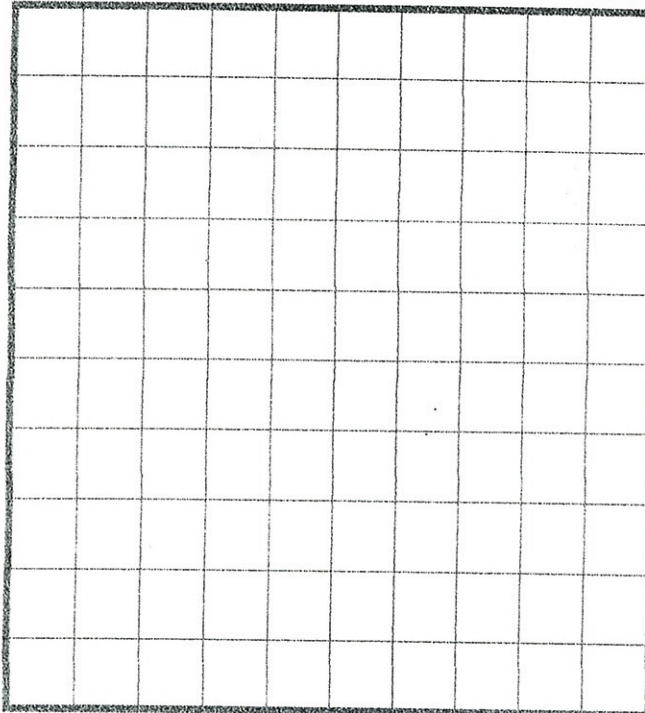

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>200</u>	<u>190</u>		<u>0</u>	<u>5.5</u>	<u>3.5</u>

	NOMENCLATURE	DEPTH
<u>MAG</u>		
<u>MD</u>	<u>Sig Illum grid M125 (1)</u>	<u>3"</u>
<u>Small Arms</u>	<u>Blanks (150)</u>	<u>3"</u>

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	<u>4-30-09</u>		
Excavation Complete	<u>4-30-09</u>		
Quality Control Complete	<u>5-4-09</u>		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name: Fort Ord Remediation Program

Grid No: C3G5C2 Size: 100 x 100 ft

Date Started: 4-30-09

Date Completed: 4-30-09

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): B. Smith
J. Remley

North
Direction

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
400	200		0	1.0	20.0

MEC	NOMENCLATURE	DEPTH
MD	Sig Illum grade M25 (1)	3"

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-30-09	<u>T. Clark</u>	
Excavation Complete	4-30-09	<u>T. Clark</u>	
Quality Control Complete	5-4-09	<u>J. Remley</u>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3F5J3 Size: 100 x 100 ft

Date Started: 4-30-09


Date Completed: 4-30-09

Work Order No.:

UXO Supervisor: L. Archer

UXO Technician(s): Pat Loran Adams

North
Direction

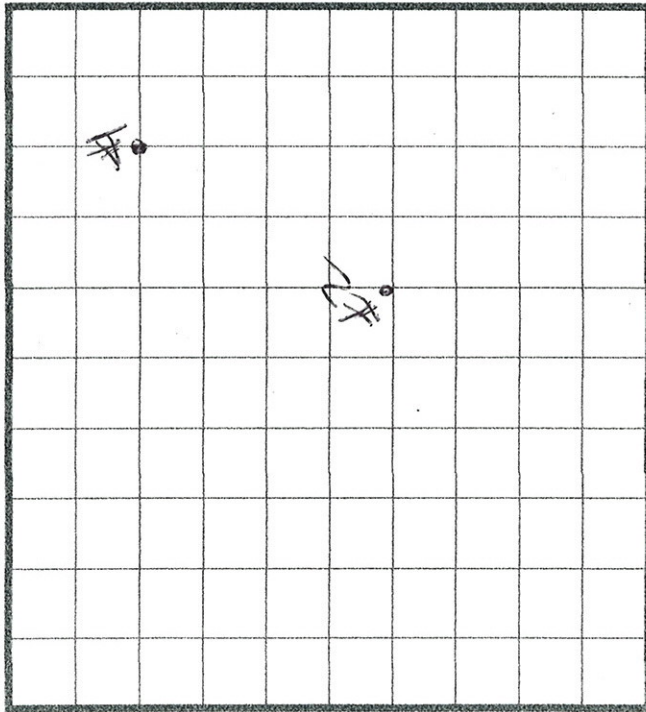

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
120	120	~	-	1	5

MEC	NOMENCLATURE	DEPTH
#1	Signal illum ground M25 (1)	
#2	Signal illum ground M25 (1)	

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-30-09	<i>[Signature]</i>	
Excavation Complete	4-30-09	<i>[Signature]</i>	
Quality Control Complete	4/30/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C2F522 Size: 100 x 100 ft

Date Started: 4-30-09

Date Completed: 4-30-09

Work Order No.:

UXO Supervisor: L Avichner

UXO Technician(s): Adams P. Z

North Direction

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
110	110	-	-	3	20

MEC	NOMENCLATURE	DEPTH
A1	Small arms Blank (3lbs)	M

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-30-09		
Excavation Complete	4-30-09		
Quality Control Complete	5-4-09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3F5J4 Size: 100 x 100 ft
 Date Started: 4-30-09
 Date Completed: 4-30-09

Work Order No.:
 UXO Supervisor: LAucher
 UXO Technician(s): LaRay Adams Pat

North
 Direction

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
160	160			75	20

MEC	NOMENCLATURE	DEPTH
#1	Small approx Blank (75 lbs)	

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-30-09		
Excavation Complete	4-30-09		
Quality Control Complete	4/30/09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3513 Size: 100 x 100 ft

Date Started: 4-29-09

Date Completed: 4-30-09

Work Order No.:

UXO Supervisor: L. Ashner

UXO Technician(s): Adam's Leaker Adams

North
Direction

63

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non- MEC Scrap
160	160	—	—	—	15

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-30-09	[Signature]	
Excavation Complete	4-30-09	[Signature]	
Quality Control Complete	4/30/09	[Signature]	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3 H5 B6 Size: 100 x 100 ft

Date Started: 4/29/09

Date Completed: 4/29/09

Work Order No.:

UXO Supervisor: Knistenson

UXO Technician(s): Raesch

Gonzalez

North
Direction

Note: Gridlines spaced 10 x10 ft.

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
45	40			1#	2#

MEC	NOMENCLATURE	DEPTH
(1ea)	expanded M125 signal illum ground	3'

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4/29/09	<i>[Signature]</i>	
Excavation Complete	4/29/09	<i>[Signature]</i>	
Quality Control Complete	4-30-09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No C3H5B4 Size 100 x 100 ft

Date Started 4/29/09

Date Completed 4/29/09


Work Order No

UXO Supervisor Kristensen

UXO Technician(s) Raasch

GONZALEZ

North Direction

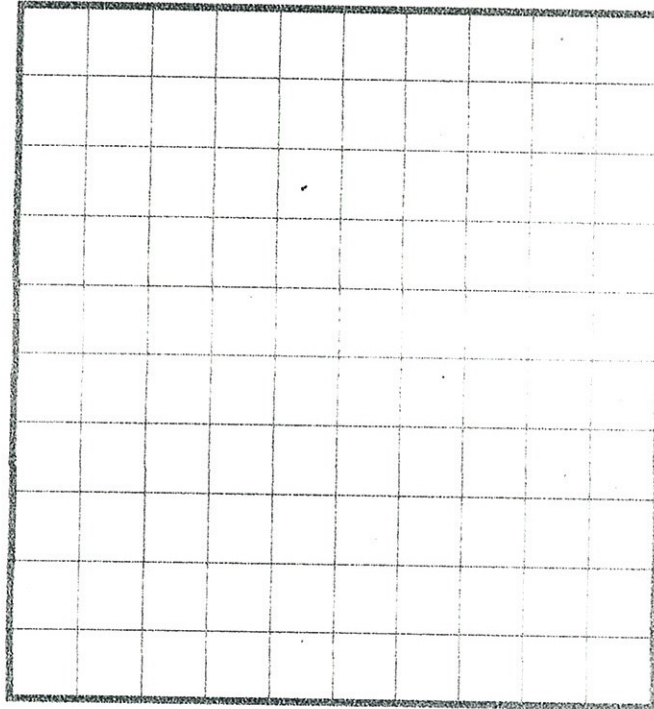

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>30</u>	<u>30</u>				<u>1#</u>

MEC	NOMENCLATURE	DEPTH

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	<u>4/29/09</u>		
Excavation Complete	<u>4/29/09</u>		
Quality Control Complete	<u>4-29-09</u>		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C345C4 Size: 100 x 100 ft

Date Started: 4/29/09

Date Completed: 4/29/09

Work Order No.:

UXO Supervisor: Mr. Jensen

UXO Technician(s): Raech, Gonzalez

North
Direction

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
60	60			2#	5#

MEC	NOMENCLATURE	DEPTH
(2)	Expanded MISS signal ground i Num	3"

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4/29/09		
Excavation Complete	4/29/09		
Quality Control Complete	4-29-09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Facility Remediation Program

Grid No. C3F505 Size 100 x 100 ft

Date Started 4-29-09

Date Completed 4-29


Work Order No

UXO Supervisor T Clark

UXO Technician(s) B. Smith

S. Herschicks, J. Remington

North:
Direction

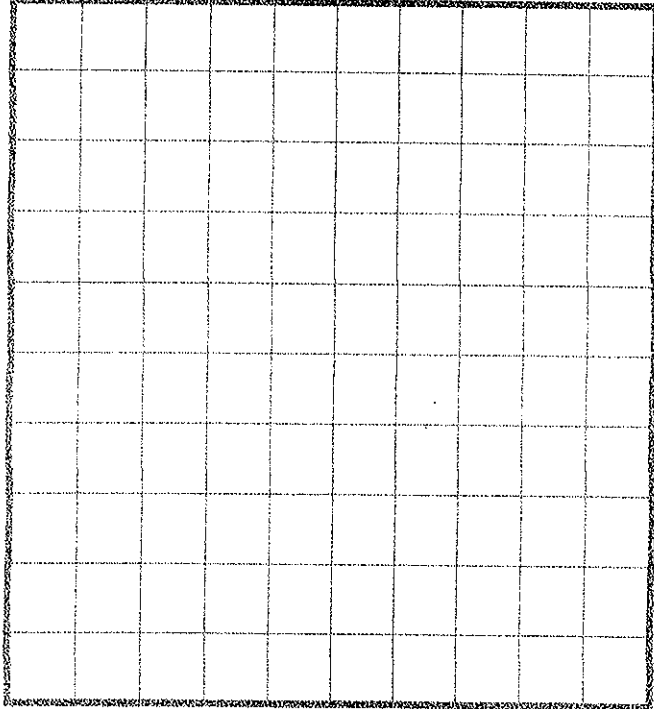

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
220	200		0	1.5	200

MEC	NOMENCLATURE	DEPTH
S.M.I. Arm	Blanks	3"
MO	Flux, Granite, Good MIO	3"
MO	Sig, Illum good MMS	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	4-29-09		
Excavation Complete	4-29-09		
Quality Control Complete	4/30/09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C365A5 Size: 100 x 100 ft

Date Started 4-29-09

Date Completed 4-29-09

Work Order No:

UXO Supervisor T Clark

UXO Technician(s) B Smith

S. Heidricks, J. Rearington

North
Direction


Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
<u>140</u>	<u>120</u>		<u>0</u>	<u>0</u>	<u>5.5</u>

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	<u>4-29-09</u>	<u>TRC</u>	
Excavation Complete	<u>4-29-09</u>	<u>TRC</u>	
Quality Control Complete	<u>4/30/09</u>	<u>JGK</u>	
Client Quality Assurance Complete			

5/15/09



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C3G5C5 Size: 100 x 100 ft

Date Started 4-29-09

Date Completed 4-29-09

Work Order No: _____

UXO Supervisor T. Clark

UXO Technician(s) B. Smith

S. Hendricks, J. Remington

North
Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
190	180		0	0	8.5

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-29-09	[Signature]	
Excavation Complete	4-29-09	[Signature]	
Quality Control Complete	4-29-09	[Signature]	
Client Quality Assurance Complete			

5/1



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C2F5H3 Size: 100 x 100 ft
 Date Started: 4-24-09
 Date Completed: 4-24-09

Work Order No.: _____
 UXO Supervisor: LAVINGTON
 UXO Technician(s): ADAMS, PAZ

North
 Direction

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non- MEC Scrap
120	120		1	-	6

MEC	NOMENCLATURE	DEPTH
-		

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-29-09	<i>[Signature]</i>	
Excavation Complete	4-29-09	<i>[Signature]</i>	
Quality Control Complete	4/30/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

cont. 5/1/09



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3F564 Size: 100 x 100 ft

Date Started: 4-29-09


Date Completed: 4-29-09

Work Order No.:

UXO Supervisor: L. Avcher

UXO Technician(s): PAZ Adams

North Direction

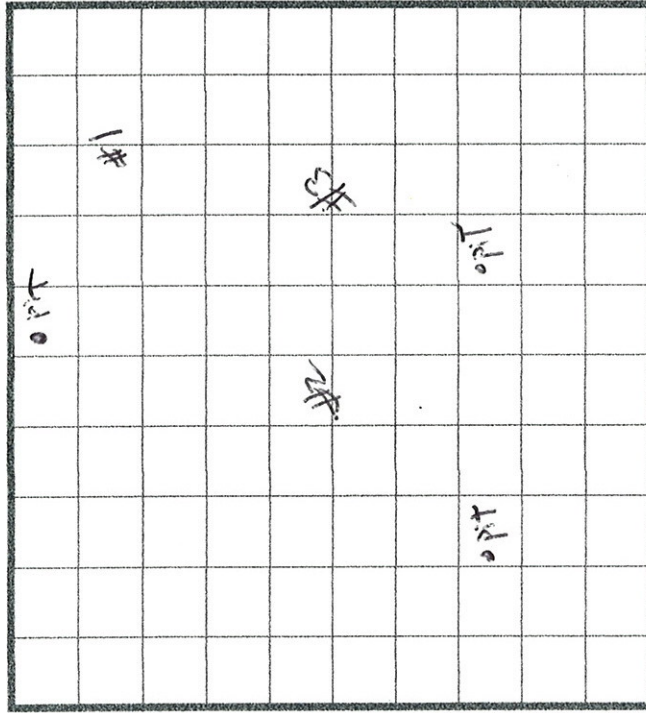

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
200	200	~	~	6	40

MEC	NOMENCLATURE	DEPTH
#1	Small illum green M125 (1)	
#2	" "	(1)
#3	Small asmb Blanks (4 lbs)	

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-29-09	[Signature]	2 link pits 1 ammo can pit 7 counts
Excavation Complete	4-29-09	[Signature]	
Quality Control Complete	4-30-09	[Signature]	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3F563 Size: 100 x 100 ft

Date Started: 4-28-09


Date Completed: 4-29-09

Work Order No.:

UXO Supervisor: L A Uchner

UXO Technician(s): Adam Paz

North
Direction

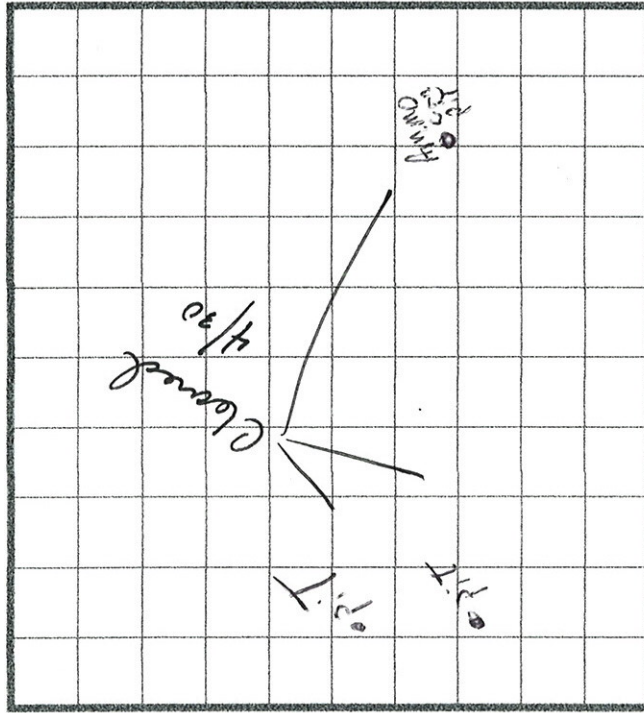

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
160	160	-	-	-	10

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	4-28-09	<i>[Signature]</i>	2 Bur type pits 1 ammo can pit
Excavation Complete	4-28-09 4-28-09	<i>[Signature]</i>	
Quality Control Complete	4-30-09	<i>[Signature]</i>	
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3E5H1 Size 100 x 100 ft
 Date Started 5/4/09
 Date Completed 5/4/09

Work Order No _____
 UXO Supervisor Caldwell
 UXO Technician(s) Remington Hendricks

North Direction _____

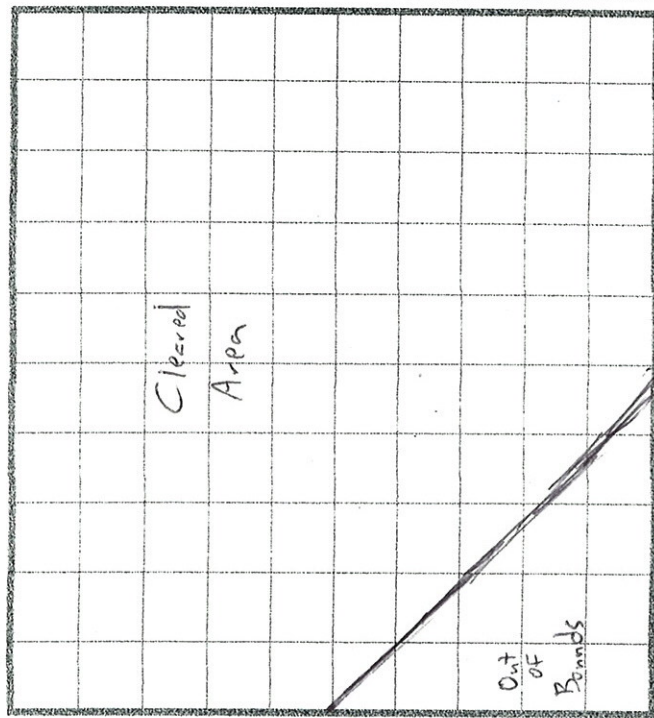

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
221			16	2	125

MEC	NOMENCLATURE	DEPTH
16 DMM	M205H2 Grenade Fuze OE #78	Surface → 18"
	(a) 5 gal BUCKETS SMALL ARMS	OE #10

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/4/09	<i>[Signature]</i>	
Excavation Complete	5/4/09	<i>[Signature]</i>	
Quality Control Complete	5/5/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3F4H0 Size: 100 x 100 ft

Date Started: 5/4/09

Date Completed: 5/4/09


Work Order No.:

UXO Supervisor: Caldwell

UXO Technician(s): Remington

Hendricks

North Direction

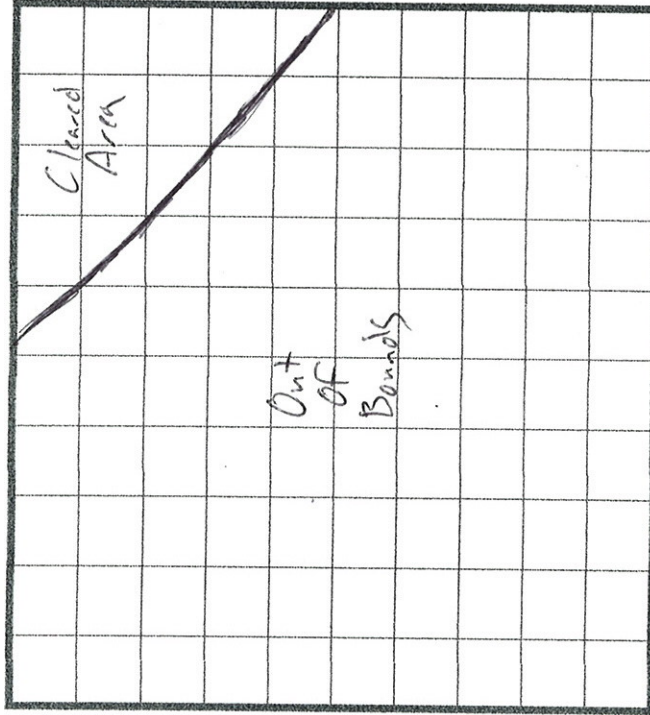

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
41	41		0	0	10

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5/4/09	<i>[Signature]</i>	
Excavation Complete	5/4/09	<i>[Signature]</i>	
Quality Control Complete	5.5.09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3FSG1 Size 100 x 100 ft

Date Started 5/4/09

Date Completed 5/4/09


Work Order No

UXO Supervisor Caldwell

UXO Technician(s) Remington

Henricks

North Direction

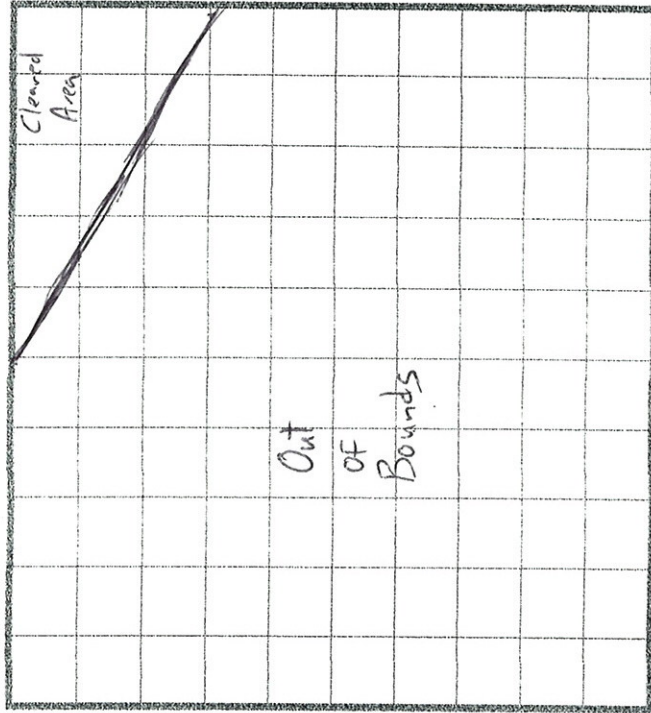

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
17			0	0	11

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/4/09	<i>[Signature]</i>	
Excavation Complete	5/4/09	<i>[Signature]</i>	
Quality Control Complete	5/5/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3F5G2 Size 100 x 100 ft

Date Started 5/4/09

Date Completed 5/4/09


Work Order No. _____

UXO Supervisor Andrew Caldwell

UXO Technician(s) Joe Remington

Steve Hendricks

North
Direction

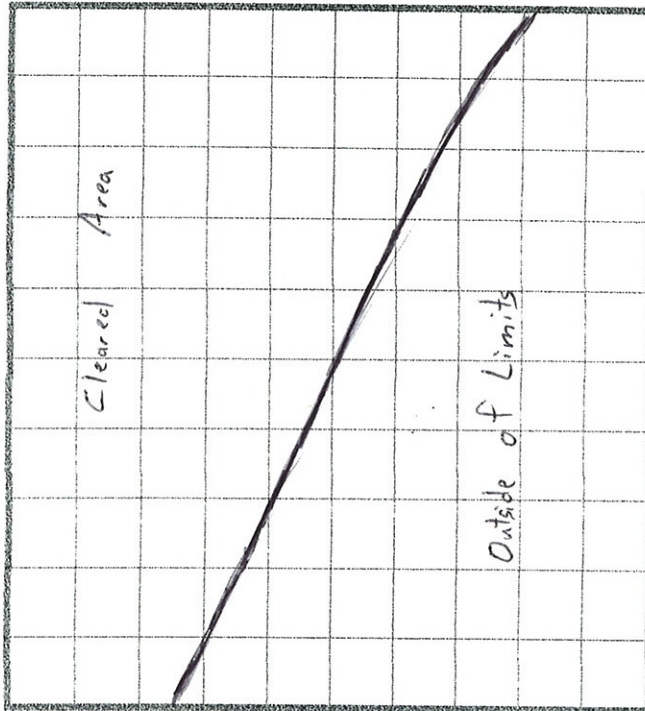

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
194			0	0	42

MEC	NOMENCLATURE	DEPTH

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/4/09	<i>[Signature]</i>	
Excavation Complete	5/4/09	<i>[Signature]</i>	
Quality Control Complete	5/5/09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3F4I0 Size 100 x 100 ft

Date Started 5/4/09

Date Completed 5/4/09


Work Order No

UXO Supervisor Caldwell

UXO Technician(s) Remington

Hendricks

North
Direction

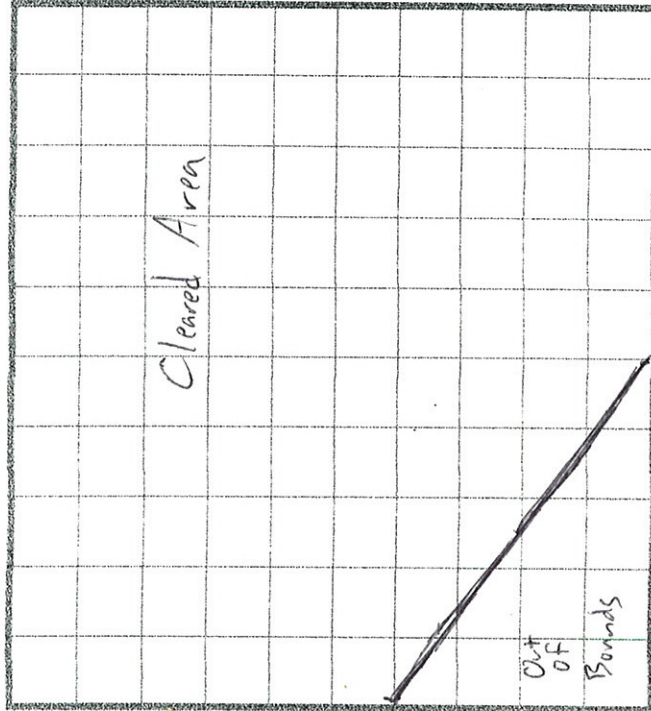

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
240	240		0	0	40

MEC	NOMENCLATURE	DEPTH
MD	(5) M125 FLARES DE #389	

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/4/09	<i>[Signature]</i>	
Excavation Complete	5/4/09	<i>[Signature]</i>	
Quality Control Complete	5/5/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. 03F419 Size: 100 x 100 ft

Date Started: 5/4/09

Date Completed: 5/4/09


Work Order No:

UXO Supervisor: Caldwell

UXO Technician(s): Remington

Hendricks

North Direction

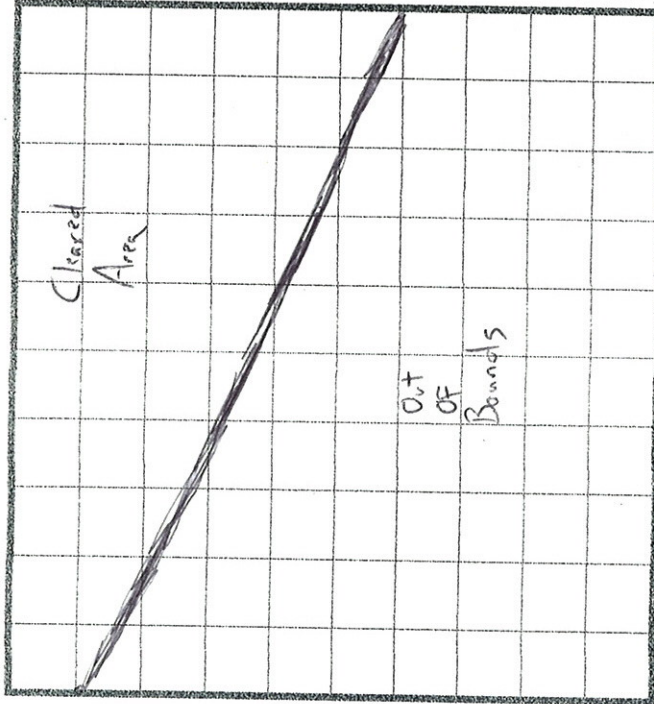

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
84			0	0	17

MEG	MD	NOMENCLATURE	DEPTH
		(1) MISS FLARE OE # 389	

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5/24/09	<i>[Signature]</i>	
Excavation Complete	5/4/09	<i>[Signature]</i>	
Quality Control Complete	5/5/09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C34498 Size 100 x 100 ft

Date Started 5-4-09

Date Completed 5-4-09


Work Order No

UXO Supervisor T. Clark

UXO Technician(s) E. Gonzales

B. Adams

North Direction

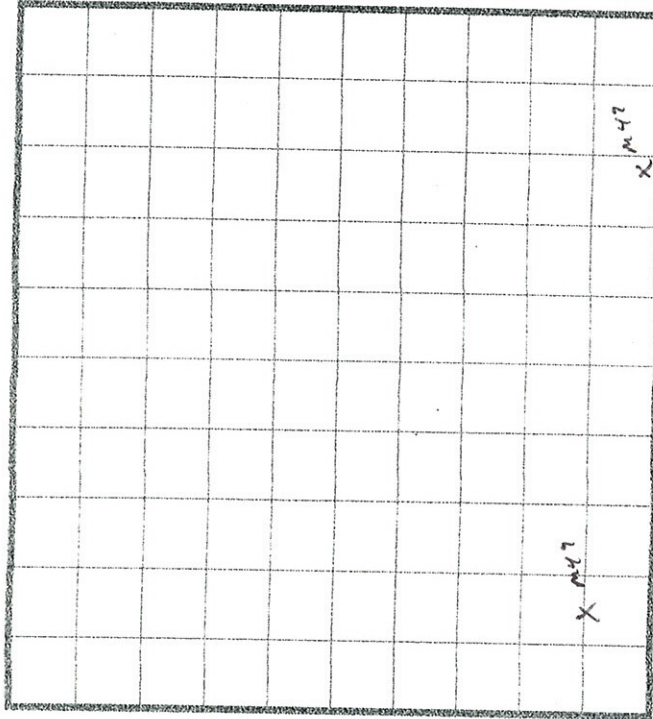

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
350	345		2	3.0	35

MEC	NOMENCLATURE	DEPTH
DMM	Flare, Trip M49 (2)	OE# 64 3"
MD	Signal Illum grad M25 (2)	OE# 389 3"
	Small Arms Blanks (65)	OE# 10 3"

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-4-09	[Signature]	
Excavation Complete	5-4-09	[Signature]	
Quality Control Complete	5-5-09	[Signature]	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C364F8 Size 100 x 100 ft

Date Started 5-4-09

Date Completed 5-4-09

Work Order No

UXO Supervisor T. Clark

UXO Technician(s) F. Gonzalez

B. Adams

North Direction

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
700	390		0	.1	40

WES	NOMENCLATURE	DEPTH
Small Arms	Blanks OE #10 (9)	3'

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-4-09	<i>[Signature]</i>	
Excavation Complete	5-4-09	<i>[Signature]</i>	
Quality Control Complete	5-5-09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3657A6 Size: 100 x 100 ft
 Date Started: 5/4/09
 Date Completed: 5/4/09

Work Order No.:
 UXO Supervisor: Kristensen
 UXO Technician(s): Laroe Paszalanec Smith

North
Direction

(Empty grid for gridlines spaced 10 x 10 ft)									
--	--	--	--	--	--	--	--	--	--

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
40	10			1 #	2 #

MEC	NOMENCLATURE	DEPTH
(1)	M125 expanded snake ground: Mium	3"
	OE # 389	

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5/4/09		
Excavation Complete	5/4/09		
Quality Control Complete	5.5.09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C36525 Size 100 x 100 ft

Date Started 5/4/2009

Date Completed 5/4/2009


Work Order No:

UXO Supervisor Kristensen

UXO Technician(s) KAROE

SMITH PASZALANIEC

North
Direction

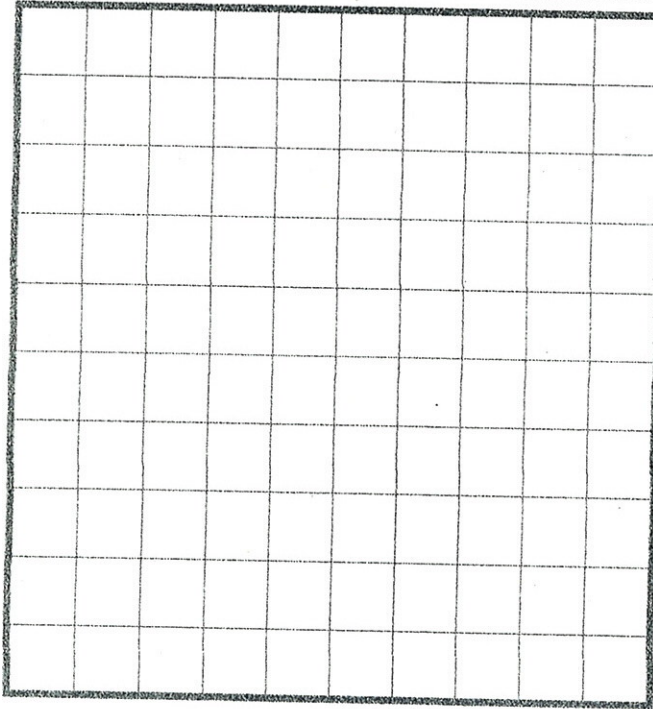

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
40	8025				4#

MEC	NOMENCLATURE	DEPTH
(1)	Expanded M125 Signal Illum Ground	3" OE# 389
(6ea)	blank 80 cal Cast OE# 15	3"

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5/4/09	[Signature]	
Excavation Complete	5/4/09	[Signature]	
Quality Control Complete	5.5.09	[Signature]	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C365J4 Size: 100 x 100 ft
 Date Started: 5/4/2009
 Date Completed: 5/4/2009

Work Order No. _____
 UXO Supervisor: Kristensen
 UXO Technician(s): Laroe
 Smith Paszalanice

North Direction

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > ____ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
60	30			3#	50#

MEC	NOMENCLATURE	DEPTH
(1)	Expanded M25 signal 7mm ground (lower) blank 30cm chart.	3" OE #389
		3" OE #15

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5/4/09	[Signature]	
Excavation Complete	5/4/09	[Signature]	
Quality Control Complete	5-4-09	[Signature]	
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C365J6 Size: 100 x 100 ft
 Date Started: 5/4/2009
 Date Completed: 5/4/2009

Work Order No.
 UXO Supervisor: Kristensen
 UXO Technician(s): LAROE SMITH PIZZAGALANIE

North Direction

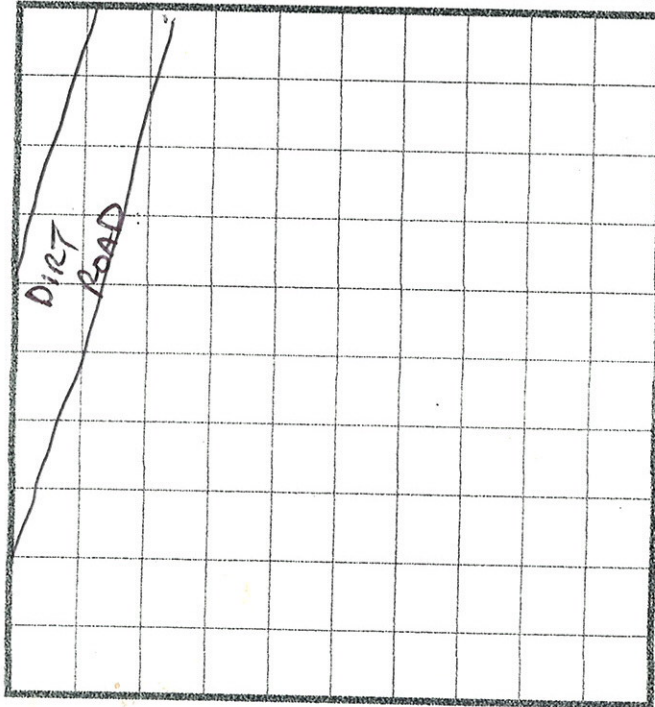

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
60	20				20#

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/4/09	<i>[Signature]</i>	
Excavation Complete	5/4/09	<i>[Signature]</i>	
Quality Control Complete	5/4/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No C34515 Size 100 x 100 ft

Date Started 5/4/09


Date Completed 5/4/09

Work Order No

UXO Supervisor LAROE

UXO Technician(s) SMITH
Paszalaniec

North Direction

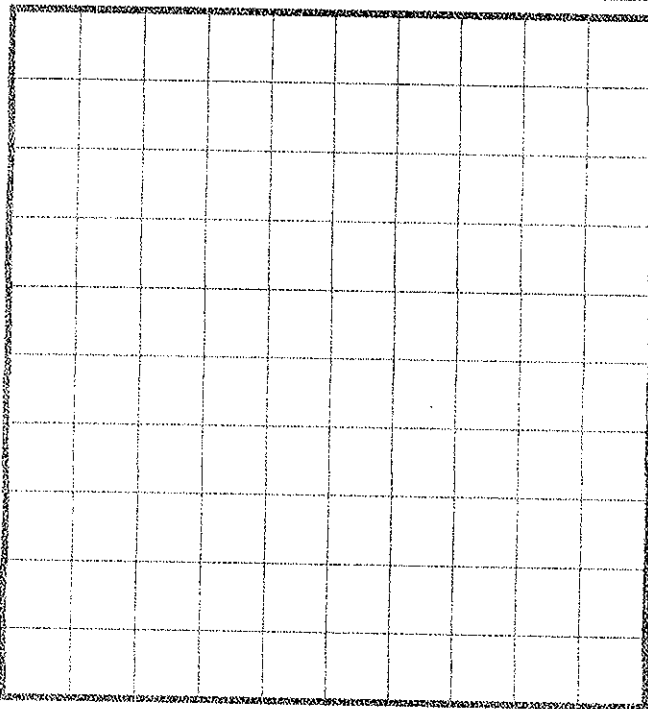

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
27	27				3

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/4/09	[Signature]	
Excavation Complete	5/4/09	[Signature]	
Quality Control Complete	5/4/09	[Signature]	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C565C# Size: 100 x 100 ft

Date Started: 5-1-09

Date Completed: 5-1-09

North
Direction

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): B. Smith

S. Heudorfs

--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
150	130		0	0	15.0

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-1-09		
Excavation Complete	5-1-09		
Quality Control Complete	5-4-09		
Client Quality Assurance Complete			



Not Entered

Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No: C364B9 Size: 100 x 100 ft.
 Date Started: 5/1/09
 Date Completed: 5/1/09

Work Order No.:
 UXO Supervisor: Kristensen
 UXO Technician(s): Reasch, Gonzalez

North Direction

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
40	25			1#	2#

MEC	NOMENCLATURE	DEPTH
(see) MK62	Grenade Practice expended	3"
	OE # 135	

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/1/09	[Signature]	
Excavation Complete	5/1/09	[Signature]	
Quality Control Complete	5-4-09	[Signature]	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C36219 Size: 100 x 100 ft
 Date Started: 5-8-09
 Date Completed: 5-8-09

Work Order No.: _____
 UXO Supervisor: J. Clark
 UXO Technician(s): B. Smith
F. Gonzalez, B. Adams

North
Direction

<i>App: 4 of</i>									

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
40	36		0	1.0	3.5

MEC	NOMENCLATURE	DEPTH
MD	Sig Ethanol MISS (1)	3"

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-8-09	<i>[Signature]</i>	
Excavation Complete	5-8-09	<i>[Signature]</i>	
Quality Control Complete	5/12/09	<i>[Signature]</i>	
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C34210 Size: 100 x 100 ft
 Date Started: 5-8-09
 Date Completed: 5-8-09

Work Order No.:
 UXO Supervisor: T. Clark
 UXO Technician(s): E. Gonzales
B. Adams

North
 Direction

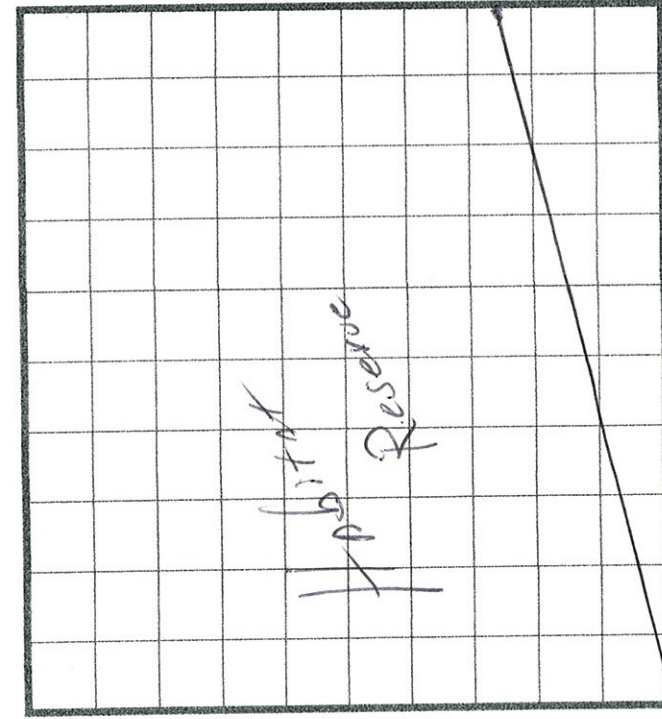

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
9	7		0	1.0	.1

MEC	NOMENCLATURE	DEPTH
MD	Sig I/In grid M25 (1)	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-8-09	[Signature]	
Excavation Complete	5-8-09	[Signature]	
Quality Control Complete	5/12/09	[Signature]	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
Grid No.: C36270 Size: 100 x 100 ft
Date Started: 5-8-09
Date Completed: 5-8-09

Work Order No.:
UXO Supervisor: T. Clark
UXO Technician(s): F. Gonzalez
B. Adams

North
Direction

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
70	60		0	1.0	2.0

MEC	NOMENCLATURE	DEPTH
MO	Sig I/lin gravel M25 (1)	3"
Small Arms	7.62 mm Brads (23)	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-8-09		
Excavation Complete	5-8-09		
Quality Control Complete	5/12/09		
Client Quality Assurance Complete			

Grid Sweep Log

Project Name: Fort Ord Remediation Program

Grid No: **C365H1** Size: 100' x 100'

Date Started: **5/8/09**

Date Completed: **5/8/09**

Work Order No:


U/D Supervisor:

U/D Technician:

**Kristensen
Caldwell
Postalaniec**

North:

Direction:

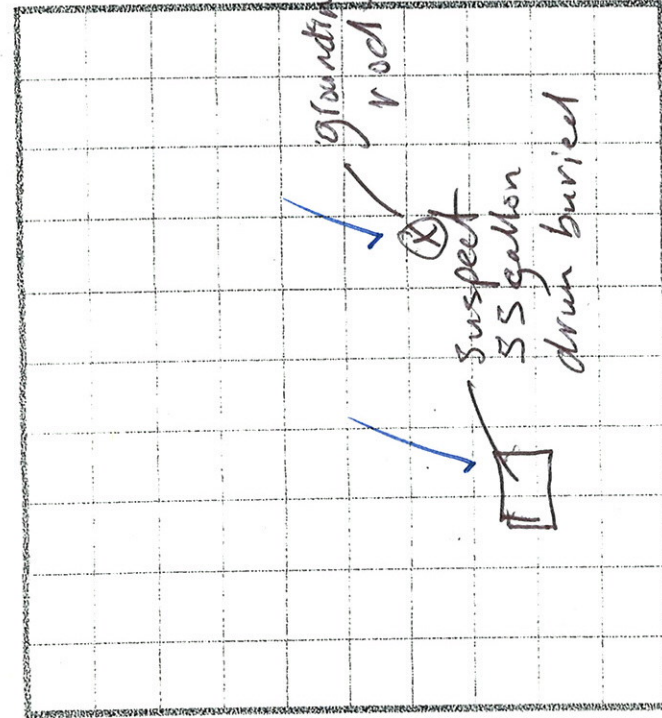

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non MEC Scrap
				2 #	4 #

MEC	NOMENCLATURE	DEPTH
	<i>Blank armor</i>	

Note: Gridlines spaced 10' x 10'

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/8/09	<i>[Signature]</i>	
Excavation Complete	5/8/09	<i>[Signature]</i>	
Quality Control Complete	5/12/09	<i>[Signature]</i>	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name: East Lynn Remediation Program
 Grid No: C3 G5 G7 Size: 100.0 x 100.0
 Date Started: 5/19/09
 Date Completed: 5/18/09



Work Center No: _____
 UWD Supervisor: Kristensen
 UWD Technician(s): Caldwell
Paszalanice

North
 Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
60	25			1#	3#

MEC	NOMENCLATURE	DEPTH
35ea	blank small ammo	

Note: Gridlines spaced to 416 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/19/09		
Excavation Complete	5/21/09		
Quality Control Complete	5-12-09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name: Fort Ord Remediation Program

Grid No: C365F5 Size: 100 x 100 ft

Date Started: 5-8-09

Date Completed: 5-8-09

Work Order No:

UXO Supervisor: Laviched

UXO Technician(s): Hendricks Demington

UXO Technician(s): LaRoi

North Direction

			#1															

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
90	90	~	~	15	5
MEC	NOMENCLATURE				DEPTH
#1	Signal illum ground MDS 07				

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-8-09		
Excavation Complete	5-8-09		
Quality Control Complete	5/8/09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C305FH Size: 100 x 100 ft

Date Started: 5-5-09


Date Completed: 5-6-09

Work Order No.

UXO Supervisor: L Archer

UXO Technician(s): Lofan Remington
Herberts

North Direction

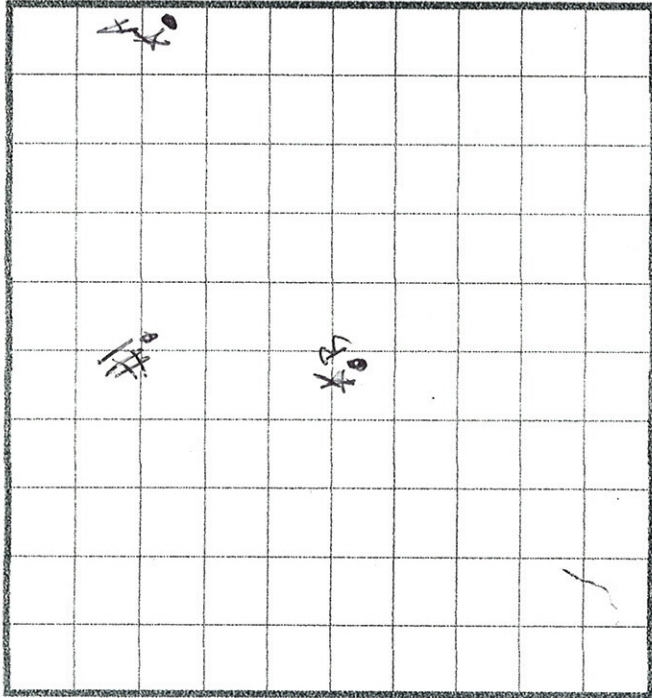

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
100	100			1	3

MEC	NOMENCLATURE	DEPTH
#1	9 Ground with signal Radium (1)	
	Small arms Blank (1)	

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-9-09		A* - Grounding Rod
Excavation Complete	5-8-09		
Quality Control Complete	5/8/09		B* - Brass and Link pit
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
Grid No: C265F3 Size 100 x 100 ft.
Date Started: 5-6-04
Date Completed: 5-6-04

Work Order No. _____
UXO Supervisor: L. A. Chner
UXO Technician(s): Headsicks, Remington

North
Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
95	95			1	4

MEC	NOMENCLATURE	DEPTH
	Small Army Block (116)	

Note: Gridlines spaced 10 x 10 ft.

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-6-04		
Excavation Complete	5-8-04		
Quality Control Complete	5-12-04		
Client Quality Assurance Complete			



Grid Sweep Log

Work Order No _____
 UXO Supervisor Kristensen
 UXO Technician(s) Caldwell Paszalanic

Project Name/Fort Ord Remediation Program
 Grid No C365H3 Size 100 x 100 ft
 Date Started 5/7/09
 Date Completed 5/7/09

North Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
30	10			2#	1#

MEC (200) expended M125 signal : 11am ground									

NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/7/09		
Excavation Complete	5/7/09		
Quality Control Complete	5/8/09		
Client Quality Assurance Complete			

Grid Sweep Log

Project Name: Fort Ord Remediation Program
 Cont. No: **C3 G5 H2** Size: 100' x 100'
 Date Started: **5/7/09**
 Date Completed: **5/7/09**

Work Order No.
 U/O Supervisor: **Kristensen**
 U/O Technician(s): **Caldwell**
Pasztalaniec

North
 Direction

Total Anomalies	Total Excavations	Anomalies \approx ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
60	30				10#

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10' x 10' ft.

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/7/09	<i>[Signature]</i>	
Excavation Complete	5/7/09	<i>[Signature]</i>	
Quality Control Complete	5/8/09	<i>[Signature]</i>	
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3H3A5 Size: 100 x 100 ft
 Date Started: 5-7-09
 Date Completed: 5-7-09

Work Order No.:
 UXO Supervisor: T. Clark
 UXO Technician(s): B. Smith
K. Gonzalez, B. Adams

North
 Direction

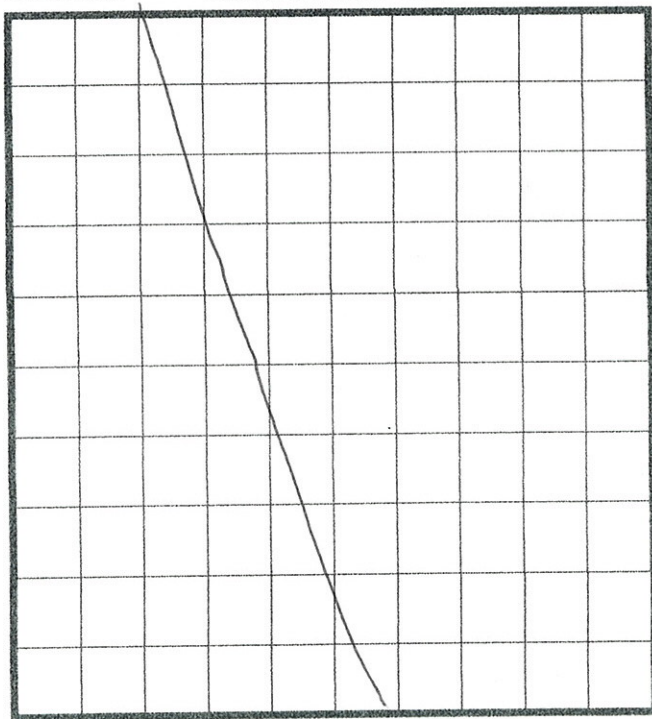

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
35	30		0	1.5	0.5

MEC	NOMENCLATURE	DEPTH
MD	Sig Thin grad M125 (1)	3"
Small Iron	S.S.C Blocks (12)	3"

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-7-09	[Signature]	
Excavation Complete	5-7-09	[Signature]	
Quality Control Complete	5/8/09	[Signature]	
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3 H3 A4 Size: 100 x 100 ft
 Date Started: 5-7-09
 Date Completed: 5-7-09

Work Order No.: _____
 UXO Supervisor: T. Clark
 UXO Technician(s): B. Smith
E. Gonzalez, B. Adams

North Direction

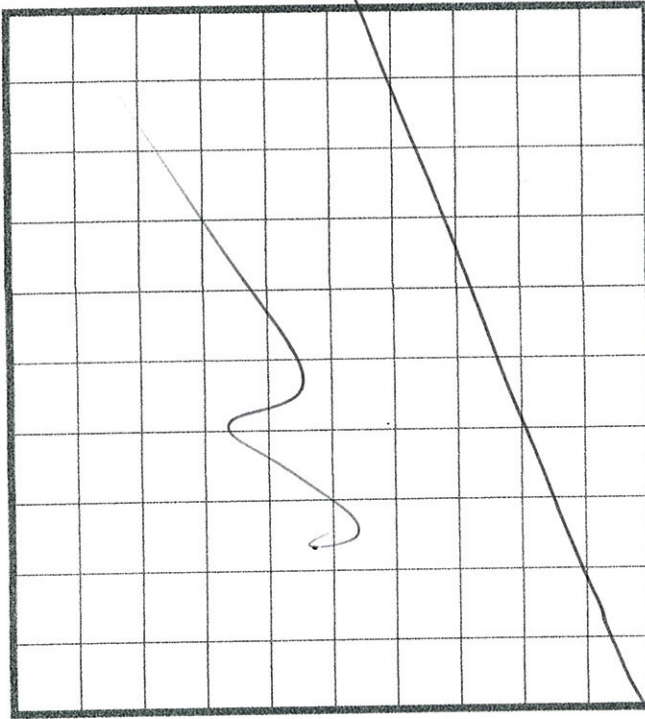

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
10	10		0	0	3.0

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-7-09	<u>[Signature]</u>	
Excavation Complete	5-7-09	<u>[Signature]</u>	
Quality Control Complete	5/8/09	<u>[Signature]</u>	
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C343J3 Size: 100 x 100 ft
 Date Started: 5-7-09
 Date Completed: 5-7-09

Work Order No.:
 UXO Supervisor: T. Clark
 UXO Technician(s): B. Smith
E. Gonzales, B. Adams

North
 Direction

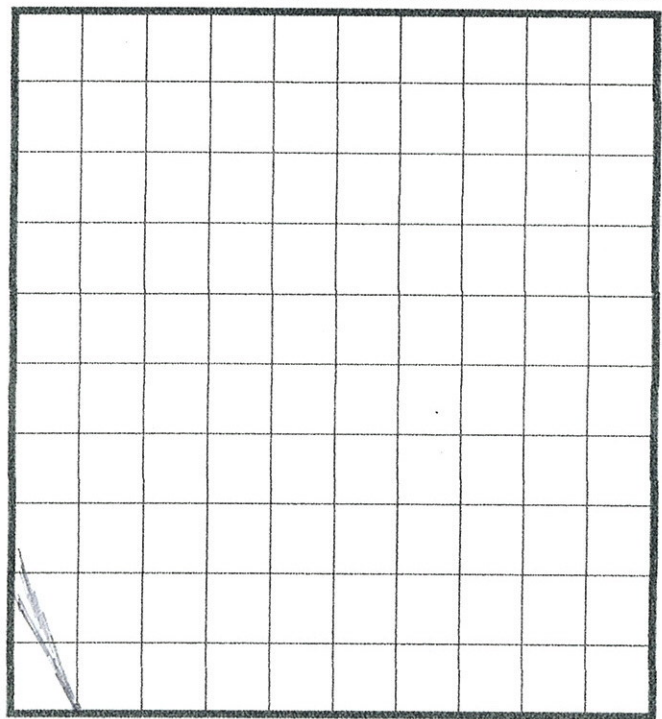

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
64	62		0	3.0	3.0

	NOMENCLATURE	DEPTH
MEC		
MR	Sig Flom grid M25 (1)	3"

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-7-09	<i>TRE</i>	
Excavation Complete	5-7-09	<i>TRE</i>	
Quality Control Complete	5/8/09	<i>DR</i>	
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
Grid No.: C39302 Size: 100 x 100 ft
Date Started: 5-7-09
Date Completed: 5-7-09

Work Order No.:
UXO Supervisor: T. Clark
UXO Technician(s): B. Smith
E. Gonzalez, B. Adams

North
Direction

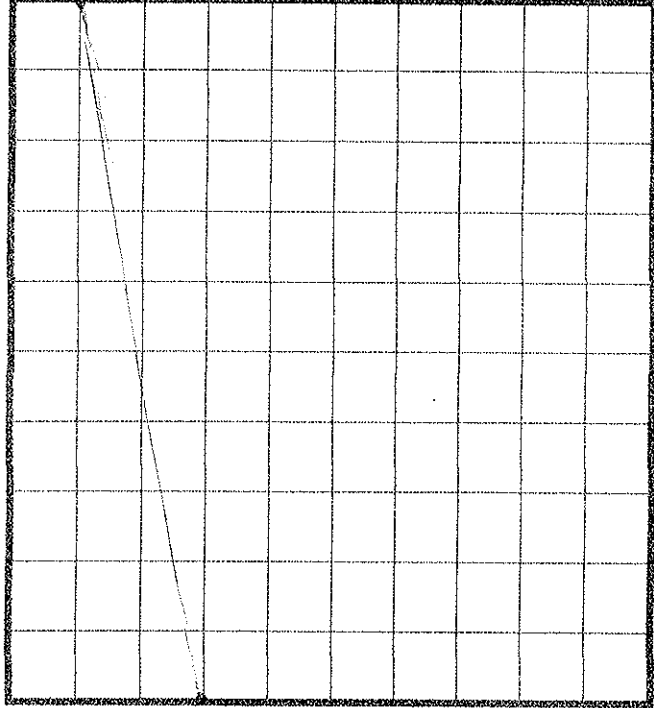

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
37	36		0	0	2.0

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5/7/09	<u>[Signature]</u>	
Excavation Complete	5/7/09	<u>[Signature]</u>	
Quality Control Complete	5/8/09	<u>[Signature]</u>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C393 V1 Size 100 x 100 ft

Date Started 5-7-09

Date Completed 5-7-09


Work Order No

UXO Supervisor T. Clark

UXO Technician(s) B. Smith

F. Gonzalez, B. Adams

North
Direction

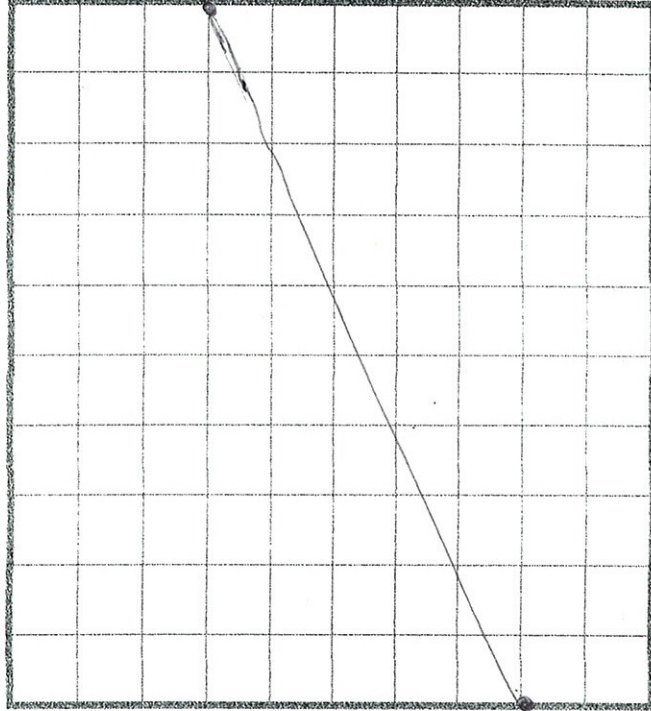

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
9	8		0	0	.1

MEC	NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-7-09	<u>[Signature]</u>	
Excavation Complete	5-7-09	<u>[Signature]</u>	
Quality Control Complete	5/8/09	<u>[Signature]</u>	
Client Quality Assurance Complete			




Grid Sweep Log

Project Name: Fort Ord Remediation Program
 Grid No.: E3 F5 T1 Size: 100 x 100 ft
 Date Started: 5-7-09
 Date Completed: 5-7-09

Work Order No.: _____
 UXO Supervisor: L. Aucher
 UXO Technician(s): Hendricks Latour

North Direction

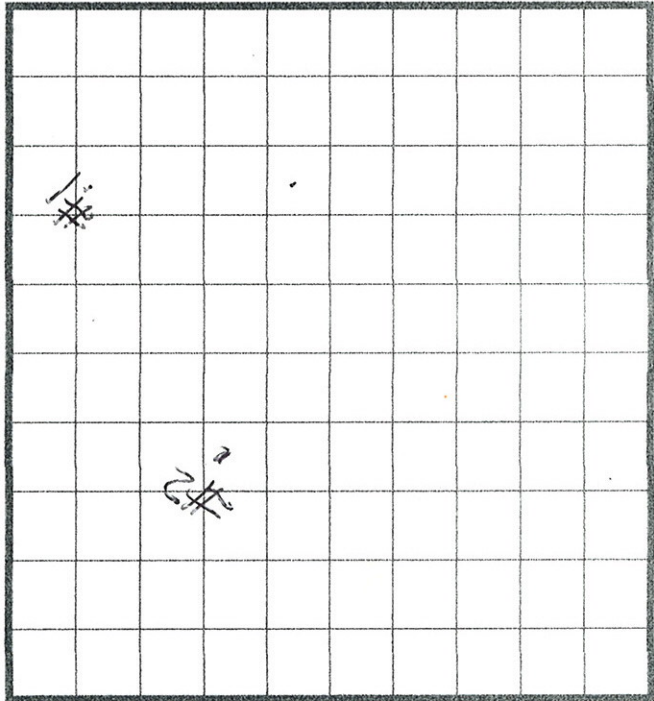

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
85	55	~	-	1	3

MEC	NOMENCLATURE	DEPTH
#1	Signal Illum. around	MEC 1
#2		

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-7-09	<i>[Signature]</i>	
Excavation Complete	5-7-09	<i>[Signature]</i>	
Quality Control Complete	5-7-09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
Grid No: C3G5A4 Size 100 x 100 ft
Date Started: 5-7-09
Date Completed: 5-7-09

Work Order No.
UXO Supervisor: L. Avachner
UXO Technician(s): Hendrick Loran
Remington

North
Direction

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
70	70	-	-	65	1

MEC	NOMENCLATURE	DEPTH
#1	Signal illum spread M125 (1)	

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-7-09		
Excavation Complete	5-7-09		* Brass in link pit
Quality Control Complete	5-7-09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C365F6 Size: 100 x 100 ft

Date Started: 5-7-09

Date Completed: 5-7-09


Work Order No.

UXO Supervisor: LAuchner

UXO Technician(s): Hendricks Labov

Remoto

North
Direction

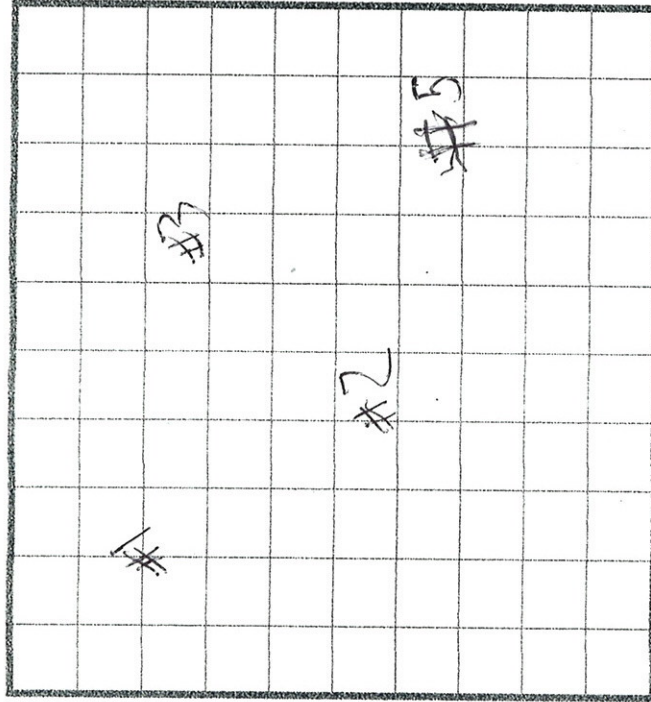

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
95	-	-	-	2	15

MEC	NOMENCLATURE	DEPTH
#1	Signal illum. exposure 0.125 (1)	
#2	" " " "	" "
#3	" " " "	" "
#4	" " " "	" "

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-7-09		
Excavation Complete	5/7/09		
Quality Control Complete	5/8/09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: E3 65B3 Size: 100 x 100 ft

Date Started: 5-7-09


Date Completed: 5-7-09

Work Order No:

UXO Supervisor: H. Aucher

UXO Technician(s): Hendrick Harris
Remendo

North Direction

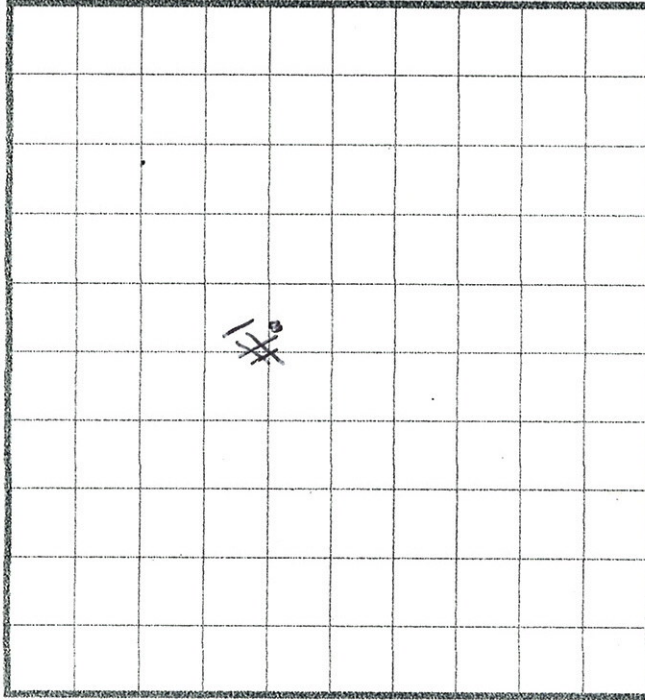

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
90	90	0	-	.5	1

MEC	NOMENCLATURE	DEPTH
#1	Signal from spade M25. (1)	

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-7-09	[Signature]	
Excavation Complete	5-7-09	[Signature]	
Quality Control Complete	5-7-09	[Signature]	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No C36565 Size 100 x 100 ft

Date Started: 5/6/09

Date Completed 5/6/09

Work Order No _____

UXO Supervisor Kristensen

UXO Technician(s) Caldwell

Paszataniec

North Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
30	10			1#	1#
<p style="text-align: center;">NOMENCLATURE</p> <p>(1) expanded MRS signal illuv ground 3"</p>					
				DEPTH	

Note: Gridlines spaced 10 x10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/6/09		
Excavation Complete	5/6/09		
Quality Control Complete	5/8/09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No C36564 Size 100 x 100 ft

Date Started: 5/6/09

Date Completed: 5/6/09


Work Order No. _____

UXO Supervisor Kristensen

UXO Technician(s) Caldwell

Pasztaakniec

North Direction _____

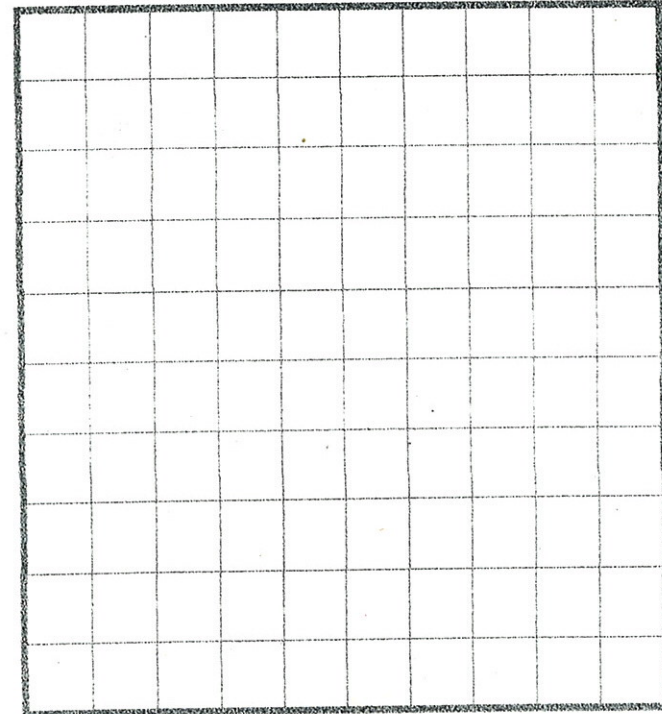

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
30	18			3#	1#

MEC	NOMENCLATURE	DEPTH
163ea	blank ammo	3"

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/6/09		
Excavation Complete	5/6/09		
Quality Control Complete	5/8/09		
Client Quality Assurance Complete			

Grid Sweep Log

Project Name: Fed Grid Remediation Program

Grid No. C395F1 Size 100 x 100 ft

Date Started 5-6-09

Date Completed 5-6-09

Work Order No. _____

UXO Supervisor T. Clark

UXO Technician(s) E. Gopalakes

B. Adams

North
Direction _____

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
200	175		0	2.0	8.5

MEG	NOMENCLATURE	DEPTH
MD	Sig. I/Ia grade MISS (2)	3"

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-6-09	<i>[Signature]</i>	
Excavation Complete	5-6-09	<i>[Signature]</i>	
Quality Control Complete	5-7-09	<i>[Signature]</i>	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name: Fort Ord Remediation Program

Grid No C39504 Size 100 x 100 ft

Date Started 5-6-09

Date Completed 5-6-09

Work Order No _____

UXO Supervisor T. Clark

UXO Technicians: B. Smith

F. Gonzalez, B. Adams

North
Direction

Total Anomalies	160	Total Excavations	158	Total MEC Items	0	Pounds MEC Scrap	0	Pounds Non-MEC Scrap	3.0
-----------------	-----	-------------------	-----	-----------------	---	------------------	---	----------------------	-----

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10' x 10' ft.

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-6-09	<i>[Signature]</i>	
Excavation Complete	5-6-09	<i>[Signature]</i>	
Quality Control Complete	5-7-09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: 0305B4 Size: 100 x 100 ft
 Date Started: 5-6-09
 Date Completed: 5-6-09

Work Order No.:
 UXO Supervisor: L. Buchner
 UXO Technician(s): Hendrix, Larson
Remington

North
 Direction

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
85	85			2	1

MEC	NOMENCLATURE	DEPTH
#1	Signal illum ground #1125 (C)	
#2	"	"
#3	"	"
#4	"	"

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-6-09		
Excavation Complete	5-6-09		
Quality Control Complete	5-7-09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C3F 439 Size: 100 x 100 ft
 Date Started: 5-6-09
 Date Completed: 5-6-09

Work Order No.:
 UXO Supervisor: L Avchner
 UXO Technician(s): Hendrick Resistor

North
Direction

#																			

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
105	105	-	-	5	1

MEC	NOMENCLATURE	DEPTH
#1	Signalillum ground (MUSLI)	

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-6-09	<i>[Signature]</i>	
Excavation Complete	5-6-09	<i>[Signature]</i>	
Quality Control Complete	5-7-09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C3 FHJ0 Size: 100 x 100 ft

Date Started: 5-6-09


Date Completed: 5-6-09

Work Order No. _____

UXO Supervisor: LAuchner

UXO Technician(s): Henricks Remington

North Direction _____

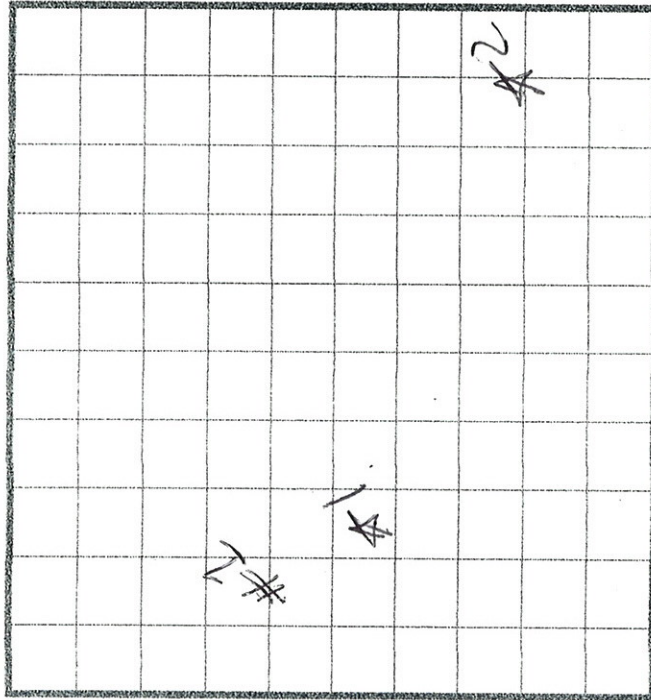

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
80	80	—	—	5	1

MEC	NOMENCLATURE	DEPTH
#1	Signal illum ground MRS (1)	

Note: Gridlines spaced 10 X 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-6-09	<i>[Signature]</i>	#1 Telephone pole, with concrete base
Excavation Complete	5-6-09 5-6-09	<i>[Signature]</i>	... and cable
Quality Control Complete	5-6-09	<i>[Signature]</i>	#1 Razor wire, over ground...
Client Quality Assurance Complete			Large Roll




Grid Sweep Log

Project Name/Fort Grid Remediation Program
 Grid No. C3G4G9 Size 100 x 100 ft
 Date Started 5-5-09
 Date Completed 5-5-09

Work Order No _____
 UXO Supervisor T. Clark
 UXO Technician(s) E. Gonzales
 B. Adams

North
 Direction

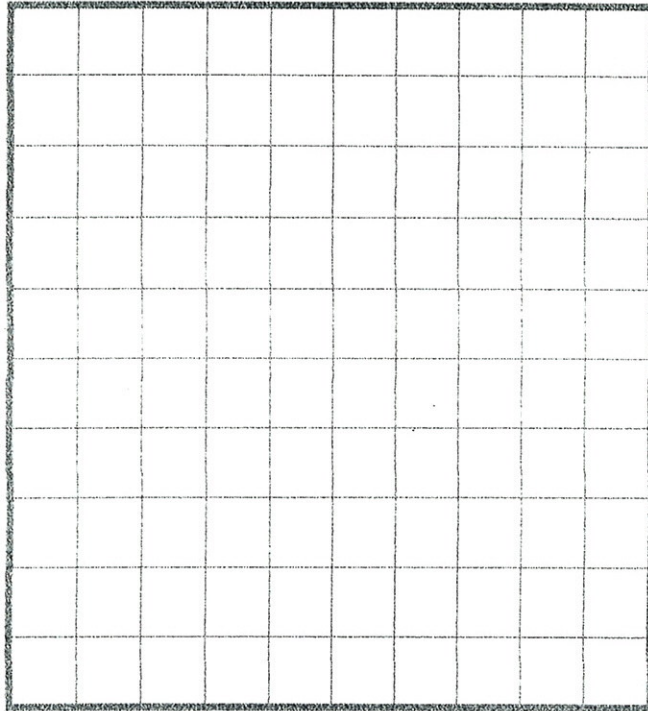

Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
160	140		0	1.0	8.5

MEC	NOMENCLATURE	DEPTH
MD	Sig Thin grade #125 (1)	3"
	DE # 389	

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-5-09	<i>[Signature]</i>	
Excavation Complete	5-5-09	<i>[Signature]</i>	
Quality Control Complete	5-5-09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No. C364C8 Size 100 x 100 ft
 Date Started 5-5-09
 Date Completed 5-5-09




Work Order No. _____
 UXO Supervisor T. Clark
 UXO Technician(s) E. Gourales
B. Adams

North
 Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
200	200		0	1.0	19.5

MEC-	NOMENCLATURE	DEPTH
MD	Gravelly Hard Pan M69 (1)	3"
	OE # 132	

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-5-09		
Excavation Complete	5-5-09		
Quality Control Complete	5-5-09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No. C36408 Size 100 x 100 ft
 Date Started 5-5-09
 Date Completed 5-5-09

Work Order No _____
 UXO Supervisor T. Clark
 UXO Technician(s) E. Gonzales
B. Adams

North
 Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
175	170		0	.5	12.5

MEC	NOMENCLATURE	DEPTH
MO	Sig Illuminant MILS (1) OE # 389	3"

Note: Gridlines spaced 10 X 10 ft

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-5-09	[Signature]	
Excavation Complete	5-5-09	[Signature]	
Quality Control Complete	5-5-09	[Signature]	
Client Quality Assurance Complete			

Project Name/Fort Ord Remediation Program

Grid No. C364E8 Size 100 x 100 ft

Date Started 5-5-09

Date Completed 5-5-09


Work Order No. _____

UXO Supervisor T. Clark

UXO Technician(s) I. Gonzales

B. Adams

North
Direction

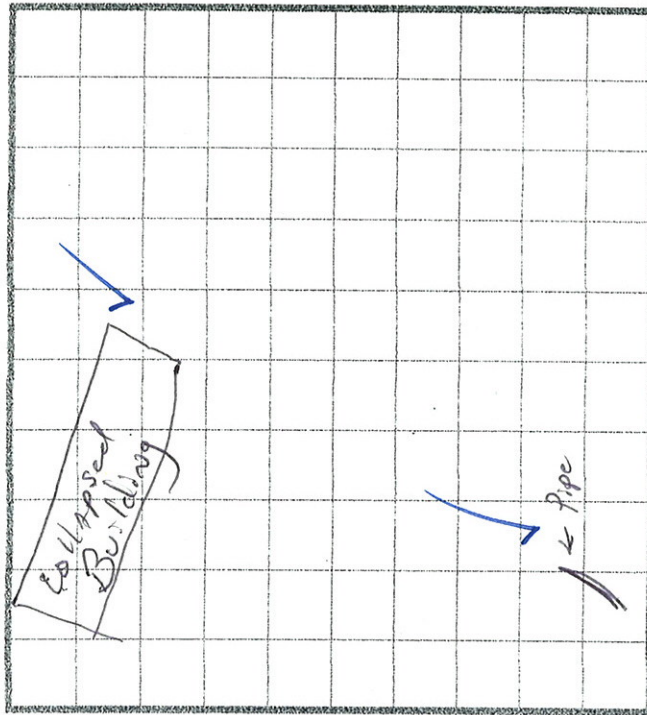

Note: Gridlines spaced 10x10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
150	140		0	0	50

MEC	NOMENCLATURE	DEPTH

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-5-09	[Signature]	
Excavation Complete	5-5-09	[Signature]	
Quality Control Complete	5-5-09	[Signature]	
Client Quality Assurance Complete			

Grid Sweep Log

Project Name/For Grid Remediation Program:

Grid No C365A5 Size 100 x 100 ft

Date Started 5/5/2009

Date Completed 5/5/2009

Work Order No

UXO Supervisor Kristensen

UXO Technician(s) Caldwell

Pasztebanics

North Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
30	15			2#	1#

NO	NOMENCLATURE	DEPTH
(1)	Expanded 162 General Panel OE # 135	3"
37 ea	UNFIRED .30 blank OE # 15	3"

Note Gridlines spaced 10' apart

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/5/09	<i>[Signature]</i>	
Excavation Complete	5/5/09	<i>[Signature]</i>	
Quality Control Complete	5-5-09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No.: C365 H6 Size: 100 x 100 ft
 Date Started: 5/5/2009
 Date Completed: 5/5/2009

Work Order No.:
 UXO Supervisor: Kristensen
 UXO Technician(s): Caldwell
 Paszalanice

North
Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
30	10				1 #

MEC	NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5/5/09		
Excavation Complete	5/5/09		
Quality Control Complete	5-5-09		
Client Quality Assurance Complete			




Grid Sweep Log

Project Name/Fort Ord Remediation Program
 Grid No C36567 Size: 100 x 100 ft
 Date Started 5/5/09
 Date Completed 5/5/09

Work Order No _____
 UXO Supervisor Kristensen
 UXO Technician(s) Caldwell Paszalaniec

North Direction

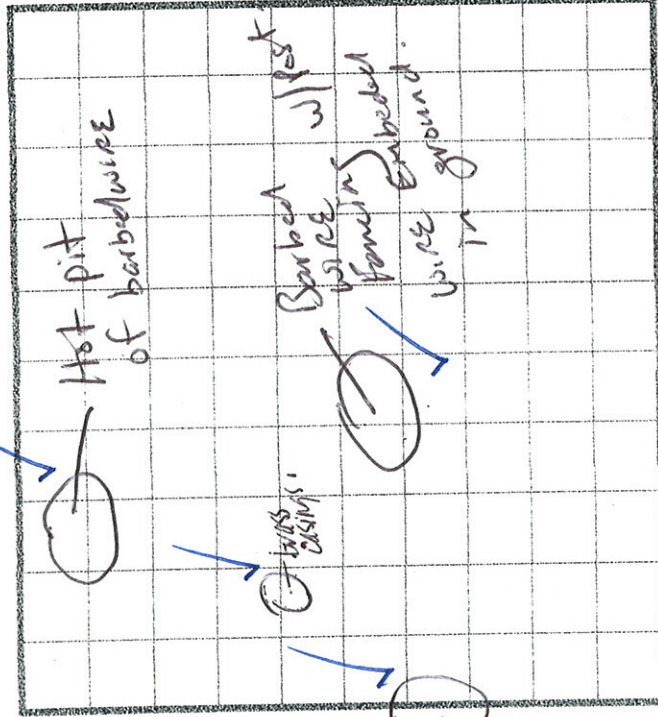

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
120	60			1#	18#

MEC	NOMENCLATURE	DEPTH
(1)	M125 signal ground illum OE# 389	3"

Note: Gridlines spaced 10 x 10 ft

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5/5/09	[Signature]	
Excavation Complete	5/5/09	[Signature]	
Quality Control Complete	5/8/09	[Signature]	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No: C364 A9 Size 100 x 100 ft

Date Started 5-5-09

Date Completed 5-5-09

Work Order No _____

UXO Supervisor Crutcher

UXO Technician(s) Hendrix Remington

North
Direction

#1									

5v Note: Gridlines spaced 10 x 10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
95	95	-	1	5	48

MEC	NOMENCLATURE	DEPTH
#1	Signal illum ground miss (1)	GE# 389

ACTION	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-5-09	<i>[Signature]</i>	
Excavation Complete	5-5-09	<i>[Signature]</i>	
Quality Control Complete	5-5-09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No. C365A1 Size 100 x 100 ft

Date Started 5-5-09

Date Completed 5-5-09

Work Order No

UXO Supervisor L Aucher

UXO Technician(s) Hendrix Remington

North Direction

Total Anomalies	Total Excavations	Anomalies > <u> </u> ft	Total MEC items	Pounds MEC Scrap	Pounds Non-MEC Scrap
110	110	1	1	4	3

MEC	NOMENCLATURE	DEPTH
#1	Small anomaly Blank (3lbs)	OE # 10
#2	Signal illum ground (12.50)	OE # 389

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-5-09	<i>[Signature]</i>	
Excavation Complete	5-5-09	<i>[Signature]</i>	
Quality Control Complete	5-5-09	<i>[Signature]</i>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Font Grid Remediation Program

Grid No. C365A2 Size 100 x 100 ft

Date Started 5-5-09

Date Completed 5-5-09

Work Order No. _____

UXO Supervisor L. Avekner

UXO Technician(s) Henrick Remington

North Direction

Total Anomalies	Total Excavations	Anomalies > _____ ft	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
105	105	1	1	15	2.5

MEC	NOMENCLATURE	DEPTH
#1	Signal wire ground - (M550)	
	OE # 389	

Note: Gridlines spaced 10 x 10 ft

ACTION:	DATE	SIGNATURE	REMARKS
Mag Sweep Complete	5-5-09		
Excavation Complete	5-5-09		
Quality Control Complete	5-7-09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C362148 Size: 100 x 100 ft

Date Started: 5-12-09

Date Completed: 5-12-09


Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): D. Caldwell

J. Remington

North Direction

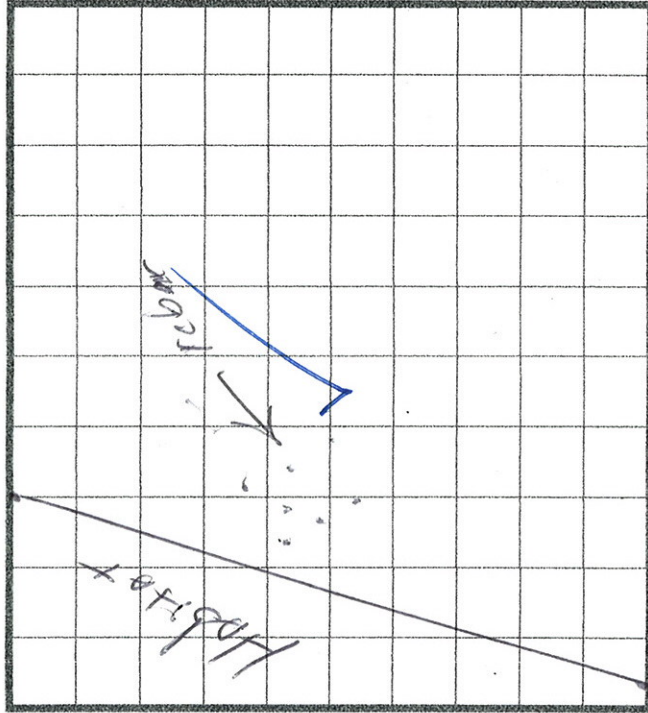

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > _____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non-MEC Scrap
70	69		0	0	8.5

NOMENCLATURE

DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-12-09		
Excavation Complete	5-12-09		
Quality Control Complete	5-15-09		
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program


Grid No.: C3G2H9 Size: 100 X 100 ft

Date Started: 5-12-09

Date Completed: 5-12-09

Work Order No. _____
 UXO Supervisor: T. Clark
 UXO Technician(s): D. Caldwell
J. Remington

North
 Direction

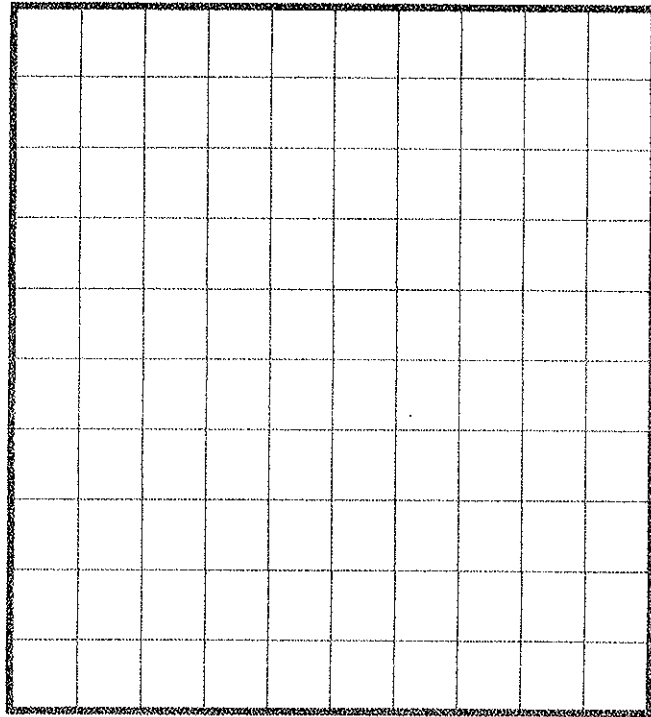

Total Anomalies	Total Excavations	Anomalies > ___ ft.	Total MEC items	Pounds MEC Scrap	Pounds Non- MEC Scrap
75	75		0	0	75

NOMENCLATURE	DEPTH

Note: Gridlines spaced 10 x10 ft

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-12-09	<u>[Signature]</u>	
Excavation Complete	5-12-09	<u>[Signature]</u>	
Quality Control Complete	5-15-09	<u>[Signature]</u>	
Client Quality Assurance Complete			



Grid Sweep Log

Project Name/Fort Ord Remediation Program

Grid No.: C3G 3H1 Size: 100 x 100 ft

Date Started: 5-12-09

Date Completed: 5-12-09

Work Order No.:

UXO Supervisor: T. Clark

UXO Technician(s): D. Caldwell

J. Remington

North
Direction

Note: Gridlines spaced 10 x10 ft

Total Anomalies	Total Excavations	Anomalies > ____ ft.	Total MEC Items	Pounds MEC Scrap	Pounds Non- MEC Scrap
50	30		0	0	5.0

NOMENCLATURE	DEPTH

ACTION:	DATE	SIGNATURE	REMARKS:
Mag Sweep Complete	5-12-09		
Excavation Complete	5-12-09		
Quality Control Complete	5-15-09		
Client Quality Assurance Complete			
