# Fort Ord MR BCT Ahtna Status, Contract No. W9123824D003 May 9, 2025

## 1. Document Development – Task Order 1

### MEC QAPP Addendum

Version	Task Description	Dates
Draft	Delivered to Agencies and Public	March 7, 2025
Draft	Comments Received from Agencies and Public	April 10, 2025 – EPA
		No Comments - DTSC
		April 4, 2025 - FOCAG
		April 8, 2025 – Nina Beety
Draft Final	Scheduled for Delivery	May 8, 2025
Draft Final	Comments Requested by	June 9, 2025
Final	Scheduled for Delivery	July 9, 2025

## Unit 17 Site Specific Work Plan

Version	Task Description	Dates
Draft	Delivered to Agencies and Public	March 7, 2025
Draft	Comments Received	April 10, 2025 – EPA
		April 8, 2025 – DTSC
		April 4, 2025 – FOCAG
		April 8, 2025 - Nina Beety
Draft Final	Scheduled for Delivery	May 8, 2025
Draft Final	Comments Requested by	June 9, 2025
Final	Scheduled for Delivery	July 9, 2025

## Unit A Site Specific Work Plan Addendum

Version	Task Description	Dates
Draft	Delivered to Agencies and Public	March 31, 2025
Draft	Comments Requested by	April 30, 2025
Draft	Comments Received	April 29, 2025 – EPA
		May 1, 2025 – DTSC
		April 29, 2025 – FOCAG
		April 30, 2025 - Nina Beety
Draft Final	Scheduled for Delivery	May 30, 2025
Draft Final	Comments Requested by	June 30, 2025
Final	Scheduled for Delivery	July 30, 2025

#### Unit A Prescribed Burn Plan

Version	Task Description	Dates
Preliminary Draft	Meeting with POMFD, Naval Post Graduate School, Monterey Bay Air Resources District, and Burn Bosses to support burn plan development	February 28, 2025
Preliminary Draft	Meeting and Site Visit with Presidio of Monterey Fire Department and Burn Bosses to support burn plan development	April 1, 2025

## Fort Ord MR BCT Ahtna Status, Contract No. W9123824D003 May 9, 2025


Preliminary Draft	BRAC/USACE Accepted Revisions	April 28, 2025
Draft	Delivered to Agencies and Public	April 30, 2025
Draft	Comments Requested By	May 30, 2025
Draft Final	Scheduled for Delivery	June 29, 2025
Draft Final	Comments Requested by	July 29, 2025
Final	Schedule for Delivery	August 29, 2025

### 2. Unit A MEC Remedial Actions – Task Order 3

Task Order 3 Awarded on February 28, 2025

Unit A Field Work Tasks Scheduled June – July 2025

- Biological Support
- Vegetation Cutting in Containment Lines
- Prescribed Burn Preparation

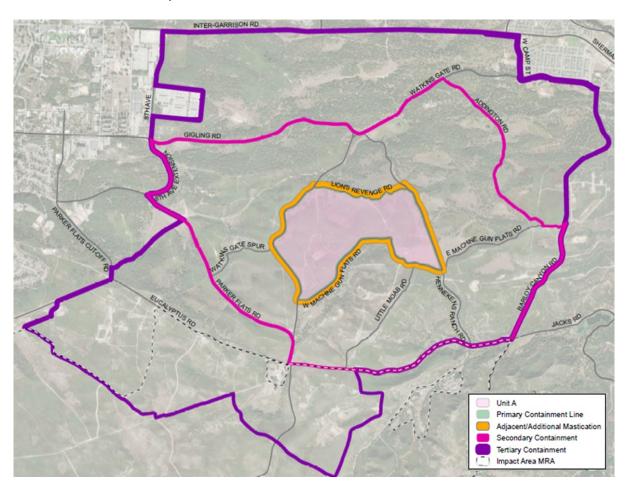

# Fort Ord MR BCT Ahtna Status, Contract No. W9123824D003 May 9, 2025

## 3. Unit 17 MEC Remedial Actions – Task Orders 2 and 3

Unit 17 Field Work Tasks Scheduled to Begin in July 2025

- Biological Support
- Vegetation Cutting
- Grid and Stake Work Area
- Technology-Aided Surface MEC Removal

