

Fort Ord MR BCT
Ahtna Status,
Contract No. W9123824D003
July 25, 2025

1. Document Development – Task Order 1

MEC QAPP Addendum

Version	Task Description	Dates
Draft Final	Delivered	May 9, 2025
Draft Final	Comments or Letters Indicating No Further Comments (NFC) - Received	June 9, 2025 – FOCAG Comments June 10, 2025 – DTSC NFC June 25, 2025 – EPA NFC
Final	Scheduled for Delivery	July 2025

Unit 17 Site Specific Work Plan

Version	Task Description	Dates
Draft Final	Delivered	May 9, 2025
Draft Final	Comments or Letters Indicating No Further Comments (NFC) - Received	June 10, 2025 – DTSC NFC June 25, 2025 – EPA NFC June 9, 2025 – FOCAG Comments
Final	Scheduled for Delivery	July 2025

Unit A Site Specific Work Plan Addendum

Version	Task Description	Dates
Draft Final	Delivered	May 30, 2025
Draft Final	Comments or Letters Indicating No Further Comments (NFC) - Received	June 25, 2025 – EPA NFC June 26, 2025 – DTSC NFC June 30, 2025 – FOCAG Comments
Final	Scheduled for Delivery	August 2025

Unit A Prescribed Burn Plan

Version	Task Description	Dates
Draft	Comments	May 30, 2025 – MBARD May 30, 2025 - FOCAG June 2, 2025 – EPA June 2, 2025 - DTSC
Draft Final	Scheduled for Delivery	July 2025
Draft Final	Comments Requested by	August 2025
Final	Schedule for Delivery	September 2025

2. Unit A MEC Remedial Actions – Task Order 3


Task Order 3 Awarded on February 28, 2025

Unit A Field Work Tasks June – August 2025

- Biological Support

July 25, 2025

- Vegetation Cutting in Containment Lines – In Progress
- Prescribed Burn Preparation - Ongoing

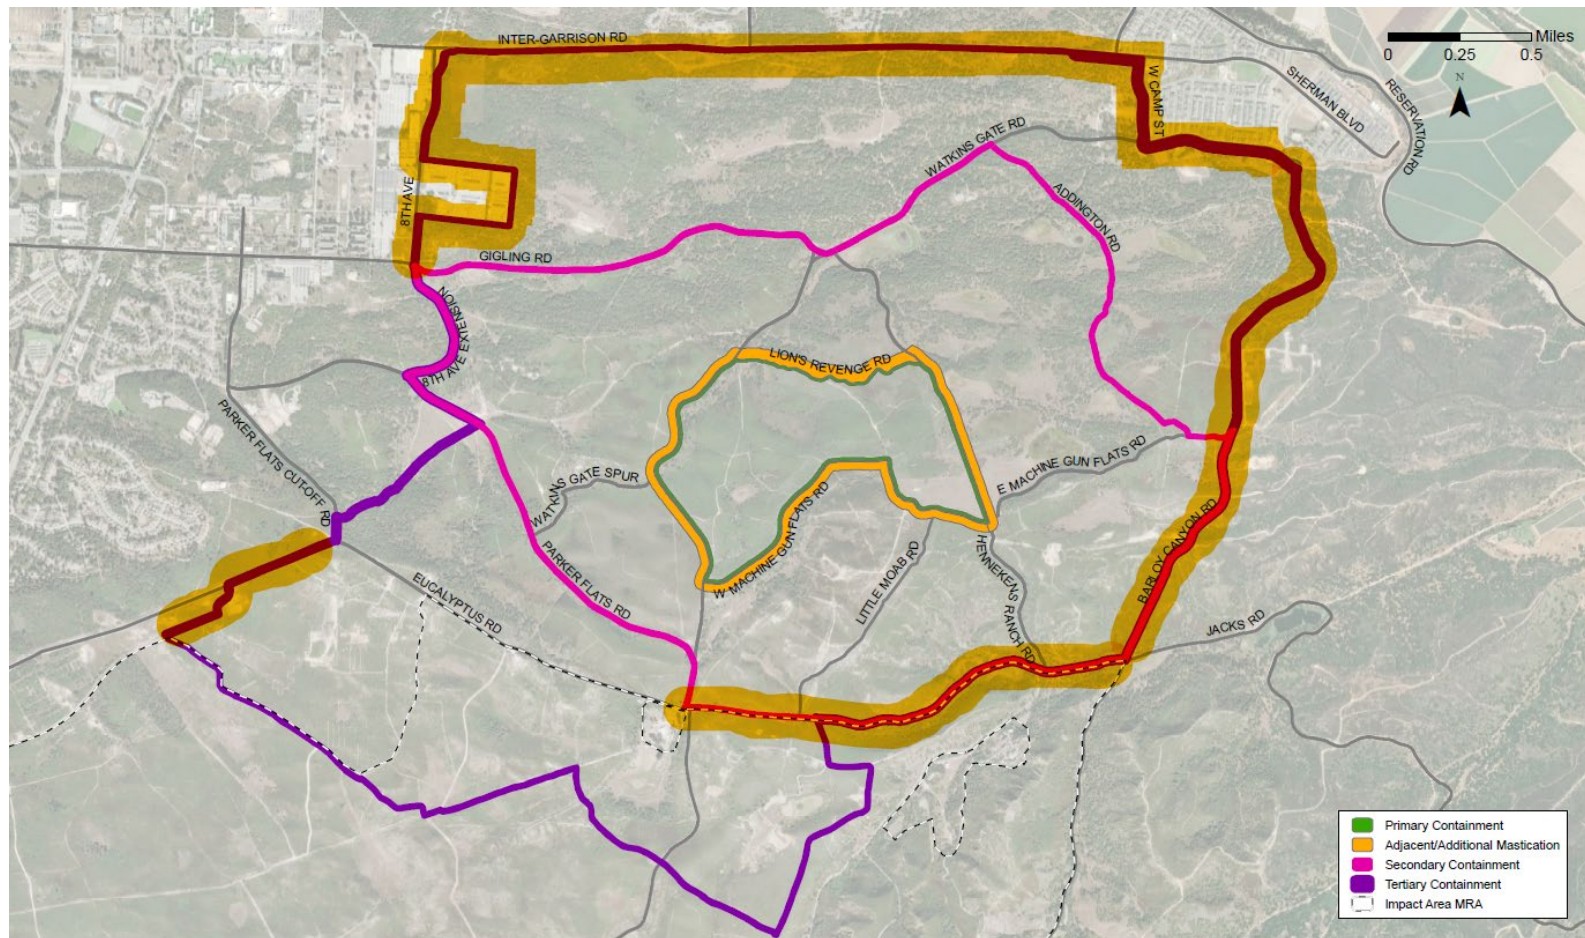

Fort Ord MR BCT
Ahtna Status,
Contract No. W9123824D003
July 25, 2025



3. Unit 17 MEC Remedial Actions – Task Orders 2 and 3

Unit 17 Field Work Tasks Scheduled to begin end of July 2025 or early August 2025

- Biological Support
- Vegetation Cutting
- Grid and Stake Work Area
- Technology-Aided Surface MEC Removal

