



# BRA and Lead Evaluation Status Fort Ord HTW BCT 14 March 2019

### **Basewide Range Assessment**

- KEMRON is resolving Army comments on the draft final sampling report for Units 1, 2, 3, 7, 10, 33, and WGBA.
- KEMRON submitted the draft final sampling results report for Units 25 and 28. DTSC has no additional comments. FOCAG comments received and RTCs are in progress.
- KEMRON is resolving comments on the HAs addressed under the current contract for the update to the Comprehensive BRA Report.
- KEMRON conducted a site reconnaissance in BLM Area B accessible areas in January and has prepared a description of the findings.

## **Lead Evaluation Sites**

• KEMRON plans to meet with DTSC to discuss the cleanup level for the ESD.

## **Site 39 Erosion Control**

- KEMRON is monitoring Site 39 areas throughout the Impact Area MRA for erosion issues.
- KEMRON is addressing maintenance issues at erosion control sites.

# **Building Demolition Project**

Please see attached table, figures, and pictures from the building demolition project.

# KEMRON Range Structure Removal Schedule March 1st, 2019 19 of 33 Structures Demolished


	ID	Structure	Burn Unit	Comp	ACM	Structure Status
IMPACT AREA	1	Latrine	1	Wood	confirmed	
	2	Latrine	1	Wood		Demolition completed/site restored. Debris is staged at the Iron Triangle
	3	Canopy	1	Wood		Demolition completed/site restored. Debris is staged at the Iron Triangle
	4	Latrine	4	Wood		Demolition completed/site restored. Debris is staged at the Iron Triangle
	5	Range House	4	Block	confirmed	
	6	Range House	4	Block		Demolition completed/site restored. Debris is staged at the Iron Triangle
	7*	Observation Deck	5	Wood		Demolition completed/site restored. Debris is staged at the Iron Triangle
	8	Observation Tower	6	Wood		Demolition completed/site restored. Debris is staged at the Iron Triangle
	9	Latrine	6	Wood	confirmed	
	10	Canopy	6	Steel		Structure removed and placed in A&S Metals salvage container
	11	Canopy	6	Wood		Demolition completed/site restored. Debris is staged at the Iron Triangle
	12	Canopy	9	Steel		Structure removed and placed in A&S Metals salvage container
	13	Latrine R9322	13	Wood		Demolition completed/site restored. Debris is staged at the Iron Triangle
	14	Latrine R9320	13	Wood		Demolition completed/site restored. Debris is staged at the Iron Triangle
	15	Observation Tower	18	Wood		
	16*	Unknown Box	21	Wood		
	17	Training Building	21	Wood	confirmed	On deck
	18	Observation Tower	21	Wood	confirmed	On deck
	19	Observation Tower	21	Wood	confirmed	
	20	Observation Tower R9386	34	Wood		
	21	Observation Tower	34	Wood	confirmed	
	22	Latrine R9382	21	Wood		
	23	Latrine R9381	34	Wood	confirmed	
		Latrine R9380	34	Wood		
		Canopy	34	Wood		
		Canopy	5A	Metal		Structure removed and placed in A&S Metals salvage container
	27		5A	Wood	confirmed	Mastic with ACM was cut out and left for Abatement contractor - structure removed to the Iron Triangle
	28*	Latrine (AD exempt)	5A	Wood		Demolition completed/site restored. Debris is staged at the Iron Triangle
		Range House	5A	Block		Demolition completed/site restored. Debris is staged at the Iron Triangle
BLM Area B		Latrine	B3W	Wood		Demolition completed/site restored and debris stockpiled at the OU2 landfill Area E - ready for placement
		Latrine	B3W	Wood		Demolition completed/site restored and debris stockpiled at the OU2 landfill Area E - ready for placement
	32	1 5	B3W	Wood		Demolition completed/site restored and debris stockpiled at the OU2 landfill Area E - ready for placement
	33	Concrete Pad	B3W	Concrete		Concrete removed and used as fill in Item 31 latrine pit.

BLM has requested demolition of these structures to facilitate future management of the Units noted; these structures are in burn or cut units where MEC cleanup has occurred and no habitat burn is required as part of the CERCLA remedy but future prescribed burns by BLM may be accomplished, DGM mapping has not been accomplished below the footprint of these structures.

\* Indicates an item designated as 'not regulated' by MBARD

Confirmed for the presence of Asbestos Construction Material

Structure Demolition and removal complete

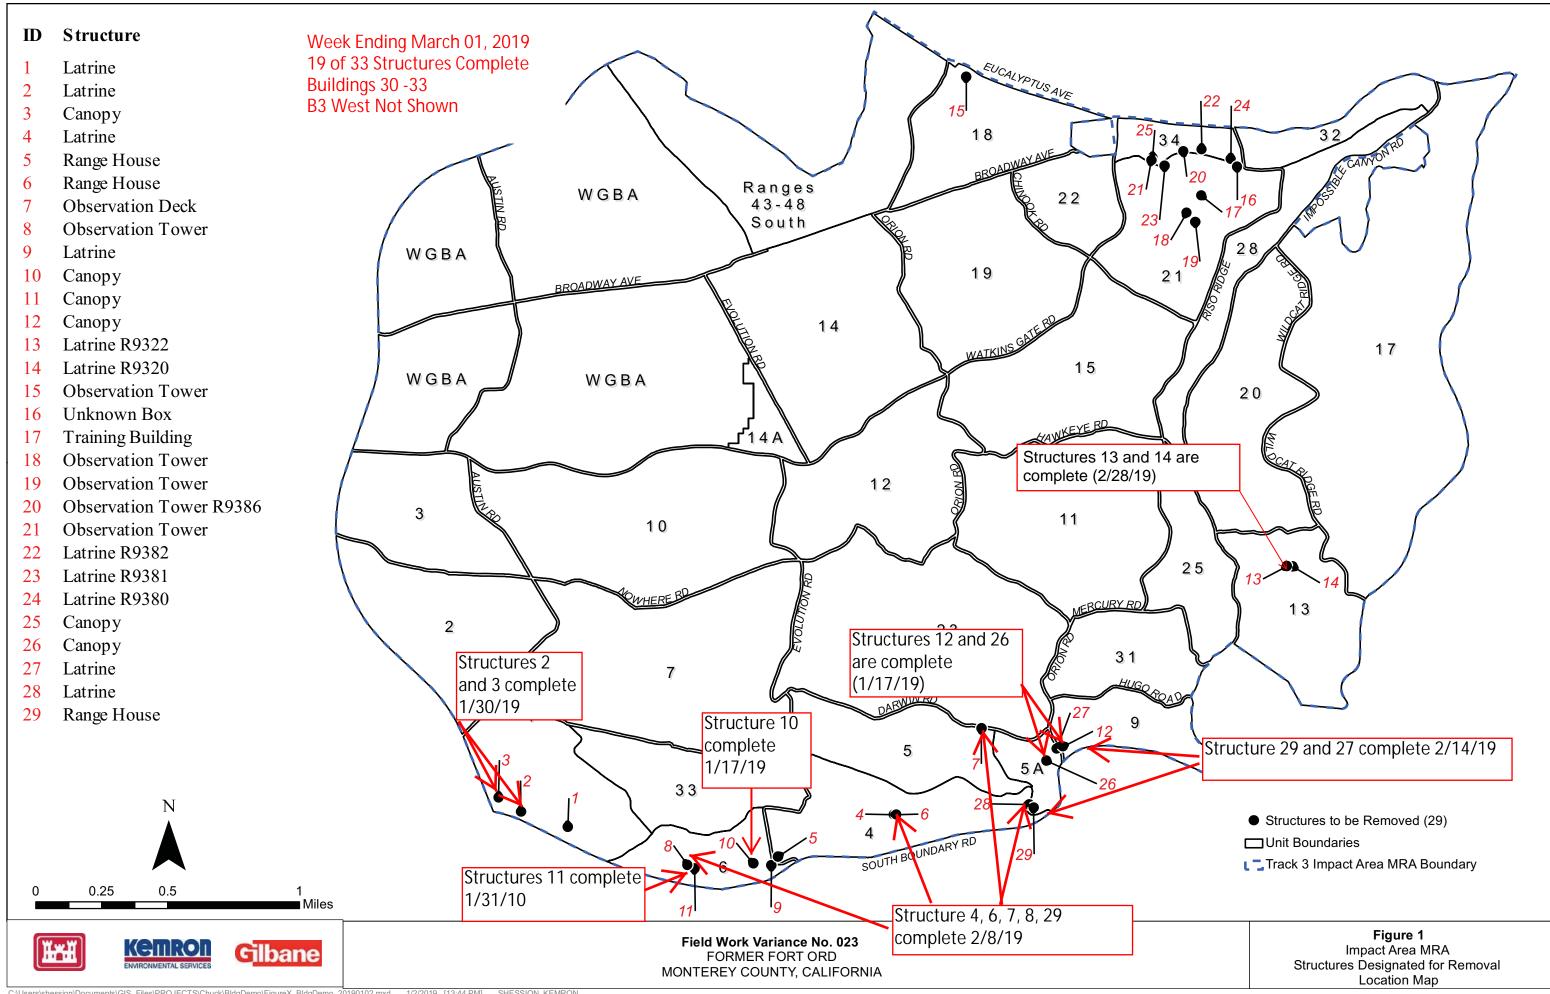





- A) Workers spent several days gaining entrance to the structures in Unit 13 by clearing the old access road.
- B) Construction workers slid the latrine to a location where it was easier to demo.





