

Fort Ord MR BCT
Ahtna Status
Contract No. W9123824D003

September 18, 2025

Document Development – Task Order 1

- MEC QAPP Addendum

Version	Task Description	Dates
Final	Delivered	July 31, 2025

- Unit 17 Site Specific Work Plan

Version	Task Description	Dates
Final	Delivered	July 31, 2025

- Unit A Site Specific Work Plan Addendum


Version	Task Description	Dates
Final	Delivered	August 29, 2025

- Unit A Prescribed Burn Plan

Version	Task Description	Dates
Draft Final	Delivered	August 7, 2025
Draft Final	Comments or Letters Indicating No Further Comments (NFC) - Received	September 8, 2025 – FOCAG Comments September 5, 2025 – EPA NFC September 5, 2025 – DTSC NFC
Final	Schedule for Delivery	TBD

Unit A MEC Remedial Actions – Task Order 3

- Unit A Prescribed Burn Prep
 - Vegetation Cutting in Containment Lines
 - Mechanical and Manual Cutting Complete – ~275 Acres
 - Exceptions include:
 - Limbing of canopy areas - Primary/Adjacent and Secondary Lines
 - Chipping - Secondary/ Tertiary
 - Habitat Management Plan Grids – seaside bird’s beak
 - POMFD Approvals Pending

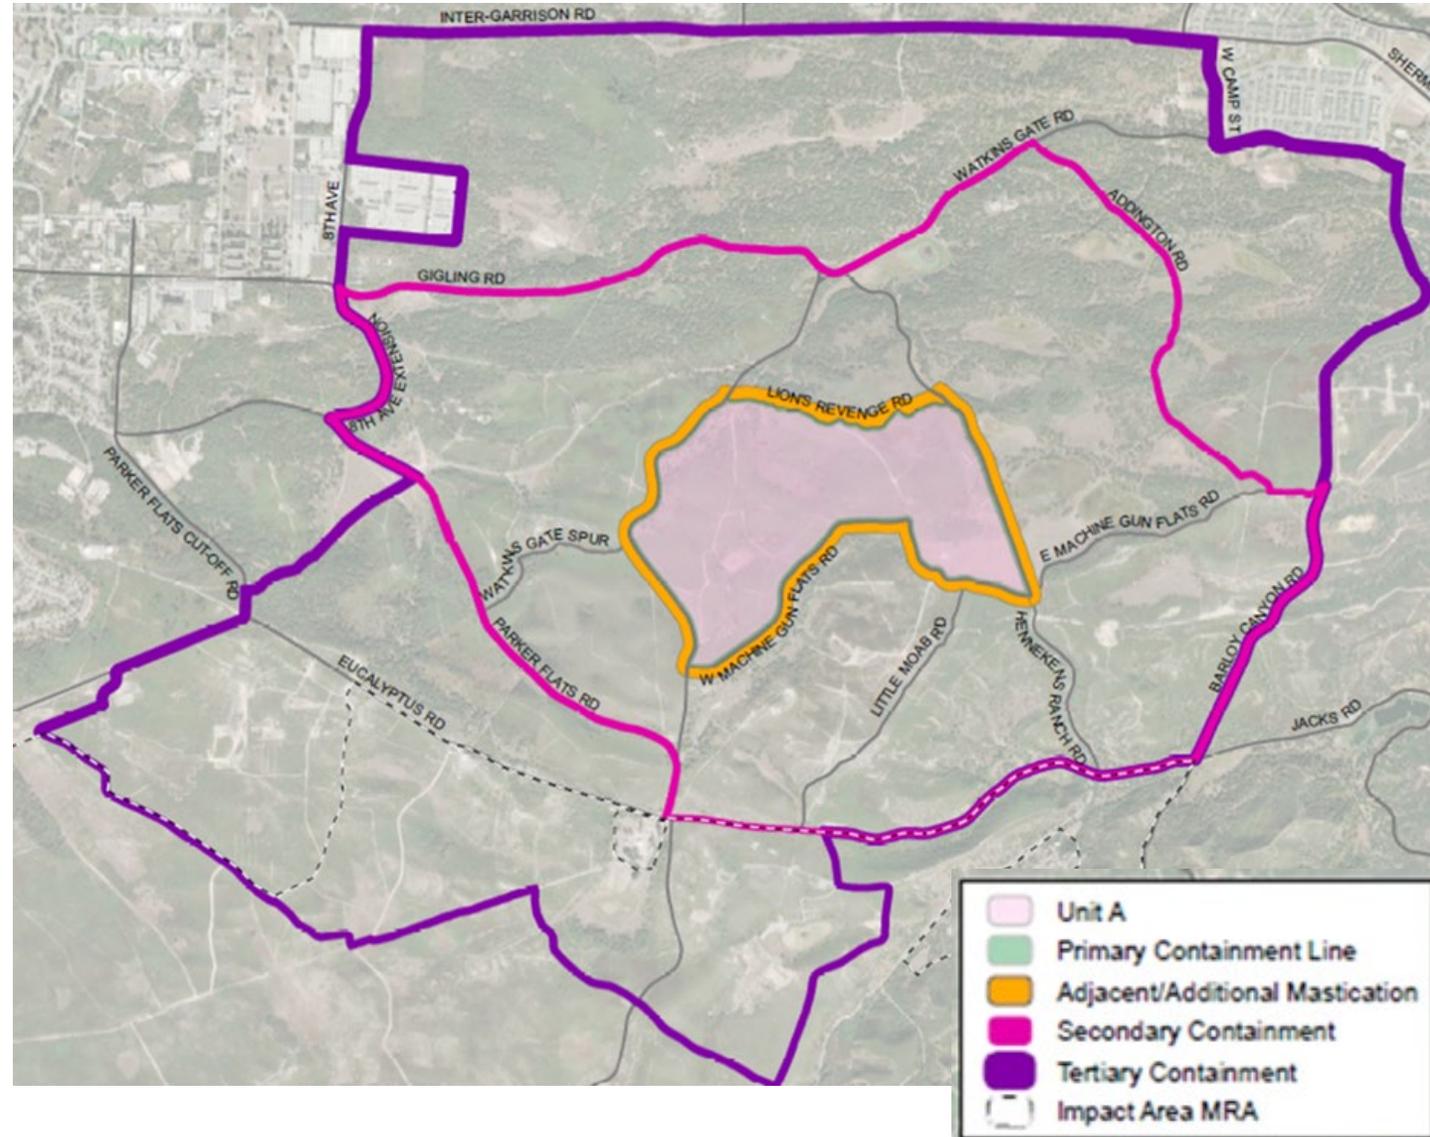

Unit A MEC Remedial Actions – Task Order 3

- Unit A Prescribed Burn Prep
 - Vegetation Cutting in Containment Lines



Unit A MEC Remedial Actions – Task Order 3

- Unit A Prescribed Burn Prep - Continued
 - Water Supply
 - Two Old Dip Tanks - Removed
 - Four New Dip Tanks - Deployed
 - Water Towers - Deployed




Unit A MEC Remedial Actions – Task Order 3

- Unit A Prescribed Burn Prep - Continued
 - Water Supply
 - Water Storage Tanks – Deployed and Filled
 - Plumbing of Water Storage Tanks to Dip Tanks - Built, Testing in Progress



Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations –
 - Boundary Survey – Started August 4, 2025
 - Vegetation Cutting - two cuts
 - Mechanical – Started August 4, 2025
 - ~ 24 acres completed to date
 - ~ 44 acres projected
 - Manual – Started September 16, 2025
 - ~ 16-20 acres projected
 - Grid Corner Staking - Started September 16, 2025
 - Instrument Aided Surface MEC Removal - anticipated to start Early October.

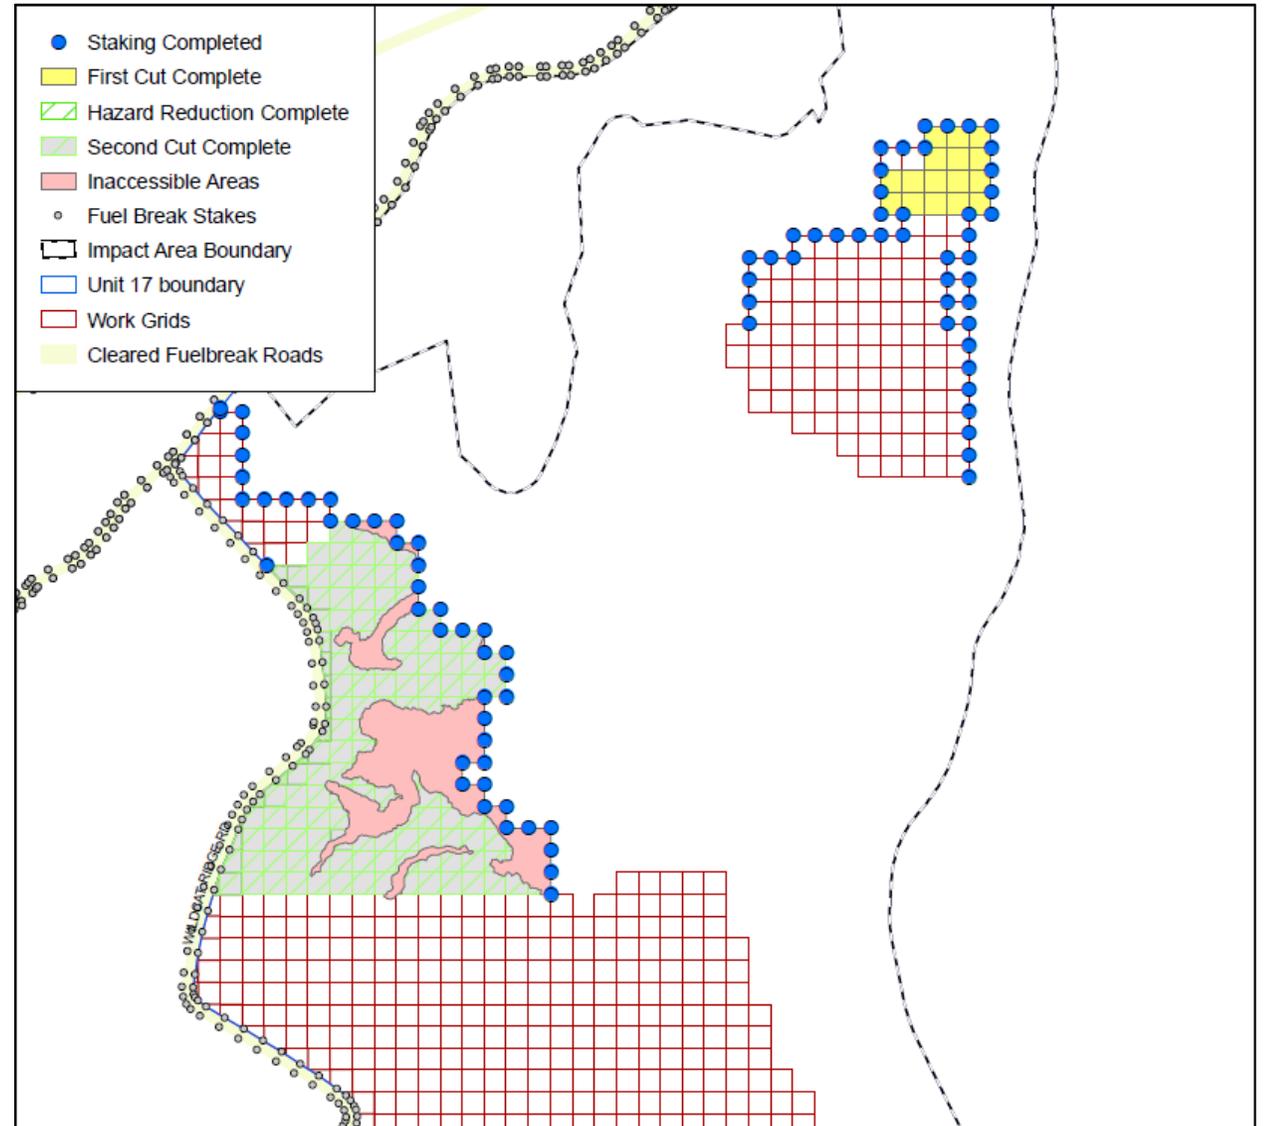

Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations –
 - Mechanical Vegetation Cutting
 - Second Cut Complete

