

Fort Ord MR BCT  
Ahtna Status  
Contract No. W9123824D003

December 11, 2025

# Document Development – Task Order 1

- Unit A Site-Specific Work Plan Addendum – Additional Comments


<b>Version</b>	<b>Task Description</b>	<b>Dates</b>
Final	Delivered	August 29, 2025
	Respond to Comments from public member on Final Site-Specific Work Plan	December 8, 2025


- Unit A Prescribed Burn Plan

<b>Version</b>	<b>Task Description</b>	<b>Dates</b>
Draft Final	Delivered	August 7, 2025
Final	Schedule for Delivery	TBD

# Unit A MEC Remedial Actions – Task Order 3

- Unit A Prescribed Burn Prep
  - Vegetation Cutting in Containment Lines
    - Mechanical and Manual Cutting Complete – ~275 Acres
    - POMFD Approvals Complete
  - Water Supply Set Up Complete
  - Air Sensors Deployed
  - Suppression Helibase Perimeter Fence Complete

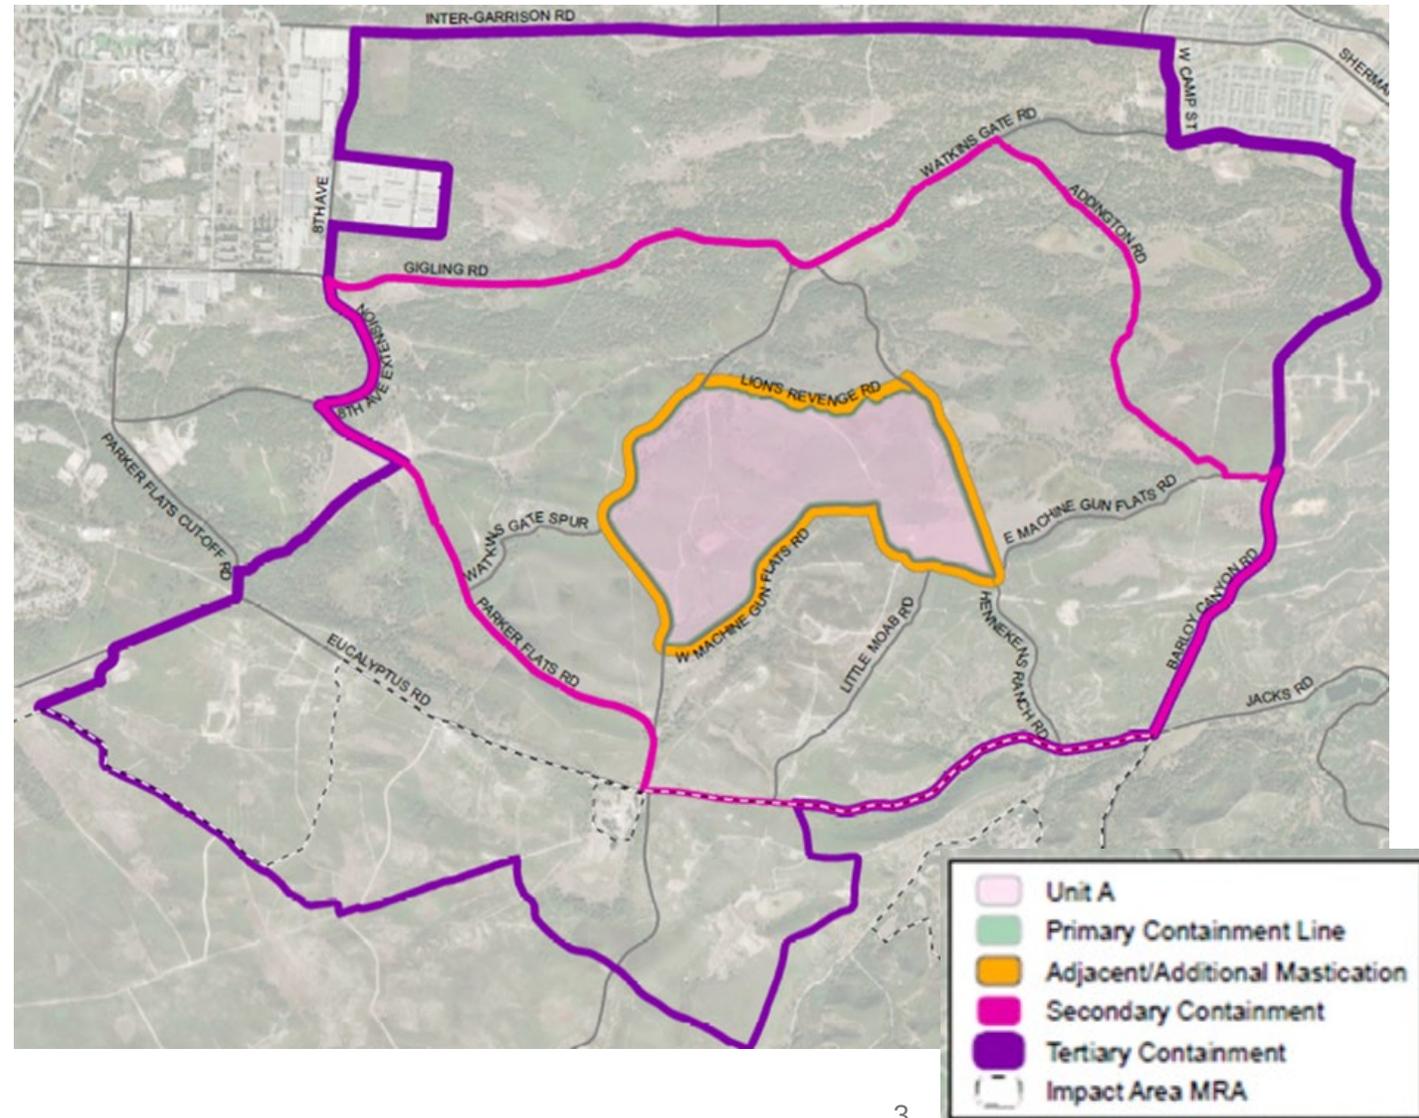

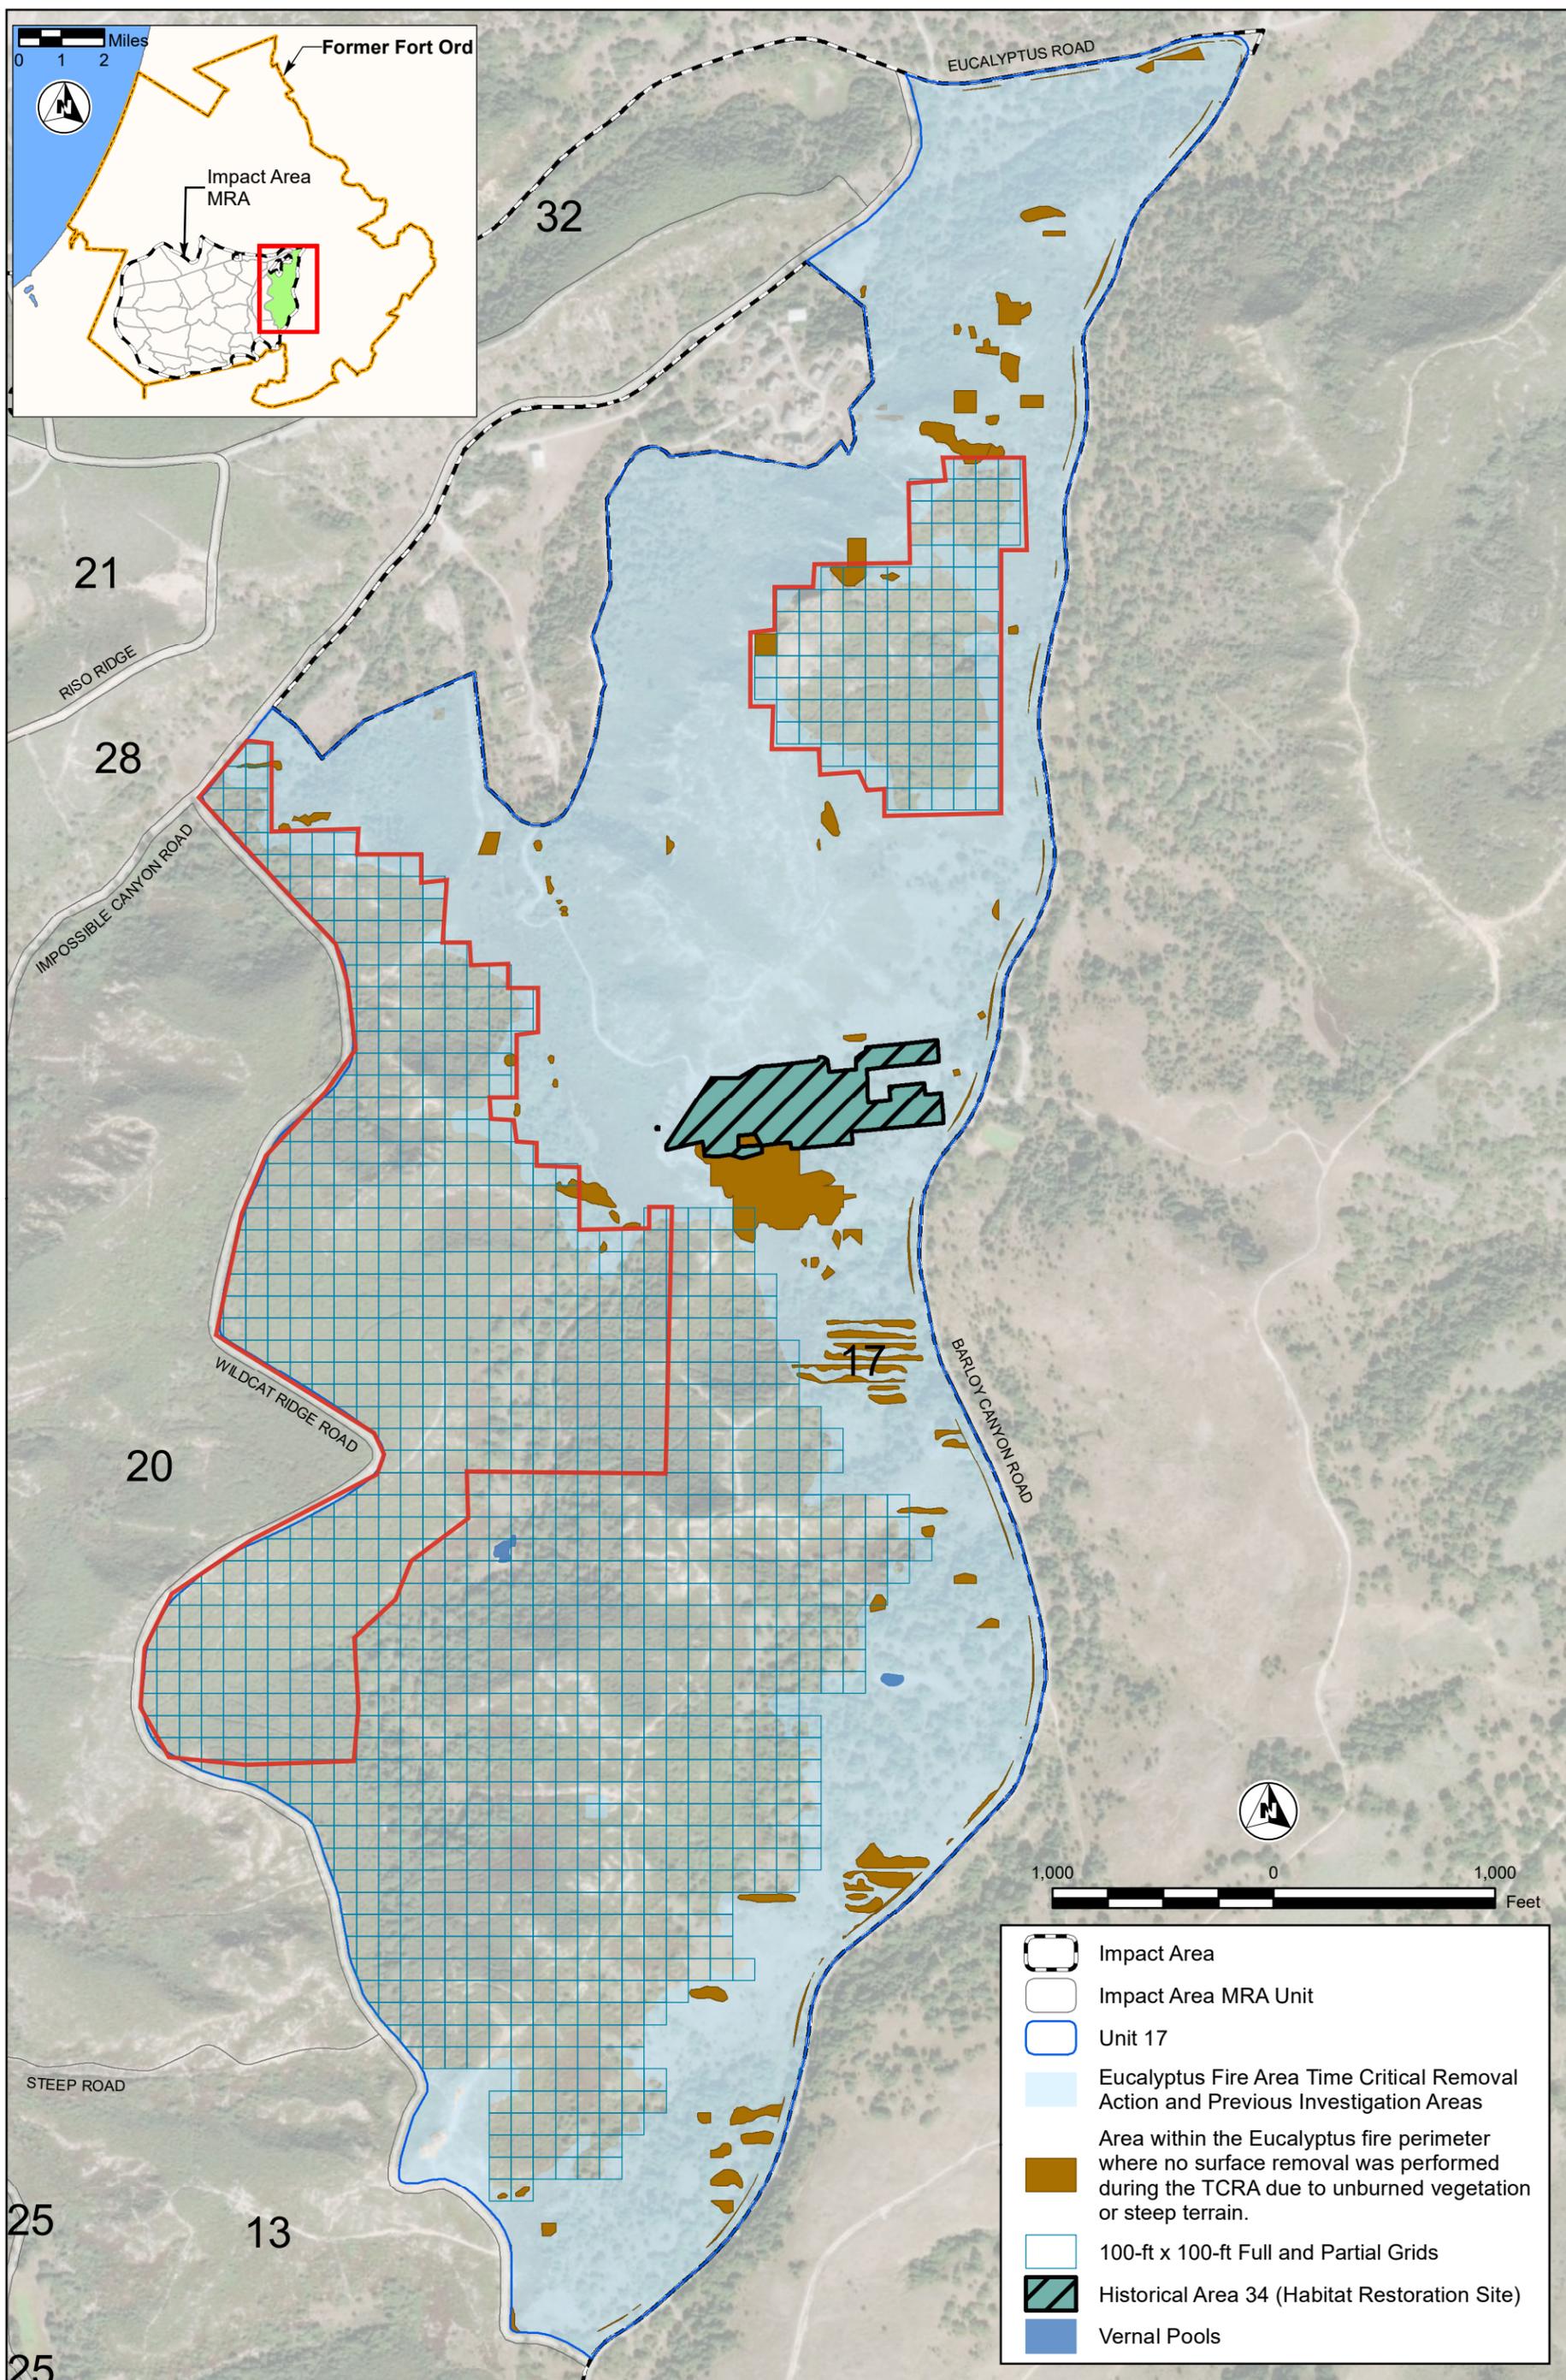

- Impact Area
- Impact Area MRA Unit
- Unit 17
- Eucalyptus Fire Area Time Critical Removal Action and Previous Investigation Areas
- Area within the Eucalyptus fire perimeter where no surface removal was performed during the TCRA due to unburned vegetation or steep terrain.
- 100-ft x 100-ft Full and Partial Grids
- Historical Area 34 (Habitat Restoration Site)
- Vernal Pools

*Ahtna*


Site Specific Work Plan  
 Munitions and Explosives of Concern Remedial Action  
 MRS-BLM Unit 17  
 Former Fort Ord, California

**Figure 4**  
 Unit 17 Planned MEC Remedial  
 Action Area

# Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations –
  - Boundary Survey – Started August 4, 2025
  - Grid Corner Staking - Started September 16, 2025
  - Vegetation Cutting - Double cut
    - Mechanical – Started August 4, 2025
      - ~ 92 acres completed to date
      - ~ 116 acres projected
    - Manual – Started September 16, 2025
      - ~ 65 acres projected
  - Erosion Control
  - Biological Support



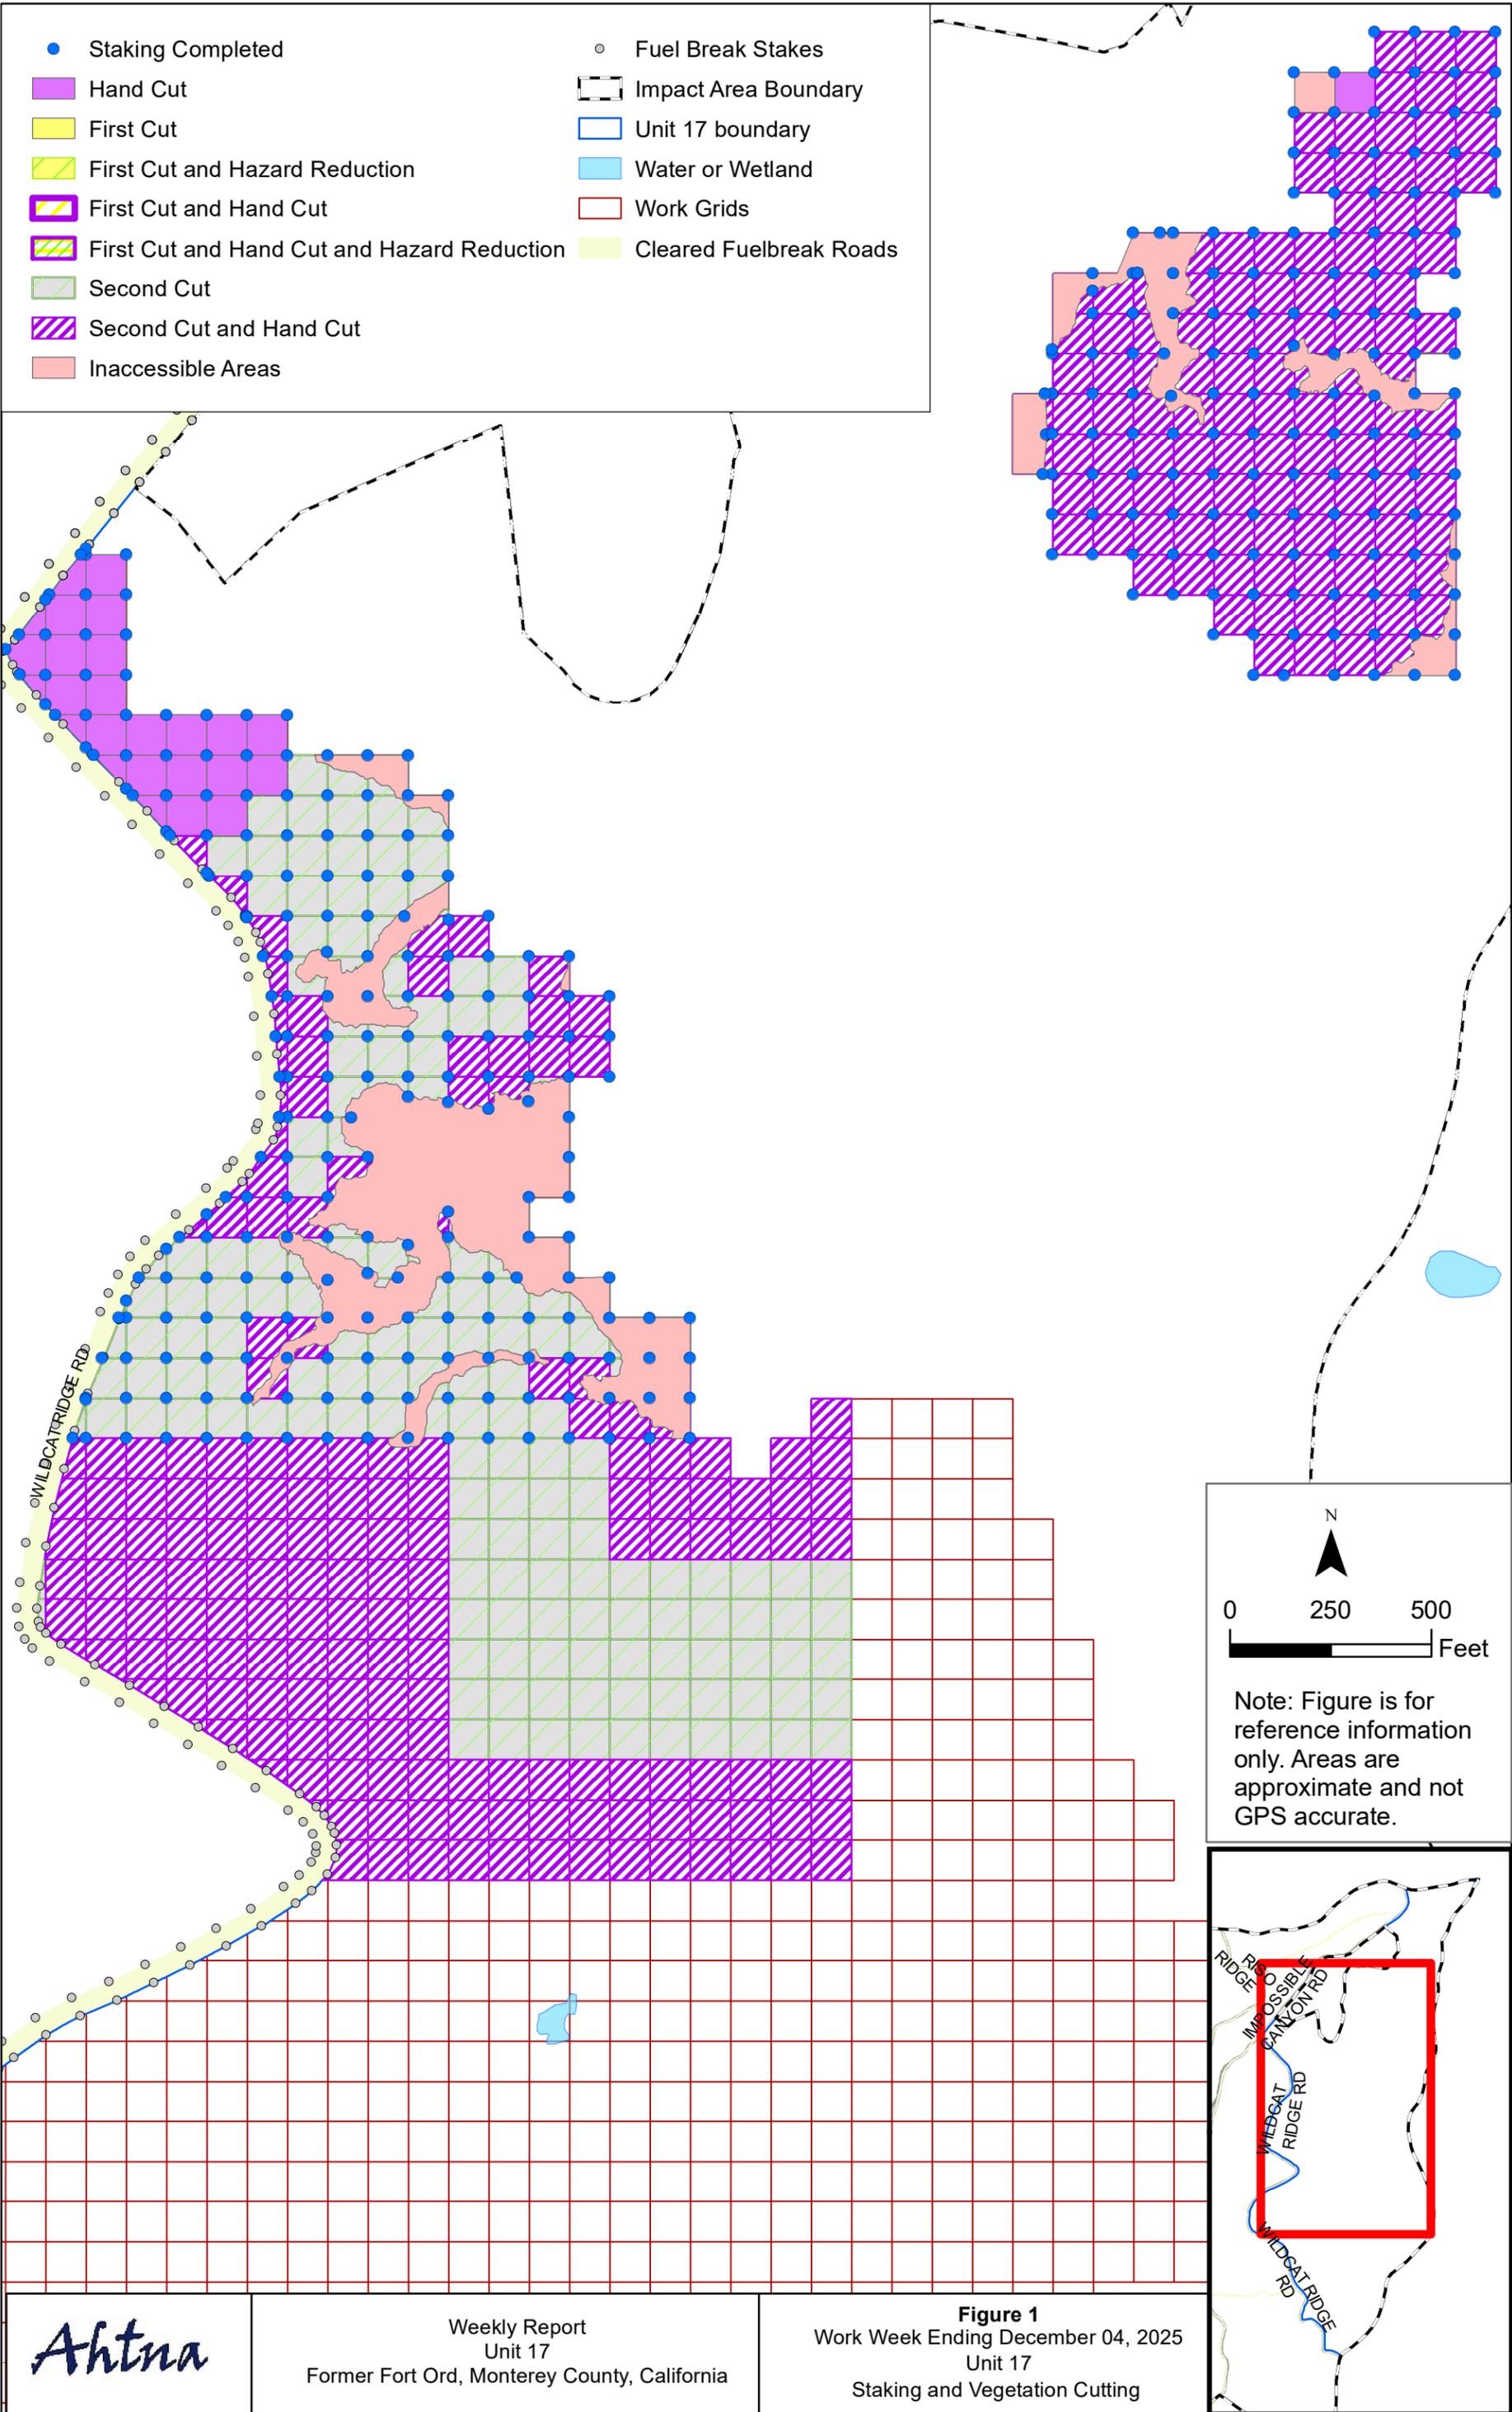


- Staking Completed
- Hand Cut
- First Cut
- First Cut and Hazard Reduction
- First Cut and Hand Cut
- First Cut and Hand Cut and Hazard Reduction
- Second Cut
- Second Cut and Hand Cut
- Inaccessible Areas
- Fuel Break Stakes
- ▭ Impact Area Boundary
- ▭ Unit 17 boundary
- Water or Wetland
- ▭ Work Grids
- Cleared Fuelbreak Roads

N

0      250      500  
Feet

Note: Figure is for reference information only. Areas are approximate and not GPS accurate.

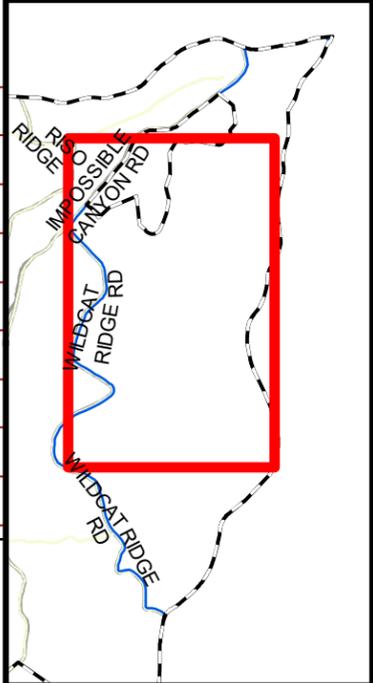

Weekly Report  
Unit 17  
Former Fort Ord, Monterey County, California

**Figure 1**  
Work Week Ending December 04, 2025  
Unit 17  
Staking and Vegetation Cutting

# Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations –

- Instrument Aided Surface MEC Removal – Started October 15, 2025

- ~ 20 acres completed to date
- ~ 118 acres projected
- Delineating inaccessible areas during surface removal


- Items recovered

- 1 – Projectile, 37mm, LE, MKII (safe to move, staged in ESL for consolidated demolition)
- 10 – Projectile, 40mm, HE, M383 (blown in place)
- 2 – Cartridge, 40mm, HE, M383 (blown in place)
- 317 lbs. MD
- 297 lbs. Other Debris


- QC/QA – In Progress





07 Oct 2025, 11:21:30

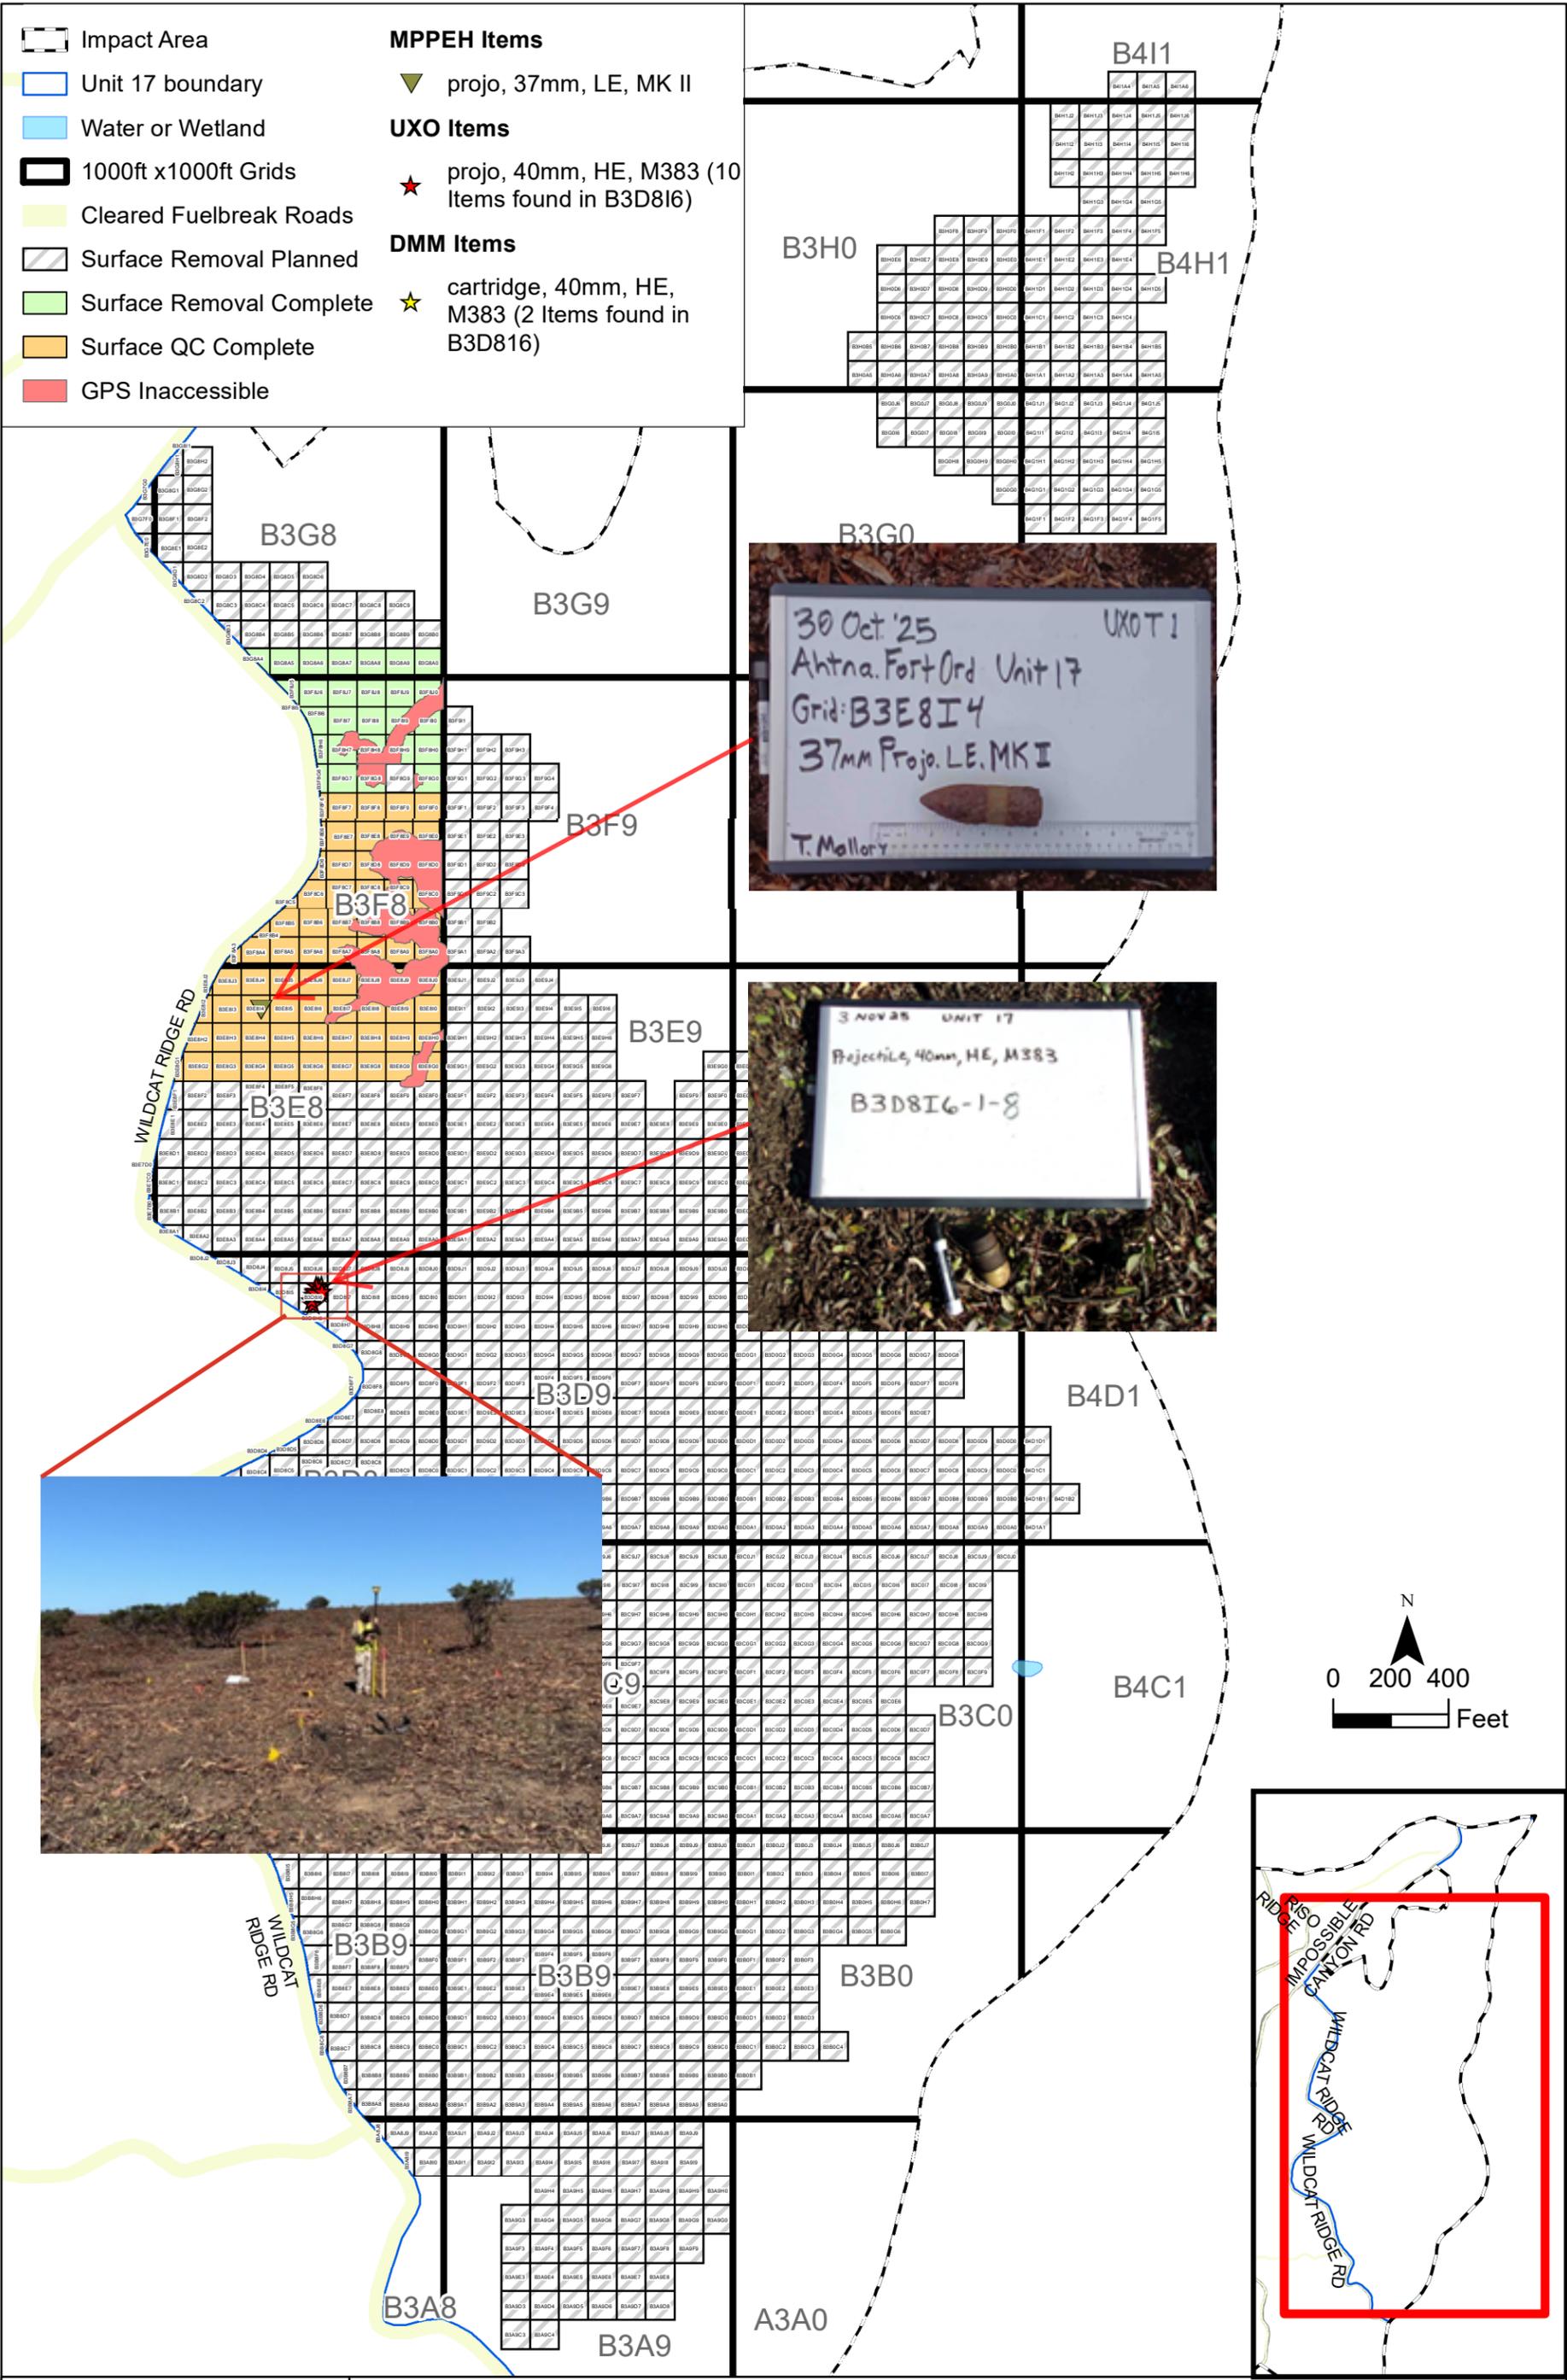

**Ahtna** Unit 17 Surface Removal  
 MEC Removal Status Week Ending Dec. 4, 2025  
 Former Fort Ord, Monterey County, California

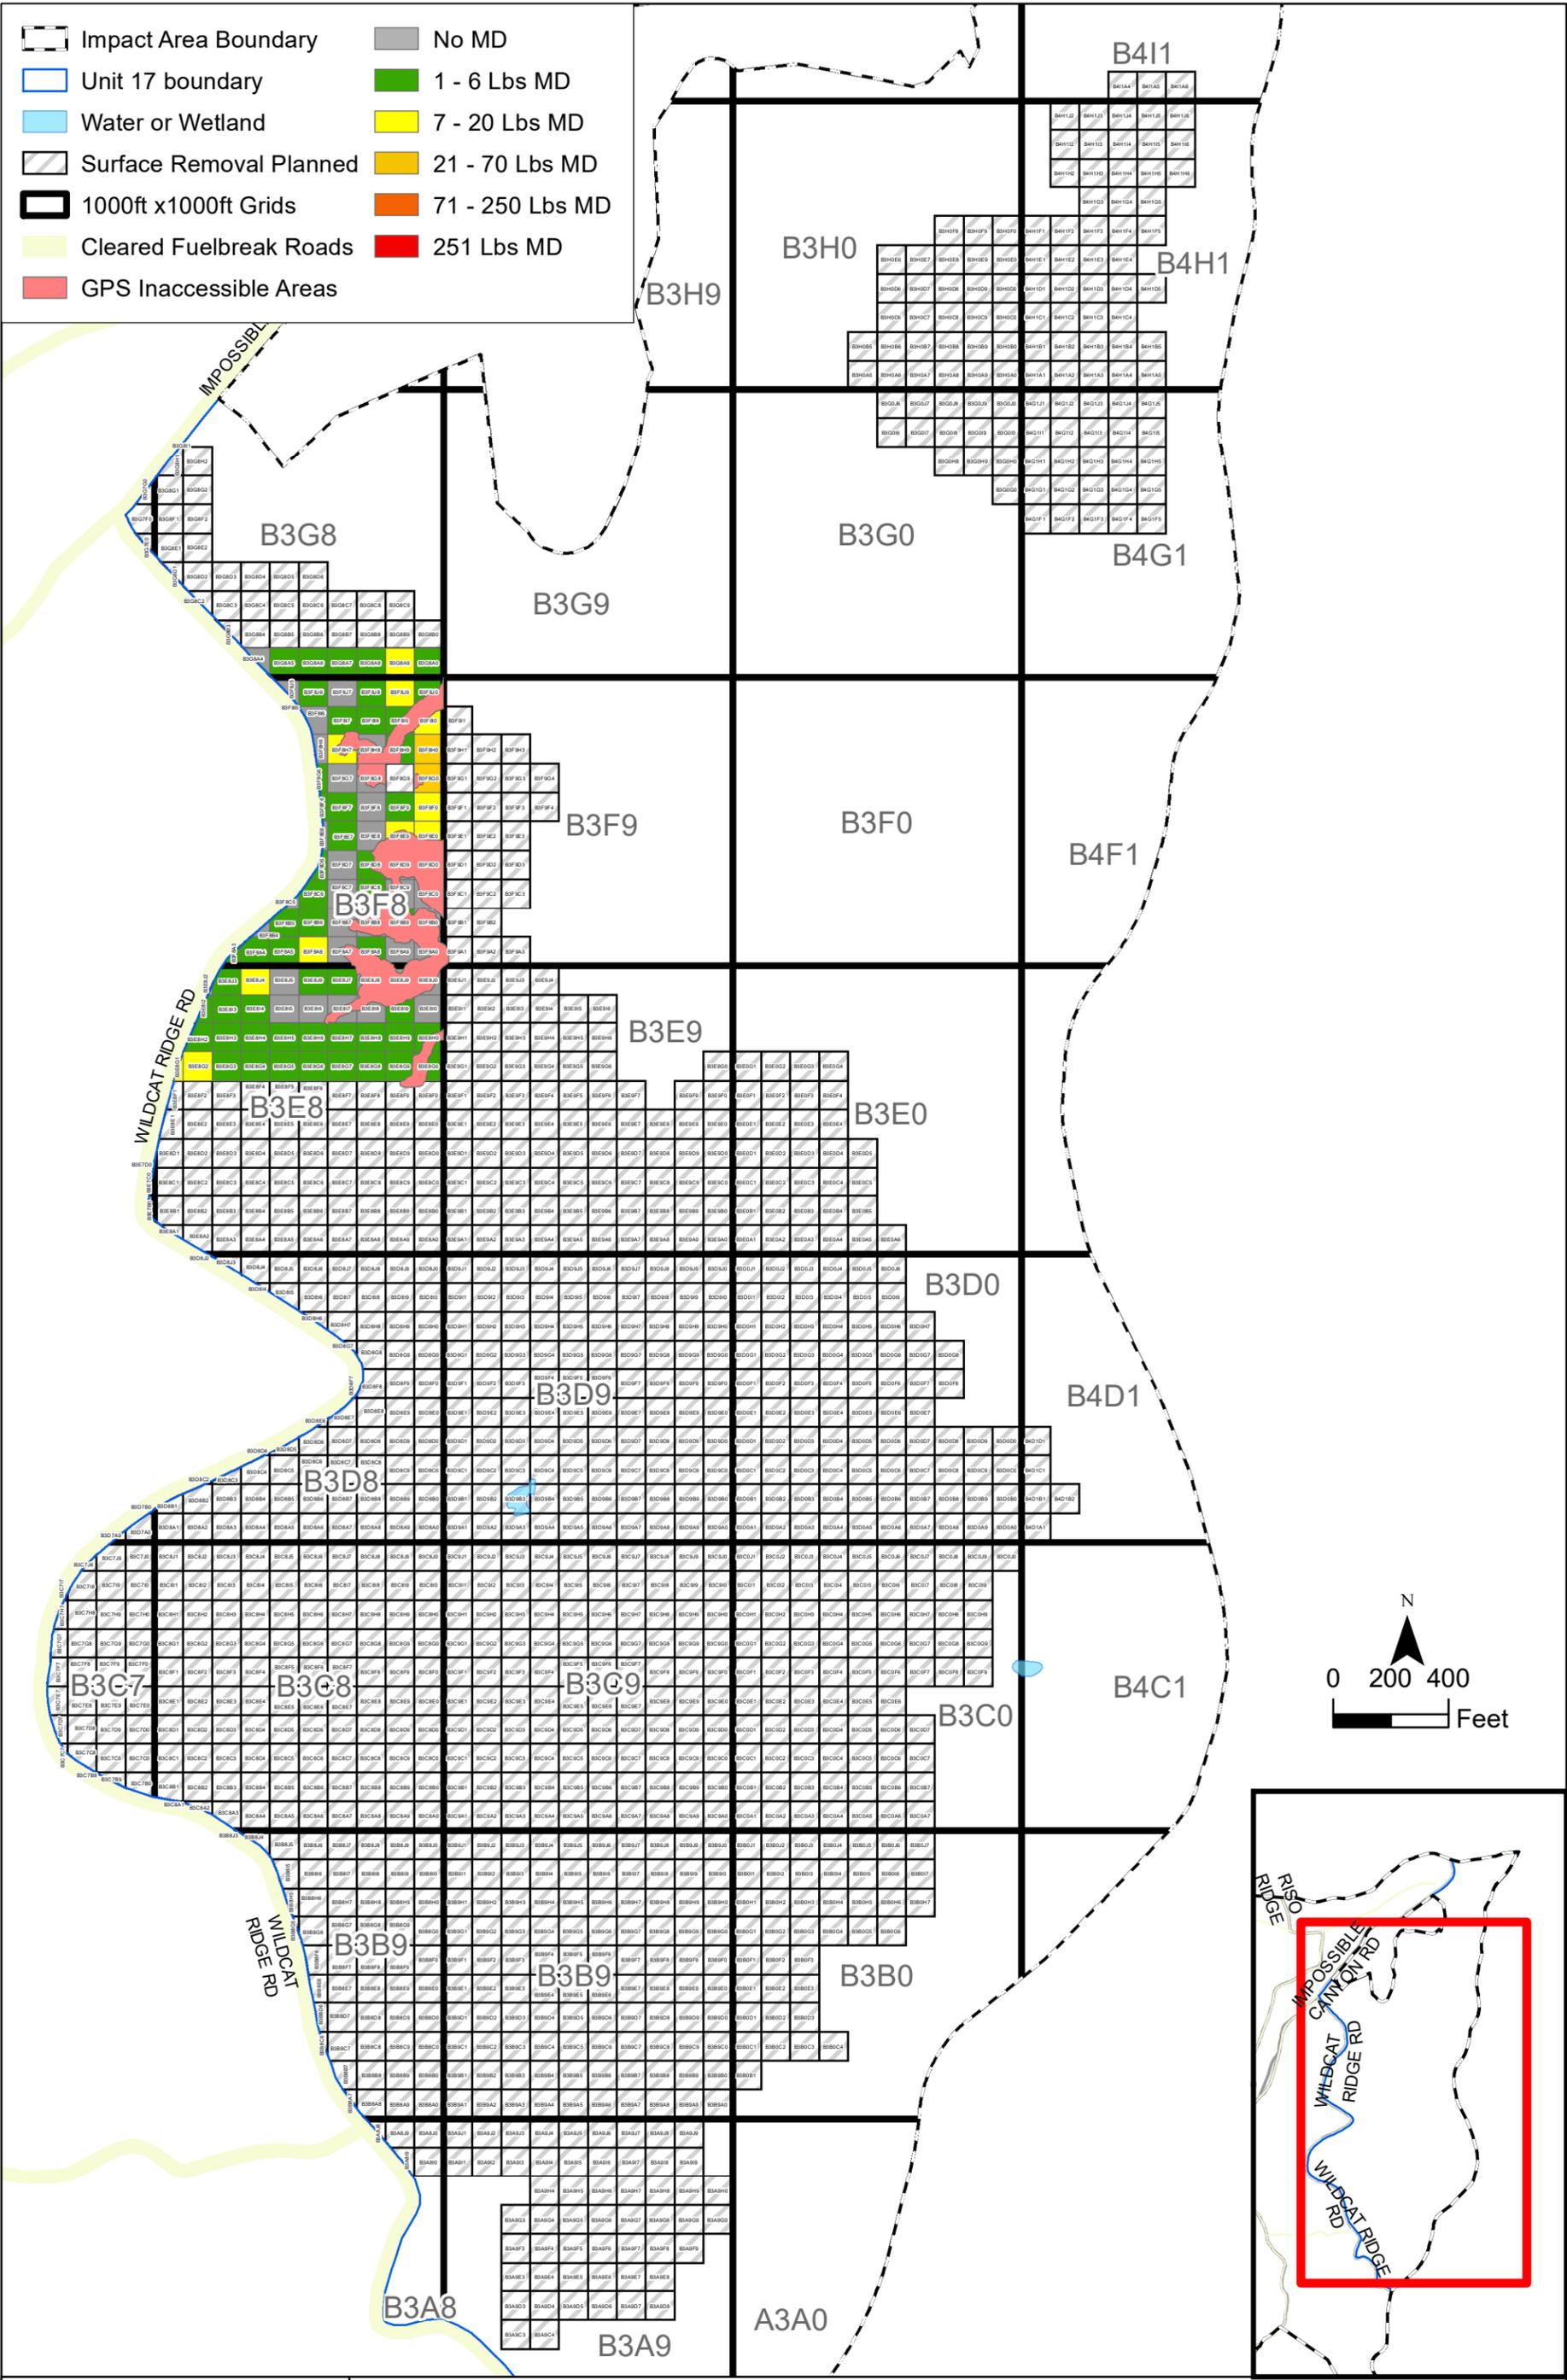

- Impact Area Boundary
- Unit 17 boundary
- Water or Wetland
- Surface Removal Planned
- 1000ft x1000ft Grids
- Cleared Fuelbreak Roads
- GPS Inaccessible Areas
- No MD
- 1 - 6 Lbs MD
- 7 - 20 Lbs MD
- 21 - 70 Lbs MD
- 71 - 250 Lbs MD
- 251 Lbs MD

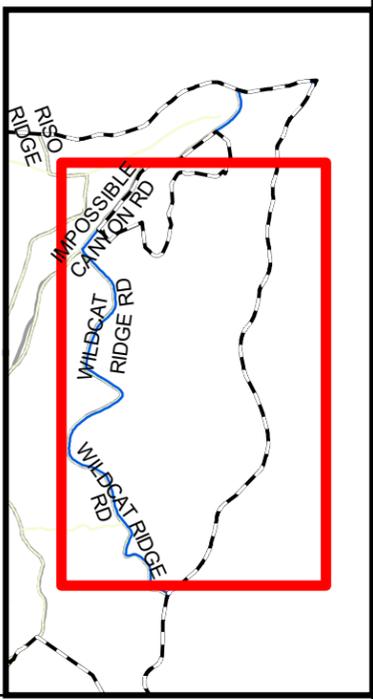

**Ahtna**

Unit 17 Surface Removal  
 MD Density Week Ending Dec. 04, 2025  
 Former Fort Ord, Monterey County, California

# Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations Schedule
  - Technology Aide Surface MEC removal
    - Started October 15, 2025, expected completion in May-June 2026
  - Digital Geophysical Mapping (DGM) Instrument Verification Strip Setup
    - December 2025
  - DGM Survey in accessible areas
    - January 5, 2026 – May-June 2026

