

Fort Ord MR BCT
Ahtna Status
Contract No. W9123824D003

February 20, 2026


Document Development – Task Order 1


- Unit A Prescribed Burn Plan

Version	Task Description	Dates
Final	Schedule for Delivery	TBD

Unit A MEC Remedial Actions – Task Order 3

- Unit A Prescribed Burn
 - Prescribed burn season ended December 2025
 - Chances for weather and fuel moisture meeting prescription became low
- Demobilization of Equipment is ongoing
 - Fuel tanks, water stands and water meters - removed
 - Temporary fence and gates at CSUMB parking lot suppression helibase - removed.
 - Water storage tanks - removal in progress
- Air Monitoring
 - Air monitoring network - in place

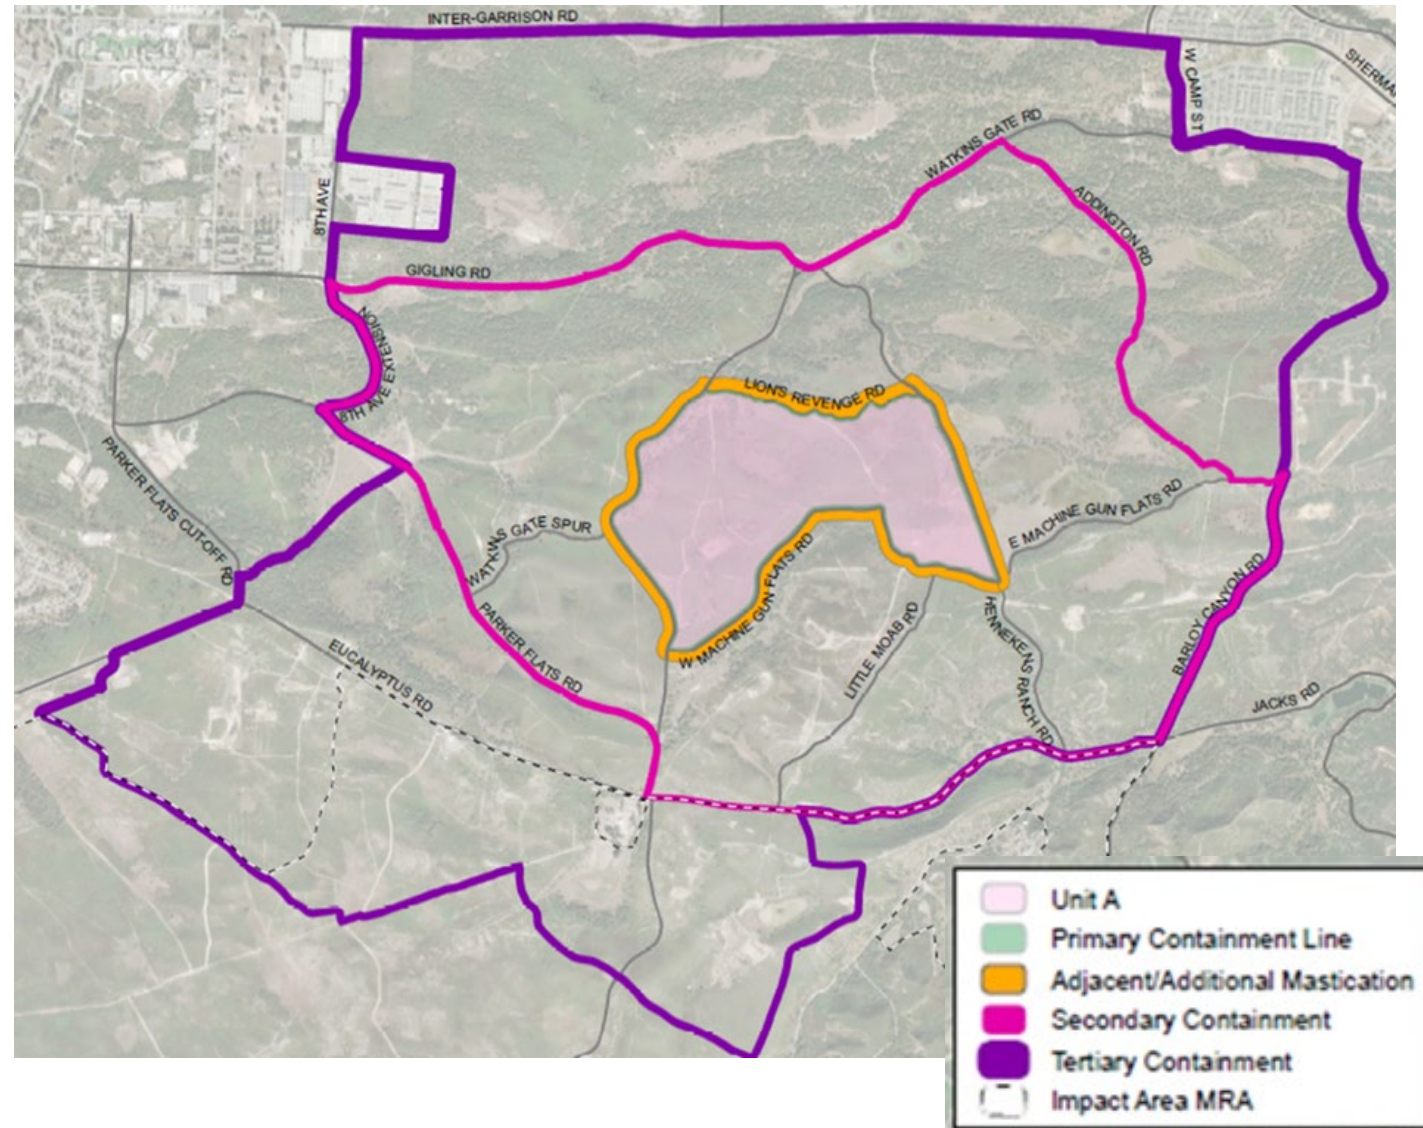


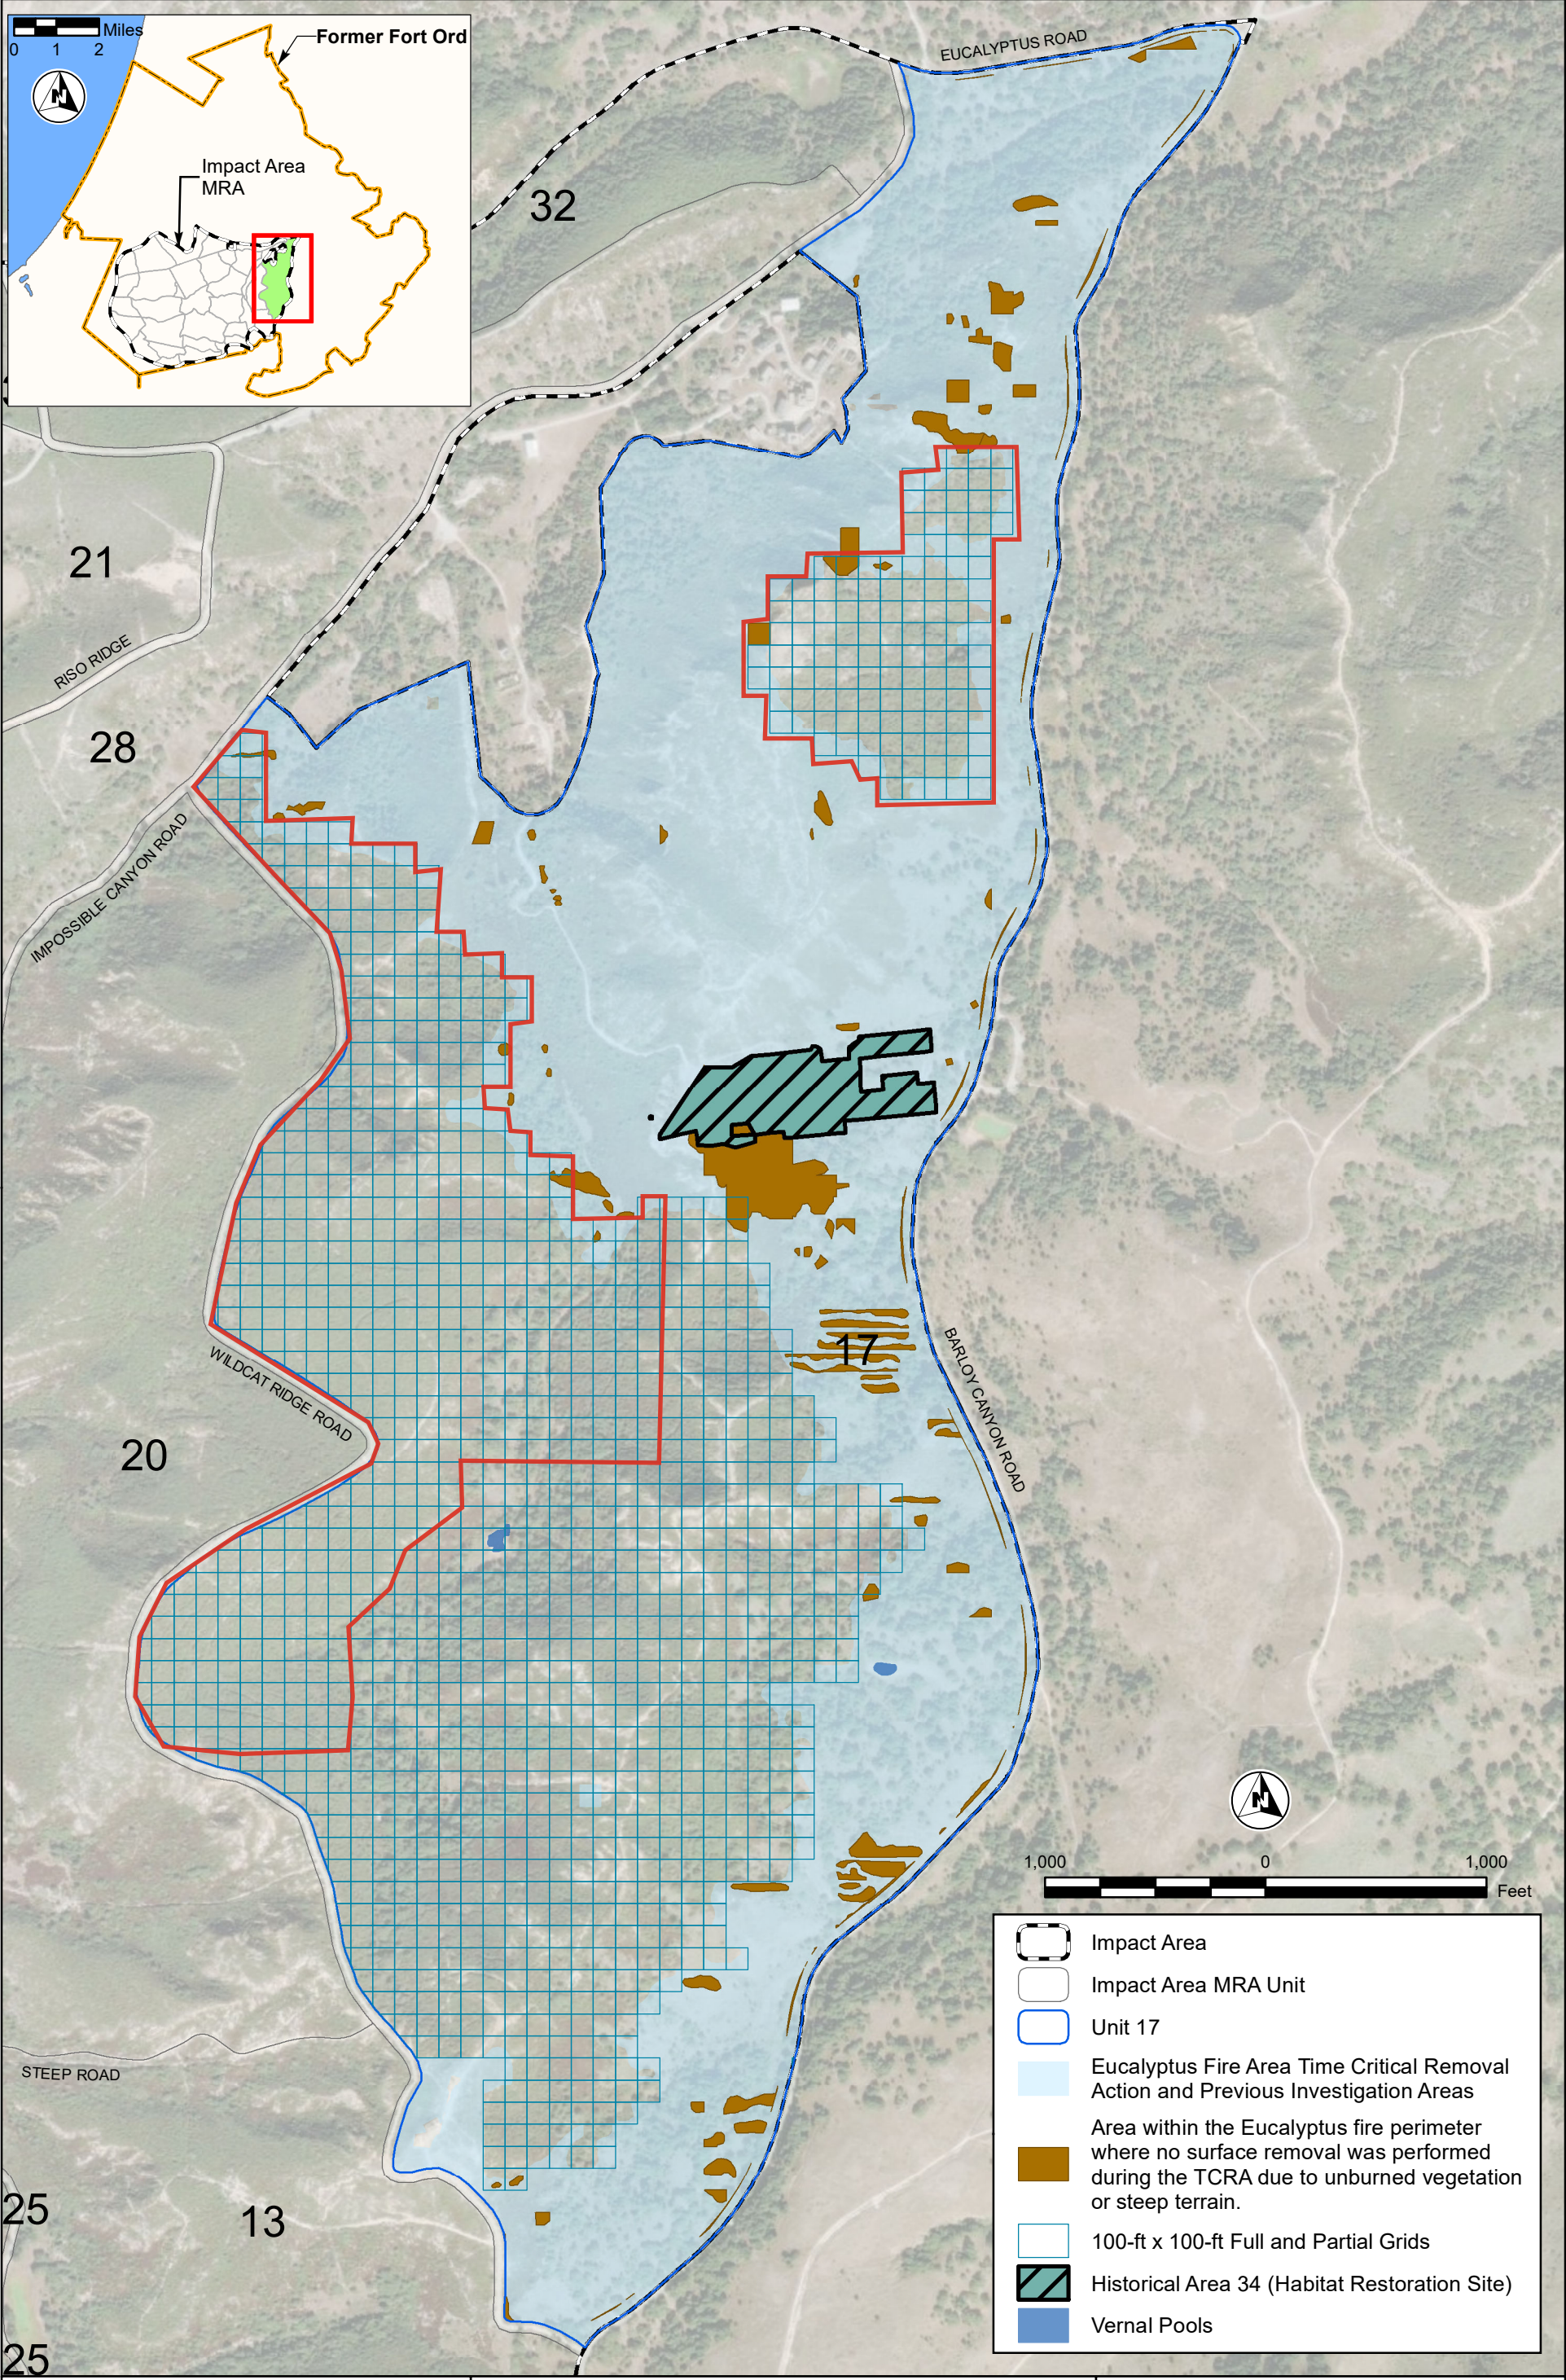

Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations
 - Boundary Survey – Completed January 26, 2026
 - Grid Corner Staking – Completed January 26, 2026
 - Vegetation Cutting
 - Mechanical – Completed December 30, 2025
 - ~ 114 acres completed
 - Manual – Completed January 8, 2026
 - Conducted in 487 grids of masticated areas
 - ~ 5 acres hand cut only completed
 - Erosion Control
 - Biological Support



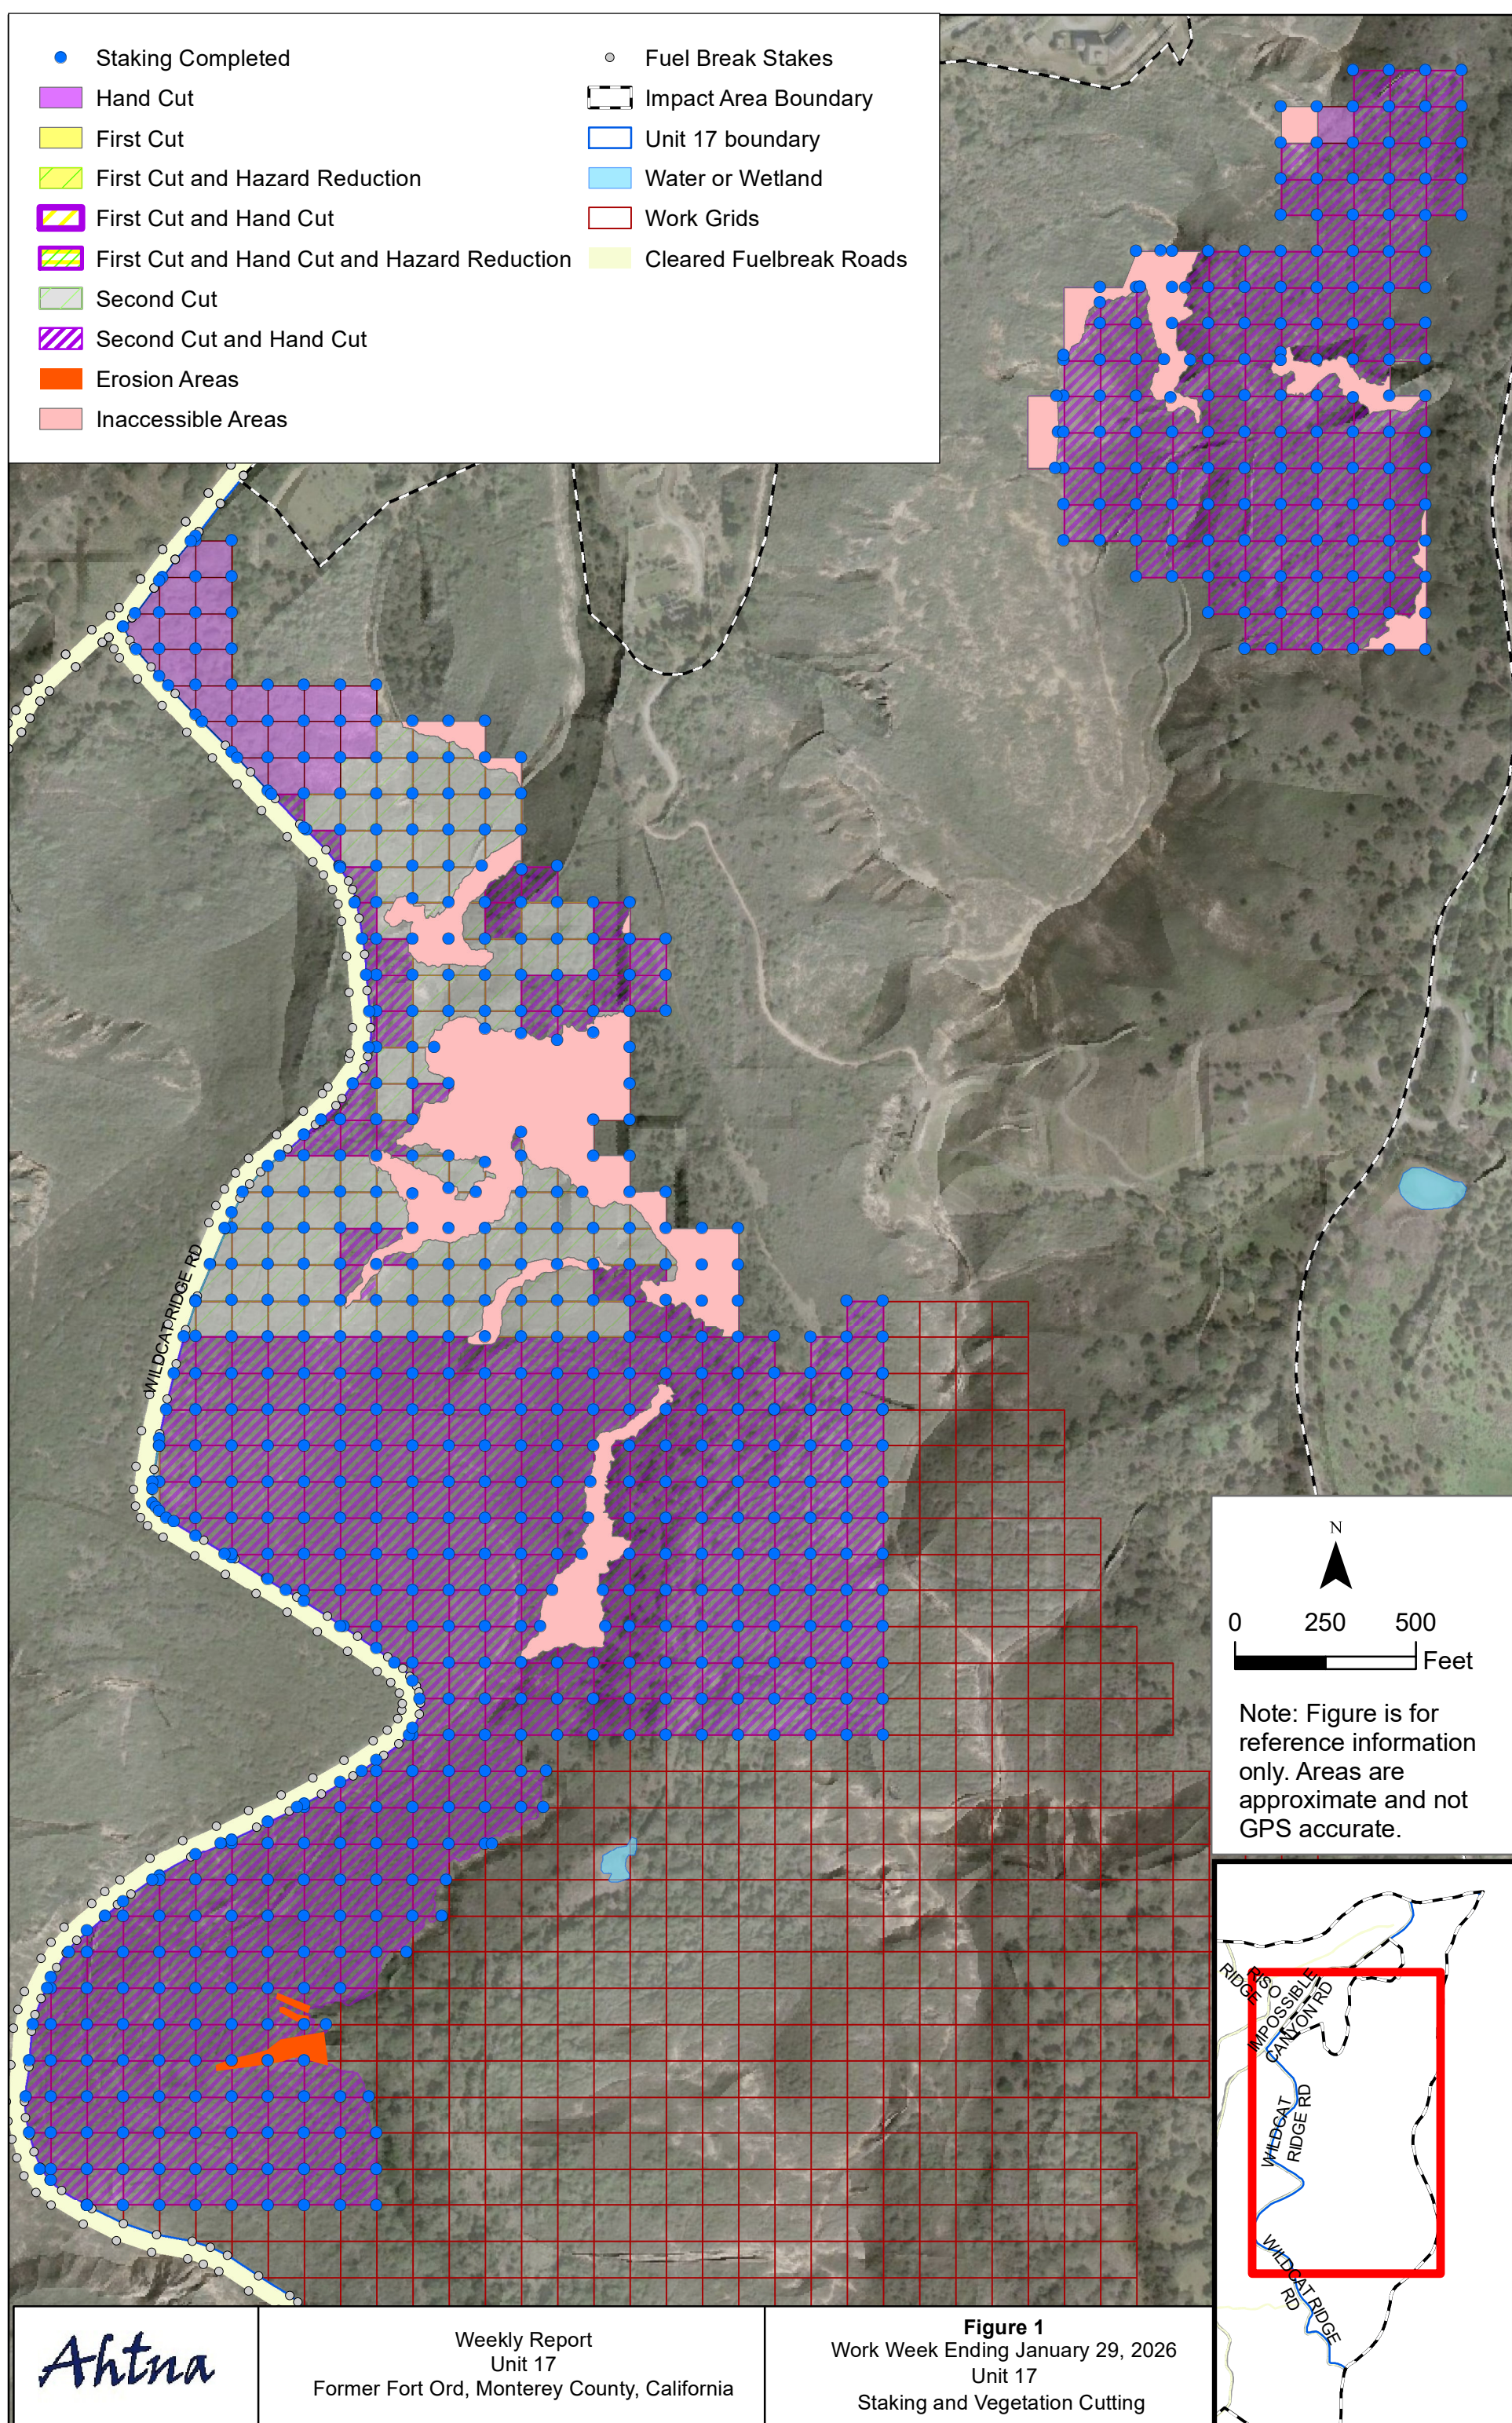



Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations
 - Instrument Aided Surface MEC Removal
 - Started October 15, 2025
 - ~ 50 acres completed to date
 - ~ 118 acres projected
 - Evaluating inaccessible terrain
 - ~ 13 acres
 - Items recovered
 - 1 – Projectile, 37mm, LE, MKII (MPPEH)
 - 1 – Projectile, 50mm, Mortar, Type89, Japanese NI (MPPEH)
 - 11 – Projectile, 40mm, HE, M383 (BIP)
 - 3 – Cartridge, 40mm, HE, M383 (BIP)
 - 1,081 lbs. MD
 - 1,058 lbs. Other Debris (scrap metal, wire)
 - QC/QA
 - 305 QA/QC seeds recovered
 - ~ 45 acres QC Complete
 - ~ 40 acres QA Complete



BIP = Blown in Place
MPPEH = Material Potentially Presenting an Explosive Hazard
MD = Munitions Debris




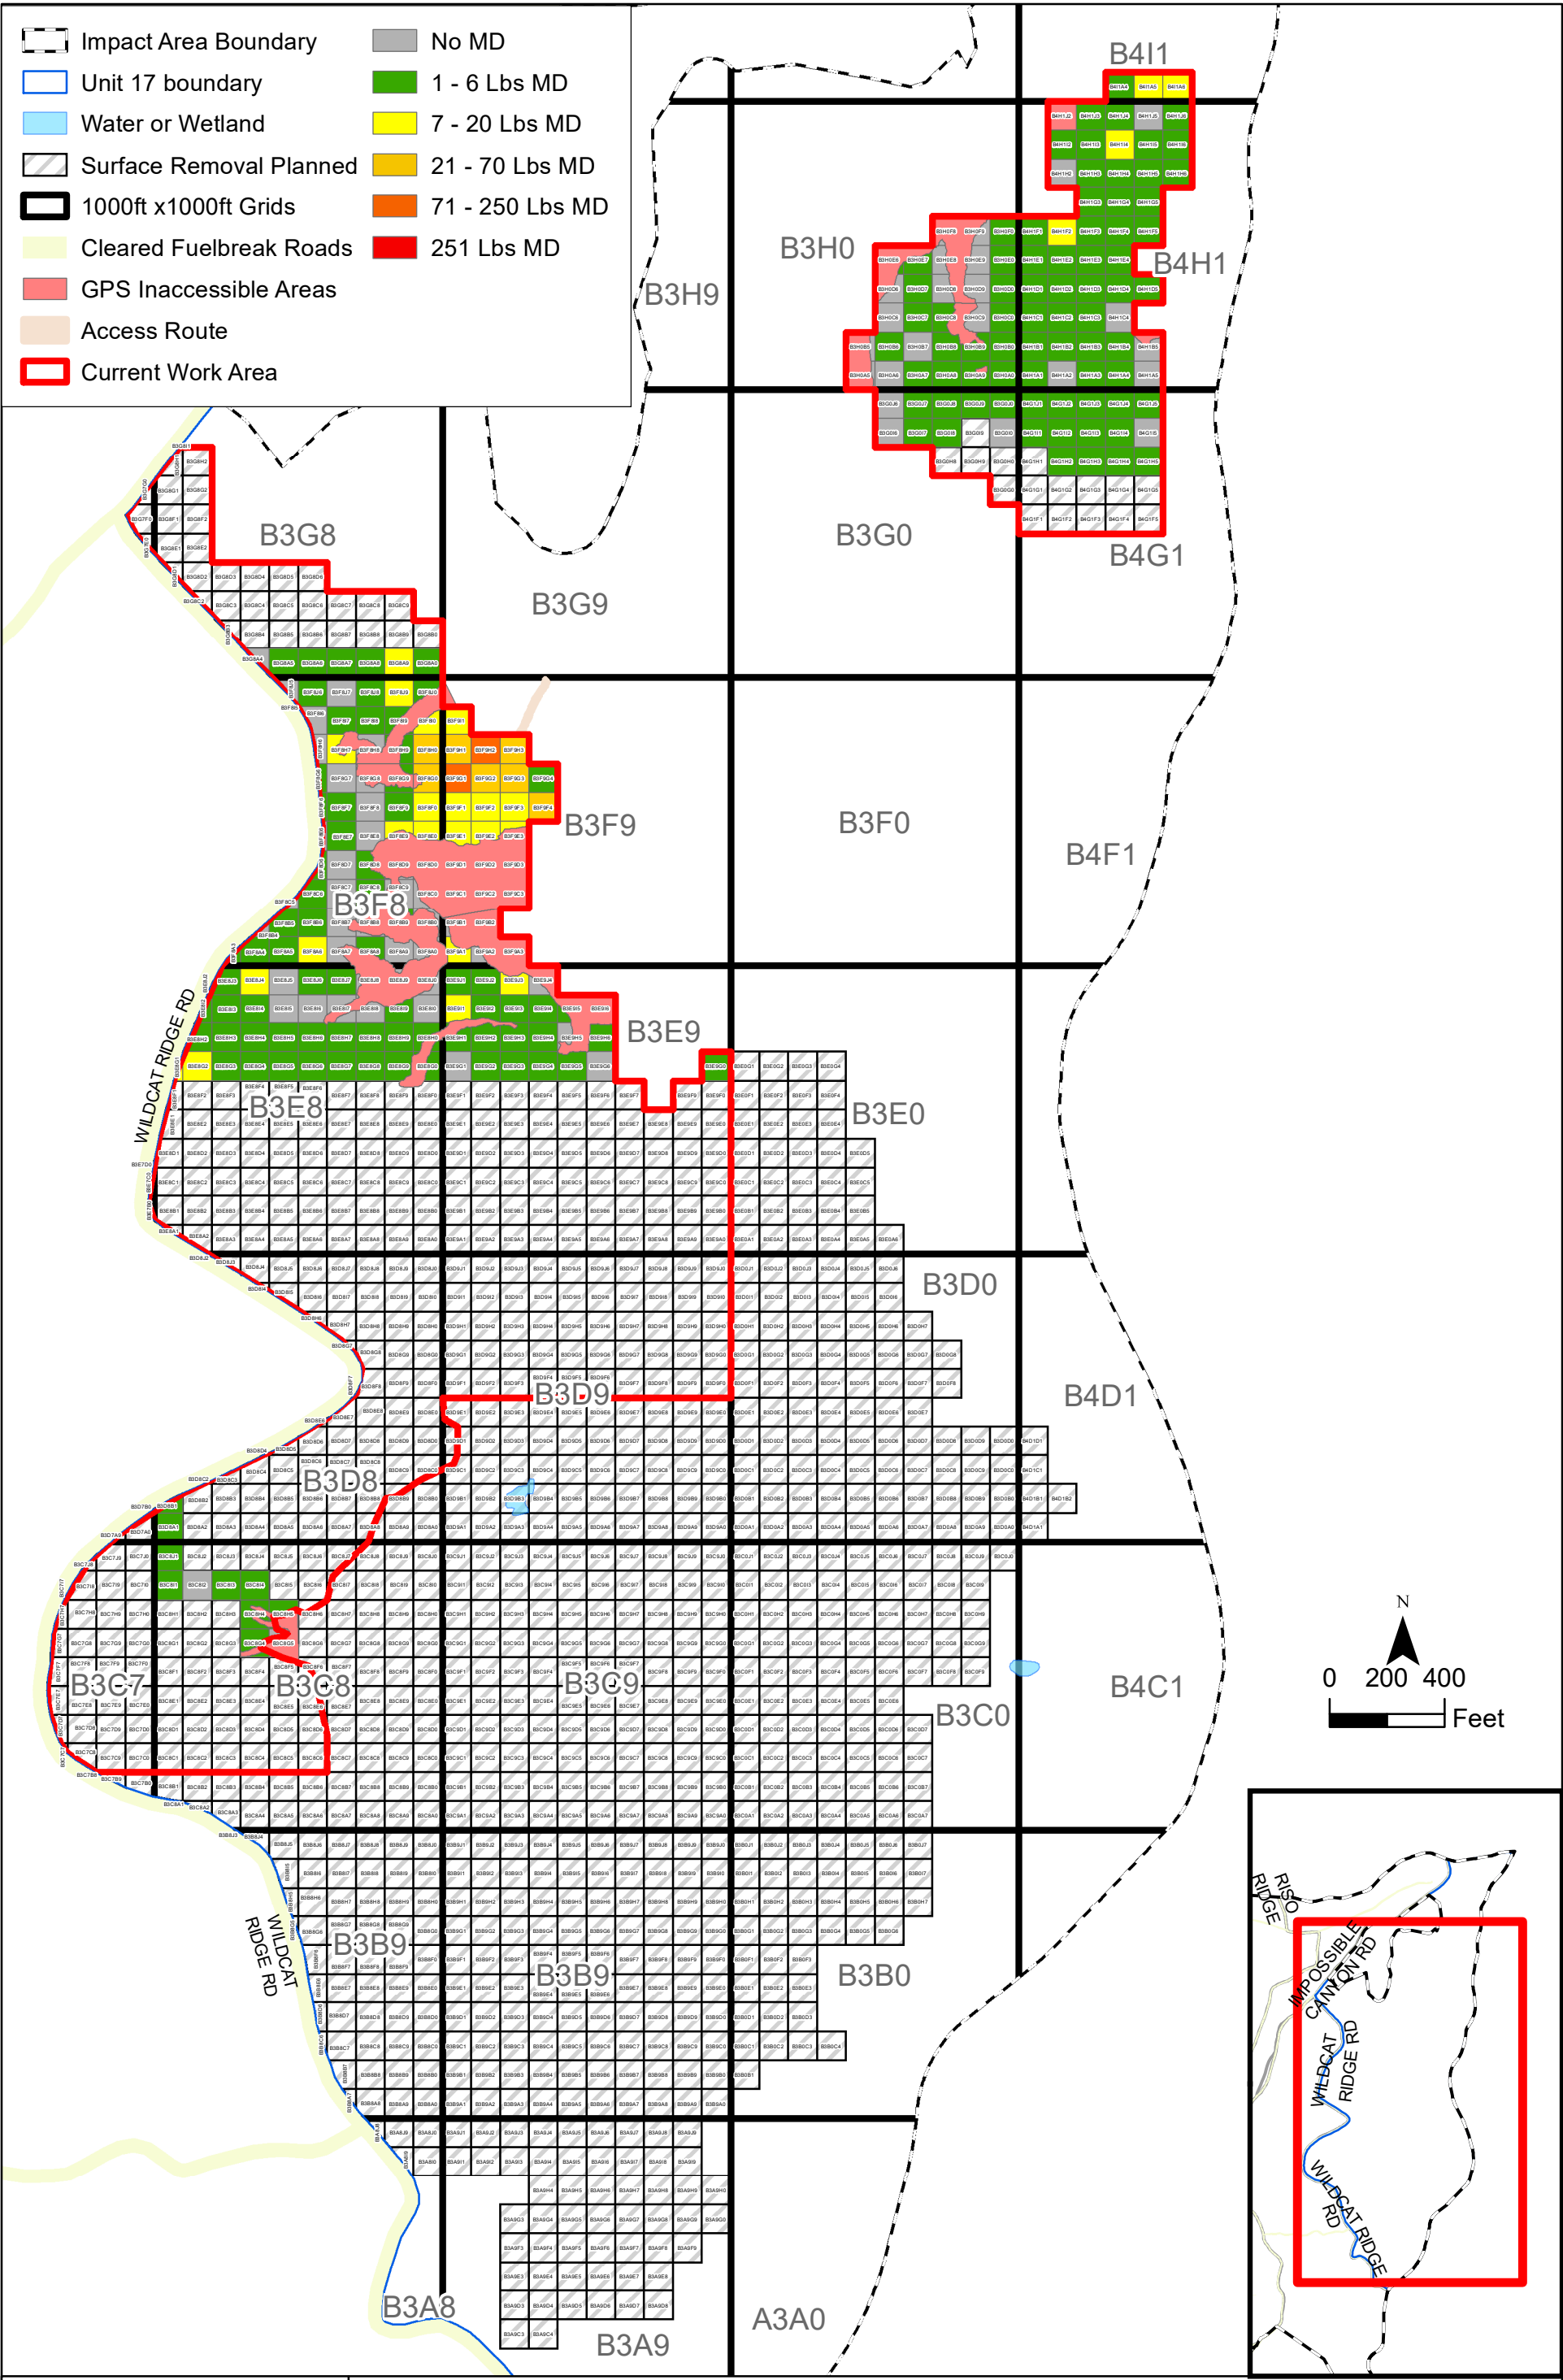

Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations –
 - Digital Geophysical Mapping (DGM) Instrument Verification Strip (IVS) Setup and Memo
 - IVS and data acquisition completed 1/26/2026
 - IVS data acquisition approved by USACE 1/27/2026
 - Draft IVS Memo in progress
 - DGM Survey Started 1/28/2026
 - ~ 7 acres completed to date



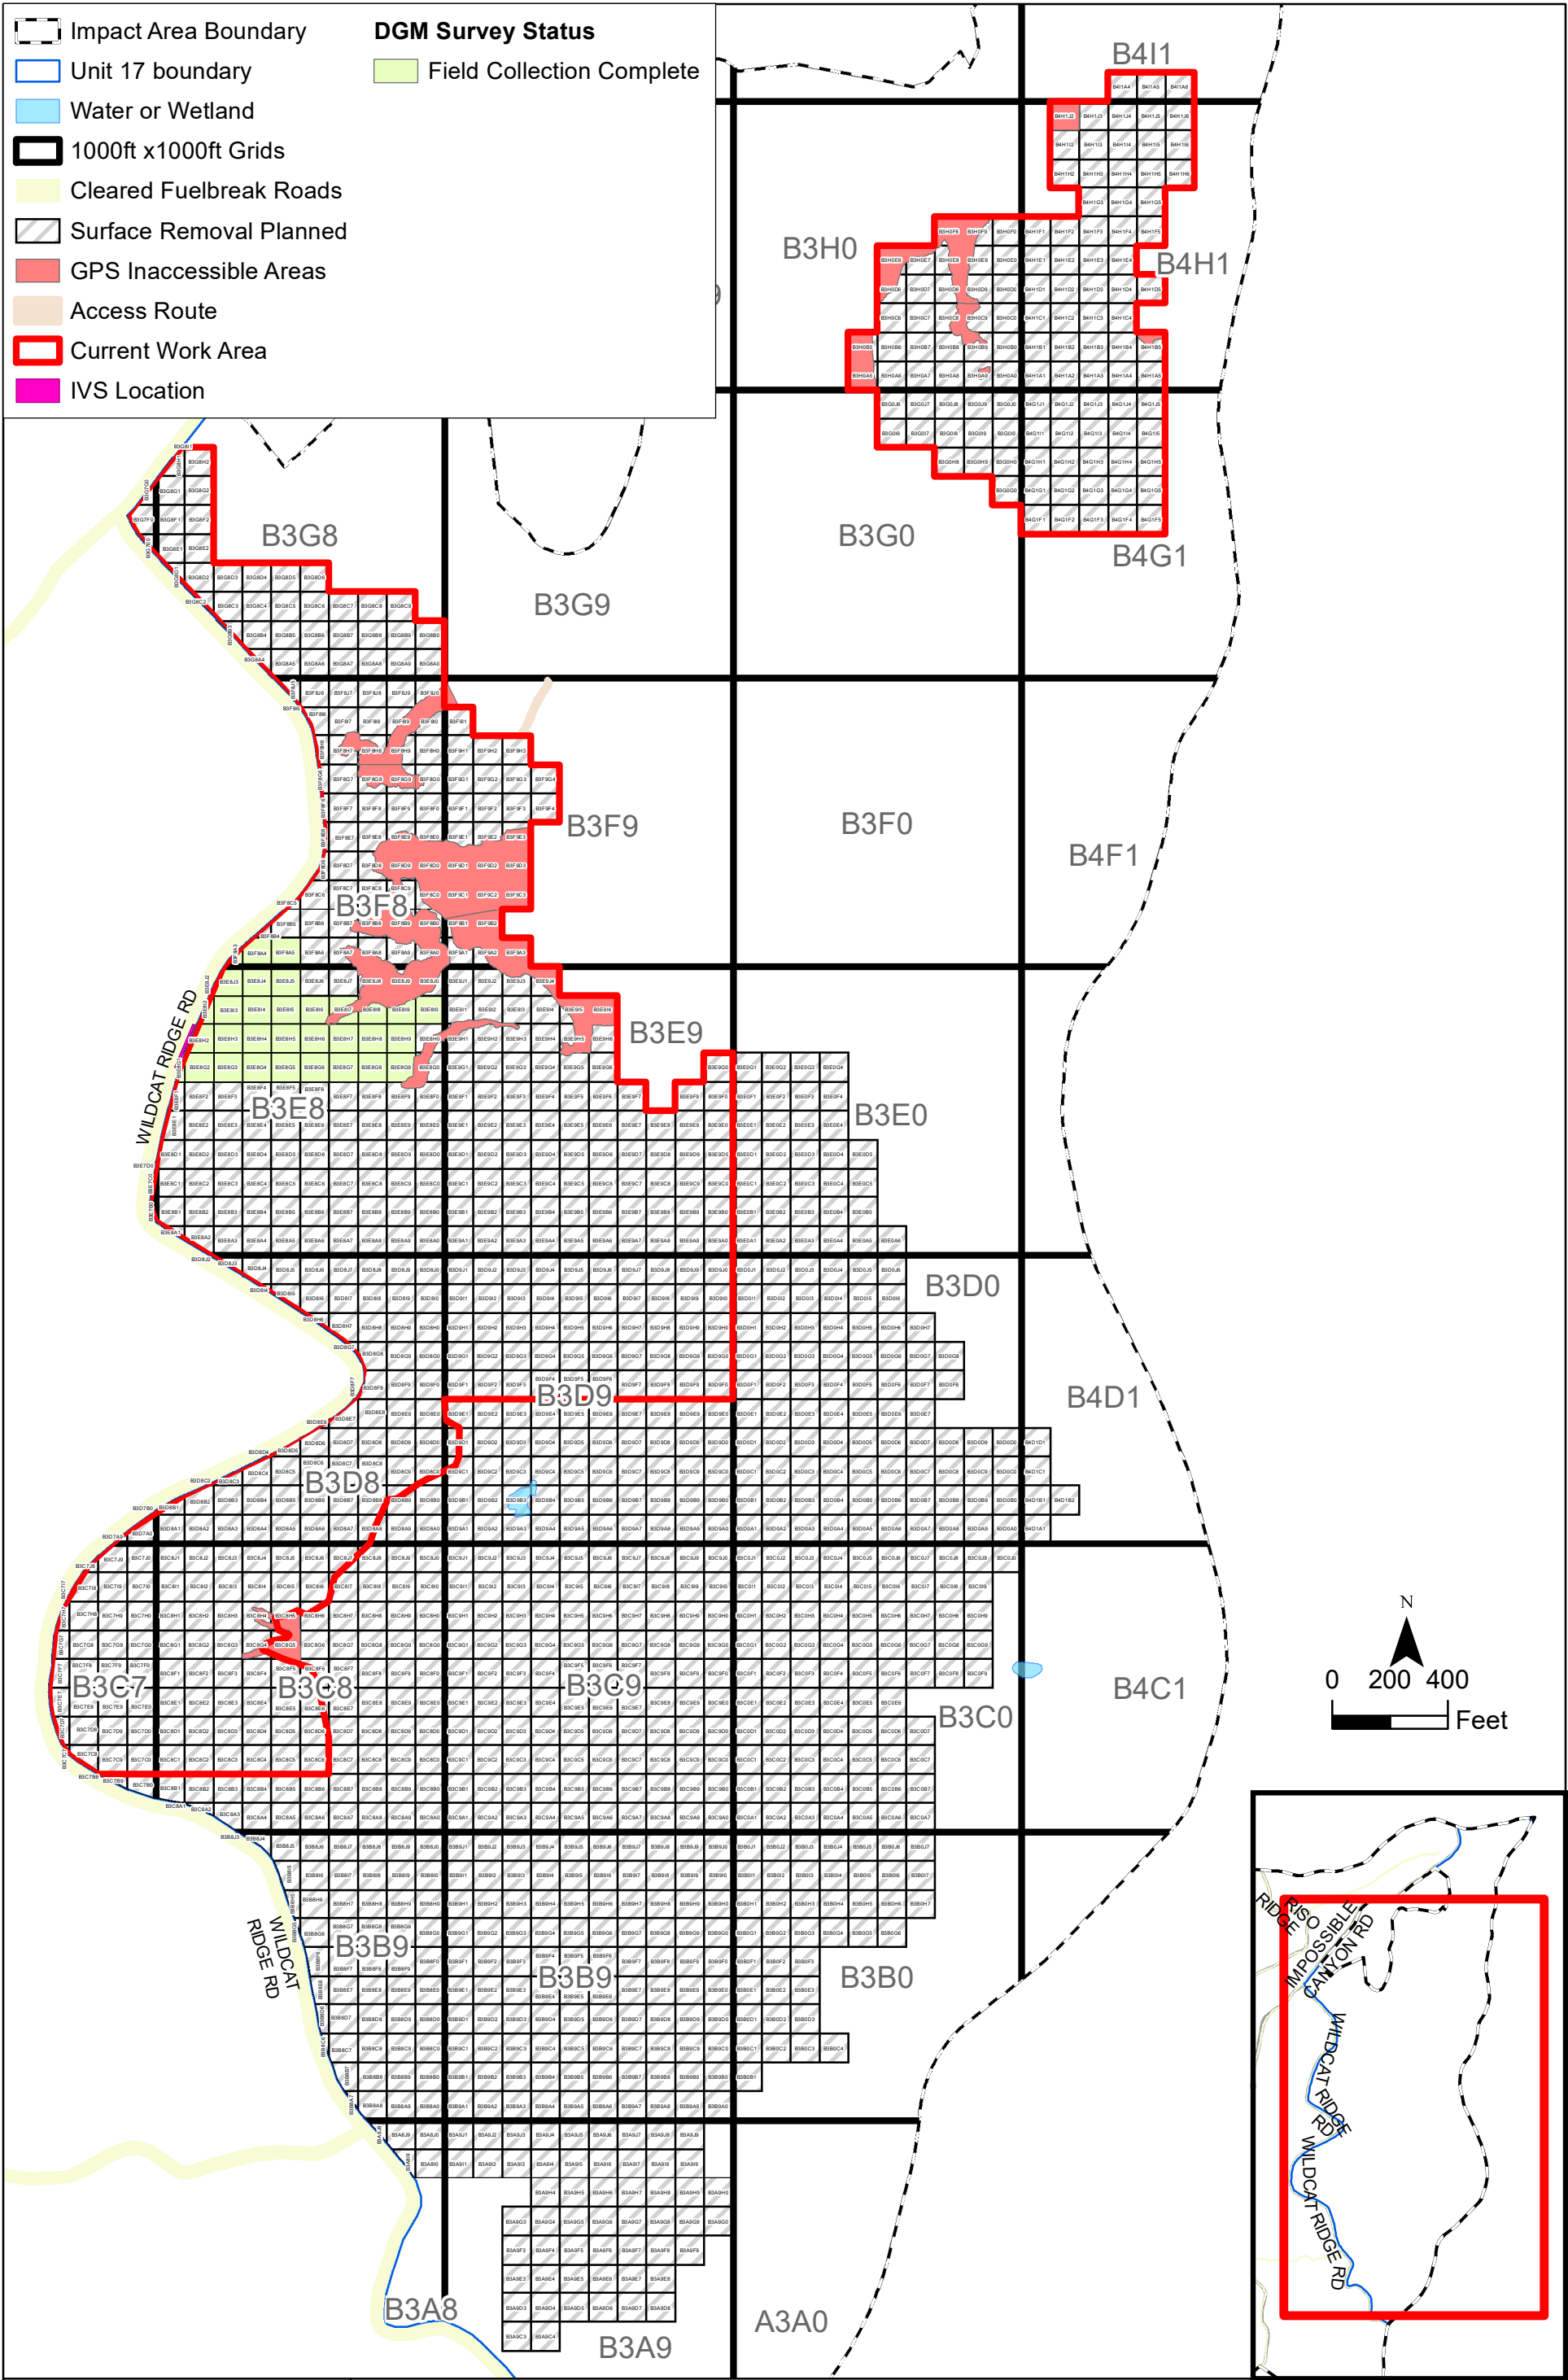

Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations Schedule
 - Technology Aide Surface MEC removal
 - Started October 15, 2025, expected completion in June 2026
 - Digital Geophysical Mapping (DGM) Instrument Verification Strip (IVS) Setup and Memo
 - IVS set up and data acquisition - Started December 6, 2025, completed January 27, 2026
 - IVS Memo – In progress
 - DGM Survey
 - January 28, 2026 – May-June 2026

