

MR BCT Meeting Agenda

Wednesday, April 23, 2014 at 10:00 a.m.
Fort Ord BRAC

Item	Action	Comment
Community Relations	Update	
Property Transfer	Update	
ESCA	Update	
Fieldwork / Track 3	Update	<ul style="list-style-type: none">- 100-ft buffer- WGBA unburned areas- Units 10 / 7 / 33- Surface Monitoring
Site Security Program	Update	
Remaining RI/FS Areas Program	Update	- Track 2 RI/FS for BLM Area B
MRS-34 (FAAF)	Update	
Report Status	Update	
FFA Schedule	Update	
Action Items	Review	
Next BCT meetings	Schedule	- 5/16 at 10:00 am

U.S. Army Community Outreach Update

Long Term Actions Underway:

1. Update all fact sheets – on-going
2. Web site reformat – on-going
3. Develop 2013 Annual Report – to be mailed in June

Recent Activities:

1. 20MAR Provided cleanup tour for DTSC (Focus: munitions cleanup)
2. 24MAR Provided cleanup tour for USEPA Region 9 Administrator (Focus: Prescribed Burns)
3. 7APR USEPA TASC meeting on the prescribed burn after action report (Meeting of interest. Note: Army did not participate. Meeting was filmed by Access Monterey Peninsula and may be broadcast on YouTube at <http://www.youtube.com/user/ampmediatv/videos>)
4. 17APR Provided presentation to Monterey County Chapter – Military Officers Association of America
5. 18APR Completed fact sheet for 2/12 Pilot Study Construction Project is available for distribution at project site
6. 18APR Sent fact sheet and well destruction work plan to property owners involved with project
7. 17APR Provided landfill cleanup presentation for CSUMB film students
8. 22APR Provided Earth Day Booth at California State University Monterey Bay
9. 23APR Provided Earth Day Booth at Defense Manpower Data Center (DMDC)


Upcoming Activities:

1. 24APR Provide Earth Day Booth at Presidio of Monterey
2. TBD Provide Munitions Safety presentation to Fort Ord Bicycle, Equestrian Trails Assistance (BETA) organization
3. TBD Provide Munitions Safety presentation to Fort Ord Equestrian Center
4. 17MAY Provide Nature Walk inside the Impact Area
5. TBD late MAY / early JUN Cleanup Bus Tour for Naval Postgraduate School class: IT1500
6. 15AUG Provide annual Munitions Safety/Awareness presentation for York School
7. 29AUG Provide cleanup Information Booth at the Monterey County Fair
8. **NEW DATE!** 23AUG Community Involvement Workshop—munitions, prescribed burns, and ESCA
9. **NEW DATE!** 26AUG Technical Review Committee— munitions, prescribed burns, and ESCA

STATUS: RESPONSE to COMMUNITY COMMENTS (RTC)

AR Number	Title/Subject	Status
OE-0802.5	Comments submitted by Mike Weaver, Fort Ord Community Advisory Group - on the Draft BLM Area B Remedial Investigation / Feasibility Study, Former Fort Ord, California	Complete
BW-2674.2	Comments submitted by Mike Weaver, Fort Ord Community Advisory Group - on the Draft Technical Memorandum Evaluation of Lead Concentrations at Selected Sites, Former Fort Ord, California	In progress
ESCA-0267.2	Comments submitted by community member, Gail Youngblood, on the Group 2 Proposed Plan, CSUMB Off-Campus MRA, FORA ESCA RP	In Progress/Part of CSUMB Off-Campus Group 2 ROD Responsiveness Summary
ESCA-0267.3	Comments submitted by community group member Mike Weaver, Fort Ord Community Advisory Group, on the Group 2 Proposed Plan, CSUMB Off-Campus MRA, FORA ESCA RP - at the June 19, 2013 public meeting	In Progress/Part of CSUMB Off-Campus Group 2 ROD Responsiveness Summary
OE-0793.4	Comments submitted by community member, Mike Weaver, Fort Ord Community Advisory Group, on the Group 2 Proposed Plan, CSUMB Off-Campus MRA, FORA ESCA RP	In Progress/Part of MRS-34 ROD Responsiveness Summary

MMRP Fieldwork Update

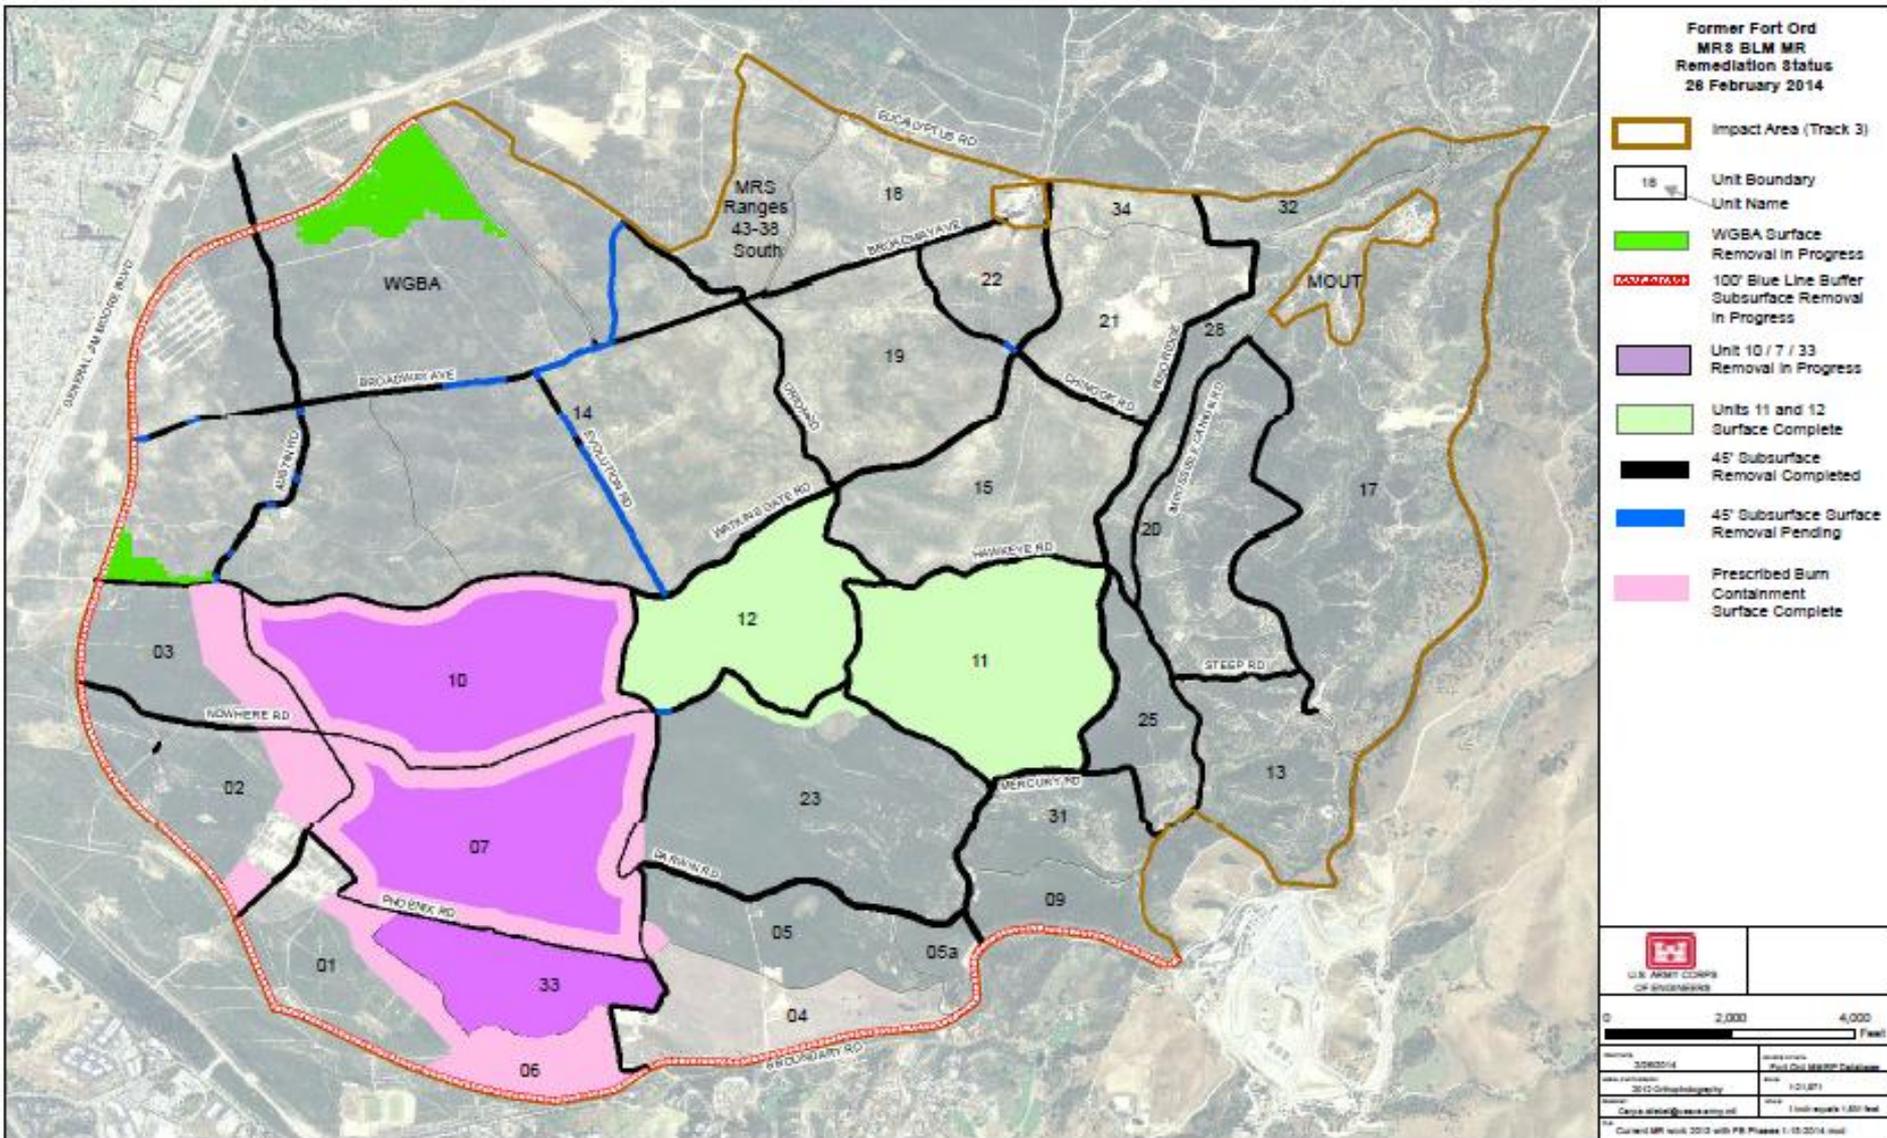

MMRP Fieldwork Update

PROJECT: MRS-BLM (Track 3) Units 6/7/10/33 (767 acres)

An MMRP action in accordance with the Track 3 ROD including vegetation removal, technology-aided surface remediation, subsurface MEC remediation in selected areas, and digital geophysical mapping (DGM). Unit 33 added (FWV).

Start date: June 2012

Estimated end date : July 2014

PHASES:

	Start	End
Site preparation (complete)		
- Cutting of containment lines (Units 6/7/10) (complete)	06-04-12	08-22-13
- Unit 6 Interior vegetation removal (complete)	07-24-12	07-11-13
Vegetation removal		
- Prescribed burn (complete)	10-14-13	10-15-13
- Mechanical cut (interiors)	10-24-13	02-27-14
MEC Removal		
- Surface remediation		
○ Extra acreage *(Units 1, 2, 3)	07-15-13	09-08-13
○ Unit 6 (complete)	08-30-12	11-13-13
○ Interior of Units 7/33/10	12-02-13	05-29-14
- Subsurface remediation (as required)	N/A	N/A
DGM		
○ Unit 6 (complete)	01-02-13	11-14-13
○ Containment lines Units 7/10	03-04-13	04-13-14
○ Extra acreage *(Units 1, 2, 3)	09-23-13	11-20-14
○ Interior Units 7/33/10	03-05-14	07-24-14

*Previous work plan

ISSUES AND CONCERNS:

- Surface removal work complete on Unit 7. Teams progressing with surface removal in Unit 10.

MMRP Fieldwork Update

PROJECT: MRS-BLM (Track 3) Non-Burn Areas (509 acres)

An MMRP action in accordance with the Track 3 ROD including vegetation clearance, technology-aided surface MEC remediation, subsurface MEC remediation in selected areas, and DGM in areas located within the Impact Area including permanent fuel breaks, non-burn habitat areas, and 100 ft buffer areas. Fuel break subsurface removal is conducted as other removal priorities allow.

Start date: March 2010

Estimated end date : TBD

PHASES:

Start

End

Site preparation (as required)

- Vegetation cutting (as required)

- 100' buffer Units 1,2,3 WGBA 05-08-13 09-13-13

MEC Removal (in progress)

- surface (complete)

- subsurface

- 45' permanent fuel breaks 04-22-12 TBD
- MOUT Site 100 ft. Buffer 02-14-13 04-11-13
- 100' buffer Units 1,2,3 08-07-13 02/19/14*
- 100' buffer WGBA (in progress) 08-07-13 TBD

ISSUES AND CONCERNS:

- *Some 100' buffer subsurface removal pending temporary relocation of fencing (Unit 2).

MMRP Fieldwork Update

PROJECT: MRS-BLM (Track 3) WGBA portions unburned in 2003 wildfire (72 acres)

An MMRP action in accordance with the Track 3 ROD including vegetation clearance, technology-aided surface MEC remediation, subsurface MEC remediation in selected areas, and DGM.

Start date: March 2010

Estimated end date : TBD

PHASES:

Start

End

Site preparation

- Vegetation cutting Mech/Manual

09-08-13

11-06-13

MEC Removal

- Tech Aided Surface Removal

08-15-14

05-20-14

- Selected Subsurface Removal

TBD

05-08-14

DGM

TBD

06-01-14

ISSUES AND CONCERNS:

- Subsurface in 100 ft buffer and surface MEC removal in remainder in progress.

MMRP Fieldwork Update

Unexploded Ordnance (UXO) / Discarded Military Munitions (DMM) /
 Material Potential Presenting Explosive Hazard (MPPEH), Munitions Debris (MD), and Range Related Debris (RRD)
 Summary

<u>Detonation</u>	<u>Location</u>	<u>Items</u>	<u>Result</u>
-------------------	-----------------	--------------	---------------

Mar 27	MRS-BLM Rng 48 (BIP)	1- 40 mm grenade	UXO
---------------	-----------------------------	-------------------------	------------

<u>RemovalArea</u>	<u>MEC</u>		
	<u>UXO/DMM</u>	<u>MD</u>	<u>RRD</u>
	<u>Items</u>	<u>lbs</u>	<u>lbs</u>
Units 6/7/10/33	193/0	24,519	48,826
FBs (permanent)	321/1	36,203	19,214
WGBA (Unburned)	40/0	3,316	16,177
100' Buffer	11/0	1,093	570

MMRP Site Security Program

- Trespass Incident Reports:

Last 30 days: 0

Year to Date: 2

- MEC Incident Reports:

Last 30 Days: 1

Year to Date: 7

April 16 – A BLM weed crew reported a missile body in Unit 21, HA37 east in vicinity of Riso Rd. Contractor ordnance safety responded and identified the item as an projectile, Rocket, 3.5 inch, practice, expended. The item was transported to MD bin for recycle.

- Community Education:

– Total recipients in 2014: 460

- MEC Rec and Safety Tng:

– Total personnel trained in 2014: 61

- Other: **Annual Track 3 Surface Monitoring fieldwork complete. Report due in September.**

Fort Ord Deliverables
MR BCT, April 23, 2014

Issue Year	Site	Document Title	Version	Issue Date	DocGroup	DocType	Author Org
2014	OE	MRS-BLM Units 4, 11 and 12 (2011 Units) Remedial Action Report, Former Fort Ord	DRAFT FINAL	2014-04-30	Primary	External	
2014	OE	BLM HQ South Buffer, Munitions and Explosives of Concern, Remedial Action, Technical Information Paper, Former Fort Ord, California	DRAFT FINAL	2014-05-30	Secondary	External	ITSI Gilbane
2014	OE	Track 2 Fritzsche Army Airfield (FAAF) Record of Decision (ROD)	FINAL	2014-05-30	Primary	External	TBD
2014	OE	Track 2 Remedial Investigation / Feasibility Study BLM Area B and MRS-16, Former Fort Ord, California	DRAFT FINAL	2014-05-30	Primary	External	ITSI Gilbane
2014	OE	Prescribed Burn 2013, MRS-BLM Units 7 and 10, After Action Report, Former Fort Ord, Monterey County, California	DRAFT FINAL	2014-05-31	Primary	External	Not Indicated
2014	OE	Superfund Proposed Plan for Munitions Response Remaining RI/FS Areas, Track 2 BLM Area B, Former Fort Ord, California	DRAFT	2014-07-30	Primary	Internal	ITSI
2014	OE	Superfund Proposed Plan for Munitions Response Remaining RI/FS Areas, Track 2 BLM Area B, Former Fort Ord, California	DRAFT FINAL	2014-10-30	Primary	Internal	ITSI
2014	OE	Superfund Proposed Plan for Munitions Response Remaining RI/FS Areas, Track 2 BLM Area B, Former Fort Ord, California	FINAL	2014-12-30	Primary	External	ITSI
2014	OE	Quality Assurance Project Plan, Superfund Response Actions, Former Fort Ord, California, Volume 2, Military Munitions Response Program, Appendix A	DRAFT	TBD	Primary	External	ITSI Gilbane
2014	OE	Quality Assurance Project Plan, Superfund Response Actions, Former Fort Ord, California, Volume 2, Military Munitions Response Program, Appendix A	DRAFT FINAL	TBD	Primary	External	ITSI Gilbane
2014	OE	Quality Assurance Project Plan, Superfund Response Actions, Former Fort Ord, California, Volume 2, Military Munitions Response Program, Appendix A	FINAL	TBD	Primary	External	ITSI Gilbane
2014	OE	Track 1 Approval Memorandum, BLM Area C	DRAFT	TBD	Primary	Internal	
2014	OE	Track 1 Approval Memorandum, BLM Area C	DRAFT FINAL	TBD	Primary	External	
2014	OE	Track 1 Approval Memorandum, BLM Area C	FINAL	TBD	Primary	External	

This report shows upcoming documents for 2014.

External reports are those that are in the Administrative Record and made available to the public.

Fort Ord Real Estate Actions Update 2014-04-23

FOST 11:

1. December 2013 – FOST staffed for signature.

FOST 12:

1. December 2012 – BRAC-D executed FOST on 14 Dec.
2. January 2013 – UC requested a discussion about how comments will be addressed 2 Jan. Draft responses to UC comments prepared and reviewed by ELD. Draft responses sent to UC.
3. February 2013 – BRAC-FO and ELD met with UC on 8 Feb, comments resolved to UC's satisfaction. Army will proceed with preparing deed for the property.
4. March 2013 – submitted draft Parcel S2.1.2 groundwater CRUP to DTSC for review 12 Mar. Submitted draft UC deed to SPK-RE for review and staffing to SPK-OC 28 Mar.
5. June 2013 – SPK-OC sent revised draft UC deed to HQ-OC on 5 Jun. HQ-OC responded with comments on 27 Jun. SPK-OC to respond by 9 Jul.
6. July 2013 – conference call between HQ-OC, SPK-OC and BRAC-FO 25 Jul to discuss deed requirements. SPK-OC finalizing deed.
7. August 2013 – UC deed finalized and submitted to SPK-RE for final review and forwarding to UC. Draft deeds for Parcels E20c.1 and E29b.3.1 sent to SPK-RE for review. Draft CRUP for Parcel S2.1.2 coordinated with DTSC.
8. September 2013 – deed forwarded to UC for execution. UC requested draft deed for review. Draft CRUP forwarded to ELD for review. Sent draft deed to UC. Negotiating CRUP language with DTSC.
9. October 2013 – DTSC executed CRUP, but did not date signature page.
10. November 2013 – per SPK-RE request, DTSC re-signed and dated signature page on 5 Nov. Call between SPK-OC, SPK-RE, ELD and BRAC-FO to discuss Parcel E20c.1 deed provisions.
11. December 2013 – deed for Parcel E20c.1 forwarded to HQ-OC for review. Received comments from UC on deed for Parcel S2.1.2.
12. January 2014 – responses to UC comments in progress. Comments received from HQ-OC.
13. February 2014 – conference call between HQ-OC, SPK-OC and BRAC-FO 4 Feb to discuss Parcel E20c.1 deed requirements. Follow up conference call between ELD, HQ-OC, SPK-OC and BRAC-FO 12 Feb.
14. March 2014 – ELD consulting with OGC on deed provisions specific to Parcel E20c.1. BRAC-FO revised Parcel E29b.3.1 deed to conform to Parcel E20c.1 deed and sent to SPK-RE and SPK-OC. SPK-OC contacted UC regarding minor revisions to deed for Parcel S2.1.2.
15. April 2014 – SPK-OC reviewing Parcel E29b.3.1 deed, revising Parcel S2.1.2 deed for resubmission to UC. Conference call 18 Apr between ELD, HQ-OC, SPK-OC and BRAC-FO to resolve questions about HMP language in deeds.

FOSET 4:

1. November 2008 – ROD for Del Rey Oaks MRA complete and signed.
2. July 2010 – Del Rey Oaks submitted letter to DTSC requesting variance to the CRUP. Draft Final Remedial Design/Remedial Action Work Plan issued.
3. August 2010 – USEPA determined all remedial actions implemented and completed.
4. February 2012 – Redevelopment Agency transferred property to the City. The City sent a letter to DTSC requesting a termination of restrictions.
5. September 2012 – CRUP amendment recorded 17 Sep.
6. January 2013 – conference call with BRAC-FO, SPK-OC, ELD. SPK-OC made additional revisions to deed amendment. BRAC-FO and ELD reviewed and returned to SPK-OC 31 Jan.
7. April 2013 – USACE HQ considers term "deed amendment" inappropriate. Per Monterey County Recorder's Office, "deed correction" or a replacement deed would be acceptable.
8. June 2013 – HQ-OC noted the deed is not a "living document" and cannot be revised or corrected; however, Army can release deed restrictions (though the instrument for doing this was not specified).

Fort Ord Real Estate Actions Update 2014-04-23

9. October 2013 – SPK-RE forwarded to BRAC-FO direction from USACE HQ for CERCLA Warranty.
10. January 2014 – BRAC-FO revised CERCLA Warranty document and prepared supplemental deed “quitclaiming” property restrictions and submitted to SPK-OC for review.

FOSET 5:

1. January 2014 – FORA notified FO-BRAC of errors in deed amendments for ESCA property in Parker Flats and County North. FORA stated the ultimate grantees (County of Monterey, Monterey Peninsula College and the State of California) will not accept the property until these errors are corrected.
2. February 2014 – FORA provided sample deed amendments for executing the corrections and requested a schedule for completing the correction process.
3. March 2014 – conference call between FO-BRAC, SPK-RE and SPK-OC. SPK-OC prepared “Scrivener's Affidavits,” an instrument that identifies and corrects the errors. FO-BRAC consulted with Monterey County Recorder’s Office, which stated Affidavits were not the appropriate instrument. FO-BRAC prepared correction cover pages per County Recorder’s instructions and sent to FORA on 19 Mar.

Parcel L20.4 (Oil Well Rd) transfer to BLM:

1. December 2012 – BRAC-FO executed ECP Update Report. Submitted to SPK with all supporting documents.
2. July 2013 – SPK-RE forwarded transfer assembly to USACE HQ. USACE HQ sent changes tracked letter of transfer (LOT) back to SPK-RE, requested changes be accepted and list of enclosures be updated.
3. August 2013 – SPK-RE sent LOT back to USACE HQ 3 Aug for coordination with DASA (IH&P).
4. January 2014 – signature authority for LOT delegated to USACE HQ Director of Real Estate.
5. March 2014 – USACE HQ Director of Real Estate resigned. Interim Director does not have signature authority.

Report Status - OE & FOST

4.23.2014

<u>Issue Year</u>	<u>Site</u>	<u>Document Title</u>	<u>DocType</u>	<u>Version</u>	<u>Proposed Issue Date</u>	<u>Issue Date Status</u>	<u>Comments Due</u>	<u>Note:</u>
TBD	OE-TK3ImpactArea	MRS-BLM Non-Burn Fuelbreaks Technical Information Paper (RTD)	External	Draft		TBD		
TBD	OE-TK3ImpactArea	MRS-BLM Non-Burn Fuelbreaks Technical Information Paper (RTD)	External	Draft Final				
TBD	OE-TK3ImpactArea	MRS-BLM Non-Burn Fuelbreaks Technical Information Paper (RTD)	External	Final				
2014	OE-TK3ImpactArea	MRS-BLM Non-Burn 100ft Buffer S of BLMHQ Technical Information Paper (RTD)	External	Draft	7-Feb-14	Issued	12-Mar-14	EPA cmt 3/12. DTSC comments are pending.
2014	OE-TK3ImpactArea	MRS-BLM Non-Burn 100ft Buffer S of BLMHQ Technical Information Paper (RTD)	External	Draft Final	23-May-14		26-Jun-14	
2014	OE-TK3ImpactArea	MRS-BLM Non-Burn 100ft Buffer S of BLMHQ Technical Information Paper (RTD)	External	Final	26-Jul-14			
2013	OE-TK3ImpactArea	MRS-BLM Non-Burn 100ft Buffer MOUT Technical Information Paper (RTD)	External	Draft	26-Nov-13	Issued	6-Jan-14	EPA comments 1/14; DTSC 2/24
2014	OE-TK3ImpactArea	MRS-BLM Non-Burn 100ft Buffer MOUT Technical Information Paper (RTD)	External	Draft Final	31-Mar-14	Issued	5-May-14	
2014	OE-TK3ImpactArea	MRS-BLM Non-Burn 100ft Buffer MOUT Technical Information Paper (RTD)	External	Final	4-Jun-14			
2013	OE-TK3ImpactArea	MRS-BLM Units 4, 11 and 12 (2011 Units) Remedial Action Report	External	Draft	31-Oct-13	Issued	5-Dec-13	EPA cmts 12/9, DTSC cmt 1/3/2014
2014	OE-TK3ImpactArea	MRS-BLM Units 4, 11 and 12 (2011 Units) Remedial Action Report	External	Draft Final	30-Apr-14		3-Jun-14	DGM QA report will be added. Issue date was extended to address DTSC comments.
2014	OE-TK3ImpactArea	MRS-BLM Units 4, 11 and 12 (2011 Units) Remedial Action Report	External	Final	3-Jul-14			
2014	OE-TK3ImpactArea	MRS-BLM Unit 6 (2013 Unit) Technical Memorandum	External	--	27-Feb-14	Issued	3-Apr-14	Agency review schedule confirmed for 4/3. EPA cmt 4/3. DTSC comments are pending.
2014	OE-TK3ImpactArea	MRS-BLM Units 7 and 10 (2013 Units) Prescribed Burn After Action Report (w/Air Monitoring and Community Notification)	External	Draft	21-Mar-14	Issued	29-Apr-14	
2014	OE-TK3ImpactArea	MRS-BLM Units 7 and 10 (2013 Units) Prescribed Burn After Action Report (w/Air Monitoring and Community Notification)	External	Draft Final	29-May-14		2-Jul-14	
2014	OE-TK3ImpactArea	MRS-BLM Units 7 and 10 (2013 Units) Prescribed Burn After Action Report (w/Air Monitoring and Community Notification)	External	Final	1-Aug-14			
2014	OE-TK3ImpactArea	Impact Area MRA Surface Remediation Area Annual Monitoring Report (2014)	External	--	30-Sep-14			

Report Status - OE & FOST

4.23.2014

<u>Issue Year</u>	<u>Site</u>	<u>Document Title</u>	<u>DocType</u>	<u>Version</u>	<u>Proposed Issue Date</u>	<u>Issue Date</u> <u>Status</u>	<u>Comments</u> <u>Due</u>	<u>Note:</u>
2013	OE-RemainingAreas	Track 2 ROD MRS-34 (FAAF)	Internal	Draft	5-Aug-13	Issued	30-Nov-13	DTSC letter received. EPA comment 11/21.
2014	OE-RemainingAreas	Track 2 ROD MRS-34 (FAAF)	Internal	Draft Final	31-Jan-14	Issued	30-Apr-14	EPA letter 3/5. Review period was extended.
2014	OE-RemainingAreas	Track 2 ROD MRS-34 (FAAF)	External	Final (signature process)	30-May-14		29-Jun-14	
TBD	OE-RemainingAreas	Track 1 Plug-In Approval Memorandum BLM Area C	Internal	Draft (agencies)		TBD		
TBD	OE-RemainingAreas	Track 1 Plug-In Approval Memorandum BLM Area C	External	Draft Final (public review)				
TBD	OE-RemainingAreas	Track 1 Plug-In Approval Memorandum BLM Area C	External	Final (RTC)				
2013	OE-RemainingAreas	Track 2 RI/FS BLM Area B & MRS-16	External	Draft	22-Nov-13	Issued	27-Feb-14	Extended by 30 days. EPA cmt 1/15, DTSC 3/3, CAG 2/27, BLM 3/6
2014	OE-RemainingAreas	Track 2 RI/FS BLM Area B & MRS-16	External	Draft Final	23-May-14		22-Jun-14	
2014	OE-RemainingAreas	Track 2 RI/FS BLM Area B & MRS-16	External	Final	22-Jul-14			
2013	OE-LUCs	Track 2 Del Rey Oaks MRA Annual Monitoring Report (2011-12)	External	--	30-Sep-13			Reported by FORA per LUC monitoring MOU; reports compiled in OTH-255
2014	OE-LUCs	Track 2 Del Rey Oaks MRA Annual Monitoring Report (2012-13)	External	--	30-Sep-14			Reported by FORA per LUC monitoring MOU; reports compiled in OTH-255
2014	OE-LUCs	MRS Security Program Annual Report (2013)	External	--	30-Jun-14			
TBD	FOST	FOSET4 (DRO) CERCLA warranty document	External	--		TBD		

Fort Ord Munitions Response BCT Meeting Summary of Action Items (March 20, 2014)

Action Item Description Action Party Due Date Comments

Site Security/Incident Reports/Detonations

Field Work/Removal Action Updates/FWVs

C	Identify participants to a discussion of meteorological modeling by DTSC and MBUAPCD.	Army	3/14/2014	
*	Provide clarification on the process for accepting equipment purchased through DSMOA.	Army	Next meeting (3/20/2014)	

FFA Schedules, MR RI/FS, Remedial LUCs

	Provide clarification on BLM participation in remedial decision for BLM Area B and MRS-16.	Army	Next meeting (3/20/2014) (4/23/2014)	
C	Confirm agency review schedule for Unit 6 Technical Memorandum.	Army	3/7/2014	
R	Confirm agency review schedule for Units 4/11/12 draft responses to comments.	Army	3/31/2014	(Mar2014) Confirm schedule after DTSC site tour on 3/20.
	Update the FFA schedule for MRS-34.	Army	3/31/2014	

Property Transfer

	FOSETs 1/4/5 CERCLA warranty document and deed correction: the Army will provide EPA and DTSC copies when final.	Army		(Sep2011) Deed Amendments for FOSET5 County North, FOSET5 Parker Flats properties and for FOSET2 properties have been provided to the agencies. Associated letters (for AR) have been provided to EPA, DTSC and FORA.
--	--	------	--	---

* indicates new action item
 "R" indicates revised action item
 "C" and gray cells indicate completed items to be withdrawn from list next month

**Fort Ord Munitions Response BCT Meeting
Summary of Action Items (March 20, 2014)**

Action Item Description Action Party Due Date Comments

Ongoing Actions/Other

	Monthly 3-month deliverables schedule review at BCT meetings	All	Monthly	The Army to work on formatting to meet agency needs.
	Finalize MR BCT minutes from December 6.	Army	Monthly	
	Finalize MR BCT minutes from January 22.	Army	Monthly	
	Finalize MR BCT minutes from February 28.	Army	Monthly	
*	Finalize MR BCT minutes from March 20.	Army	Monthly	

* indicates new action item
 "R" indicates revised action item
 "C" and gray cells indicate completed items to be withdrawn from list next month

← April 2014 →						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		<u>1</u>	<u>2</u>	<u>3</u>	<u>4</u>	<u>5</u>
<u>6</u>	<u>7</u>	<u>8</u>	<u>9</u>	<u>10</u>	<u>11</u>	<u>12</u>
<u>13</u>	<u>14</u>	<u>15</u>	<u>16</u> MR IPM (10 am) HTW IPM (1:30)	<u>17</u>	<u>18</u>	<u>19</u>
<u>20</u>	<u>21</u>	<u>22</u>	<u>23</u> MR BCT (10 am) HTW BCT (1:30 pm)	<u>24</u> GW Mtg (10 am)	<u>25</u>	<u>26</u>
<u>27</u>	<u>28</u>	<u>29</u>	<u>30</u>			

← May 2014 →						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				<u>1</u> MR IPM (10:00 am)	<u>2</u>	<u>3</u>
<u>4</u>	<u>5</u>	<u>6</u>	<u>7</u> HTW IPM (10 am)	<u>8</u>	<u>9</u>	<u>10</u>
<u>11</u>	<u>12</u>	<u>13</u>	<u>14</u>	<u>15</u>	<u>16</u> MR BCT (10 am) HTW BCT (1:30 pm)	<u>17</u>
<u>18</u>	<u>19</u>	<u>20</u>	<u>21</u>	<u>22</u>	<u>23</u>	<u>24</u>
<u>25</u>	<u>26</u>	<u>27</u>	<u>28</u>	<u>29</u>	<u>30</u>	<u>31</u>

June 2014						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

July 2014						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		
