

Fort Ord MMRP
Ahtna Status
Contract No. W9123824D003

September 9, 2026




Document Development – Task Order 1


- Unit A Prescribed Burn Plan

Version	Task Description	Dates
Final	Schedule for Delivery	TBD

Unit A MEC Remedial Actions – Task Order 3

- Unit A Prescribed Burn Preparation conducted from June 2025 to September 2025
- Demobilization of equipment completed March 2026
- Water storage tank(s) - left in place
- Dip Tanks – left in place



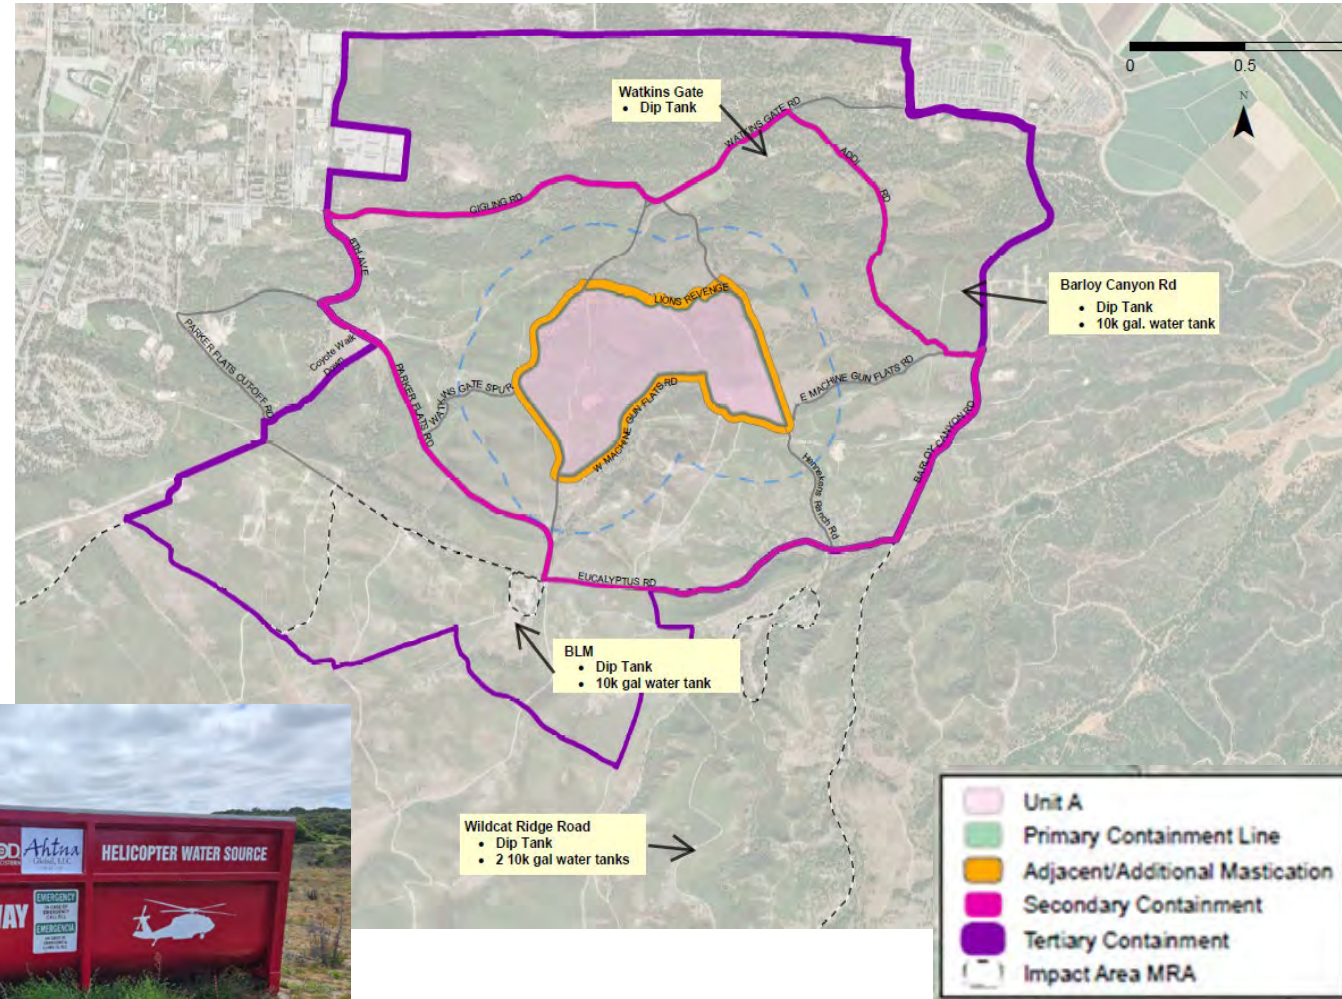


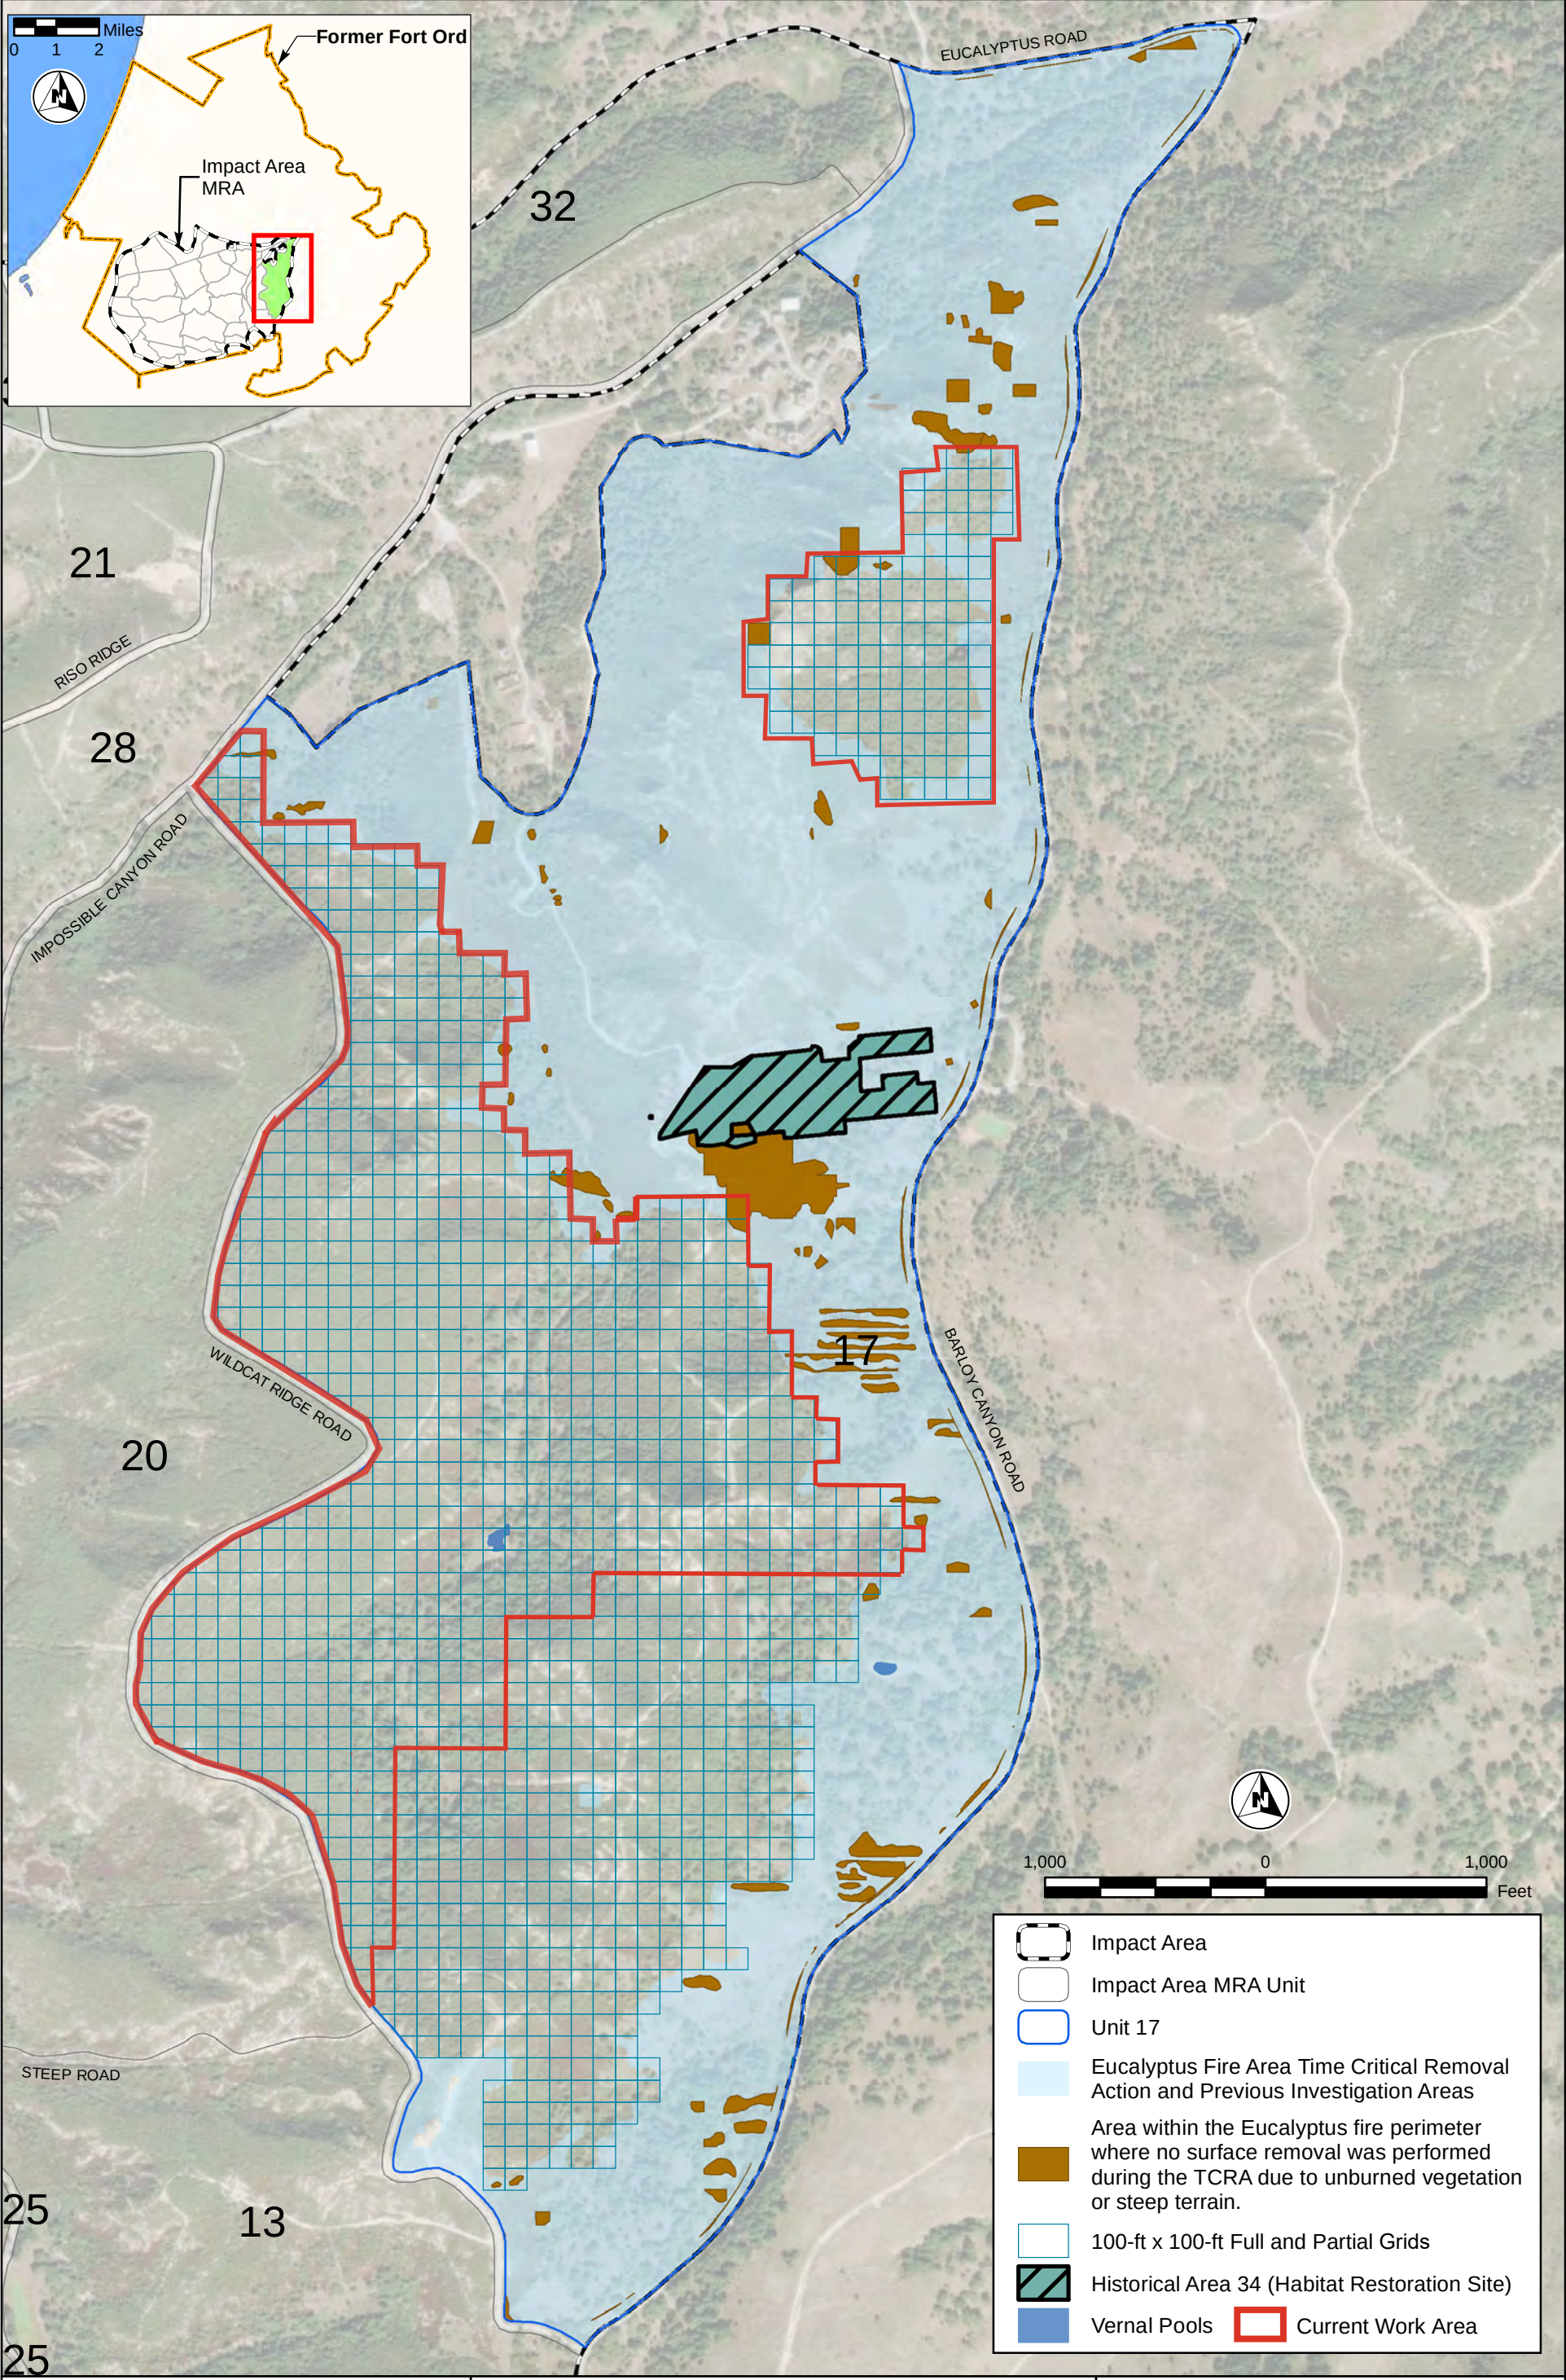

Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations - Completed to date
 - Original ~118 acres
 - Additional Vegetation Cutting
 - ~ 60 acres
 - Mechanical – May 26 - July 8, 2026
 - ~ 38 acres cut
 - Manual – June 1 - August 20, 2026
 - ~22 acres – hand cut/skid steer only
 - ~32 acres - limbing following mastication



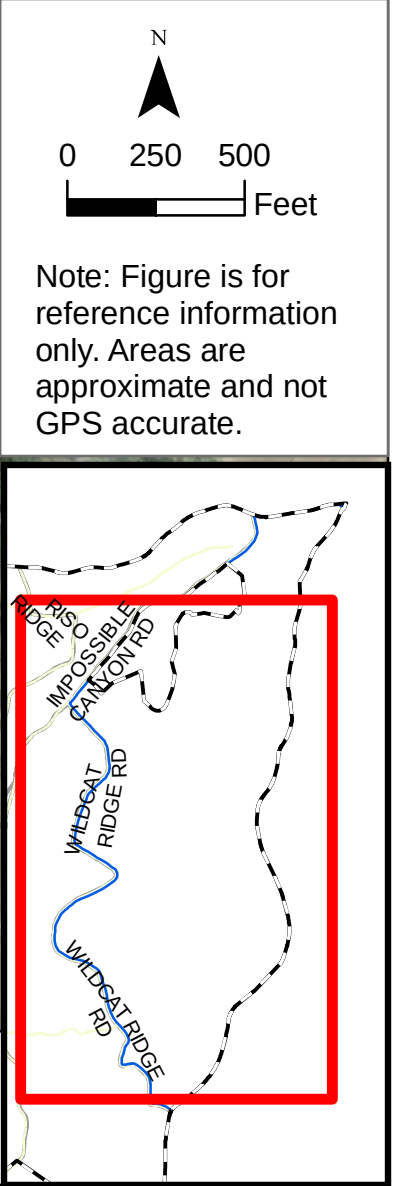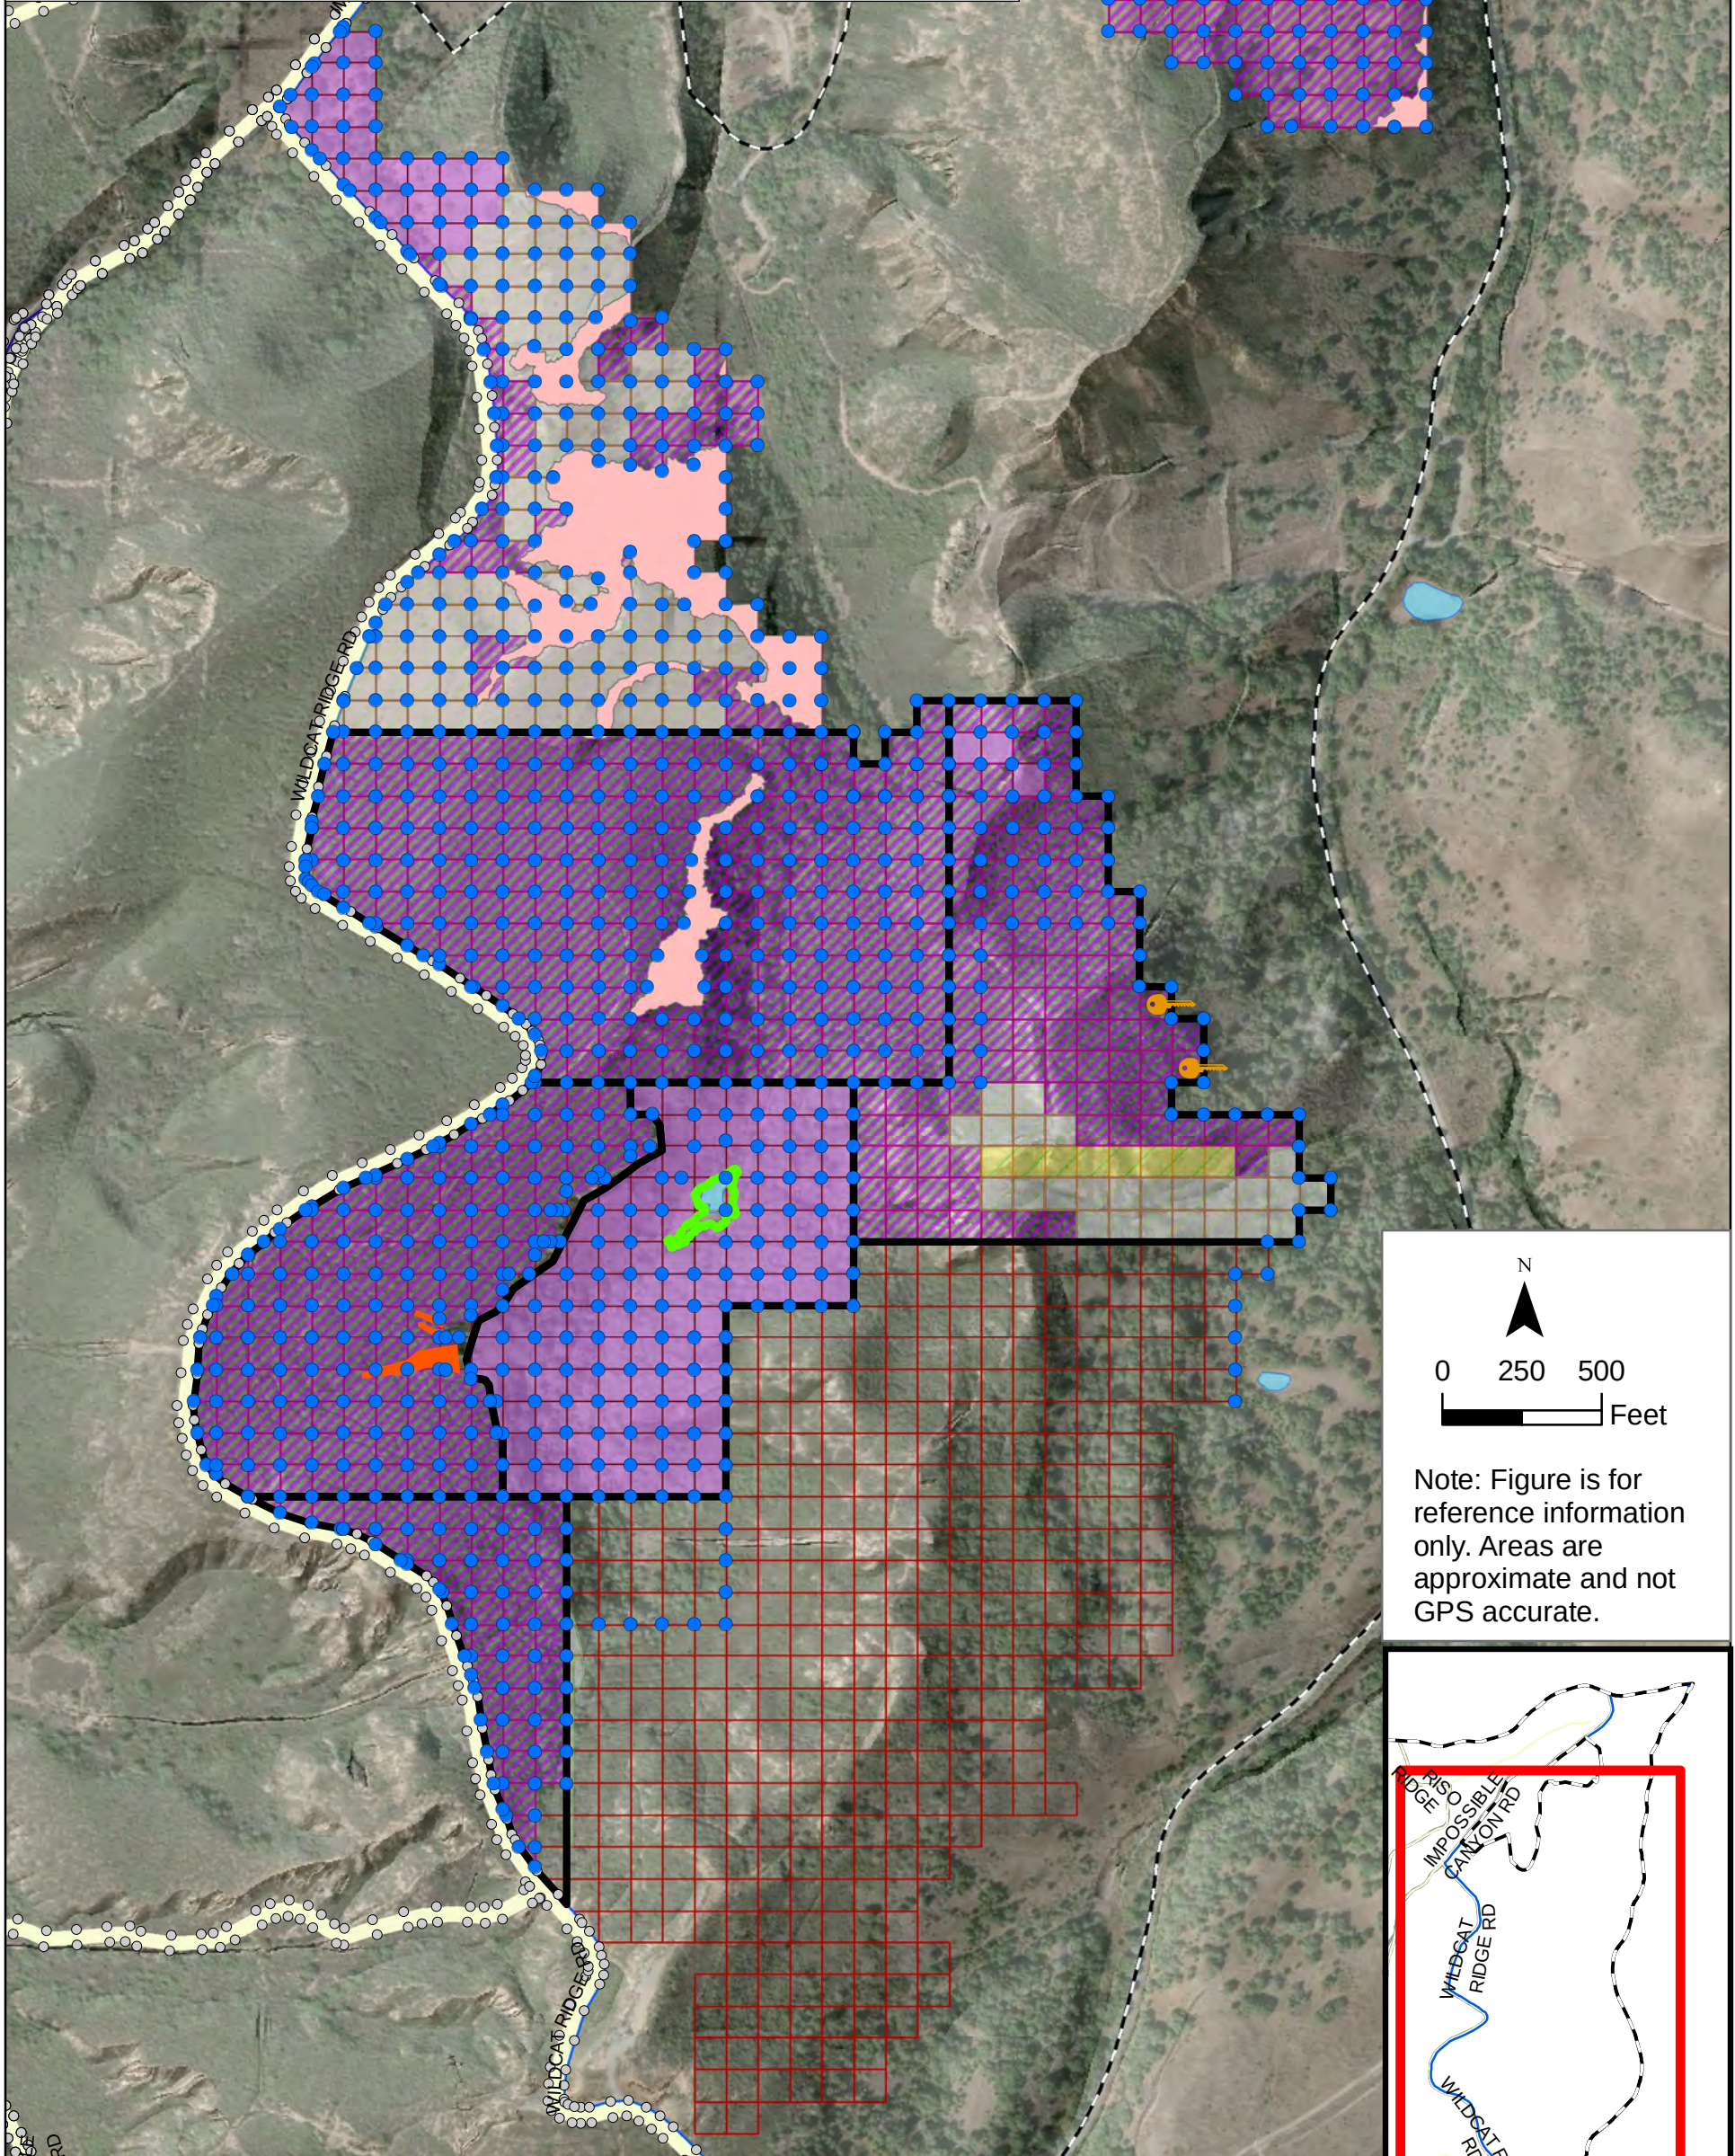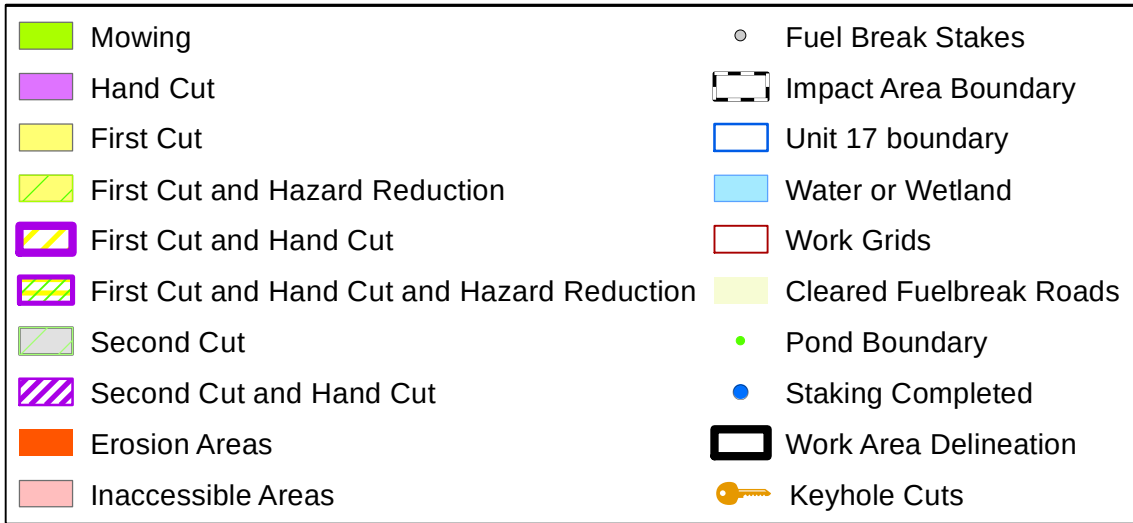

Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations - Completed To Date
 - Instrument Aided Surface MEC Removal
 - Started October 15, 2025
 - ~ 124 acres
 - ~ 118 acres initially projected, ~60 additional acres
 - Evaluating inaccessible terrain;
 - o ~13 acres inaccessible
 - 25 items recovered - acceptable to move
 - 1 – Projectile, 37mm, LE, MKII
 - 1 – Projectile, 50mm, Mortar, Type89, Japanese NI
 - 2 – Hand Grenade, Practice, MKII
 - 2 – Projectile, 40mm, HE, M383 (unfuzed)
 - 1 - Rifle Grenade, Smoke, M23 series
 - 11 – Signal, Illumination, Ground, Parachute, M19 series
 - 1 – Hand Grenade, Smoke, M18 series
 - 1- Projectile, 57mm, HE, M306 series
 - 4 – Cartridge, 20mm, TP, M55A2
 - 1 – Projectile, 75mm, Shrapnel, MKI
 - 99 BIP items recovered
 - 50 – Projectile, 40mm, HE, M383 (DMM)
 - 2 – Projectile, 40mm, HE, M383 (UXO)
 - 46 – Cartridge, 40mm, HE, M383 (DMM)
 - 1 – Fuze, Point Detonating, M535 (UXO)
 - 2,501 lbs. MD
 - 4,283 lbs. Other Debris
 - QC/QA
 - ~ 118 acres QC Complete
 - ~ 112 acres QA Complete

BIP=Blown in Place

DMM=Discarded Military Munitions


MPPEH=Material Potentially Presenting an Explosive Hazard

MD=Munitions Debris





C:\Users\Shannon.D\OneDrive\Ahtna Inc\Documents\GCs_Files\Projects\FredOrd\MEC\Unit17\Status\9160\9160\17\ASWP_0117_20250425.mxd 9/8/2026 [11:53 AM] SHESSON, AHTNA

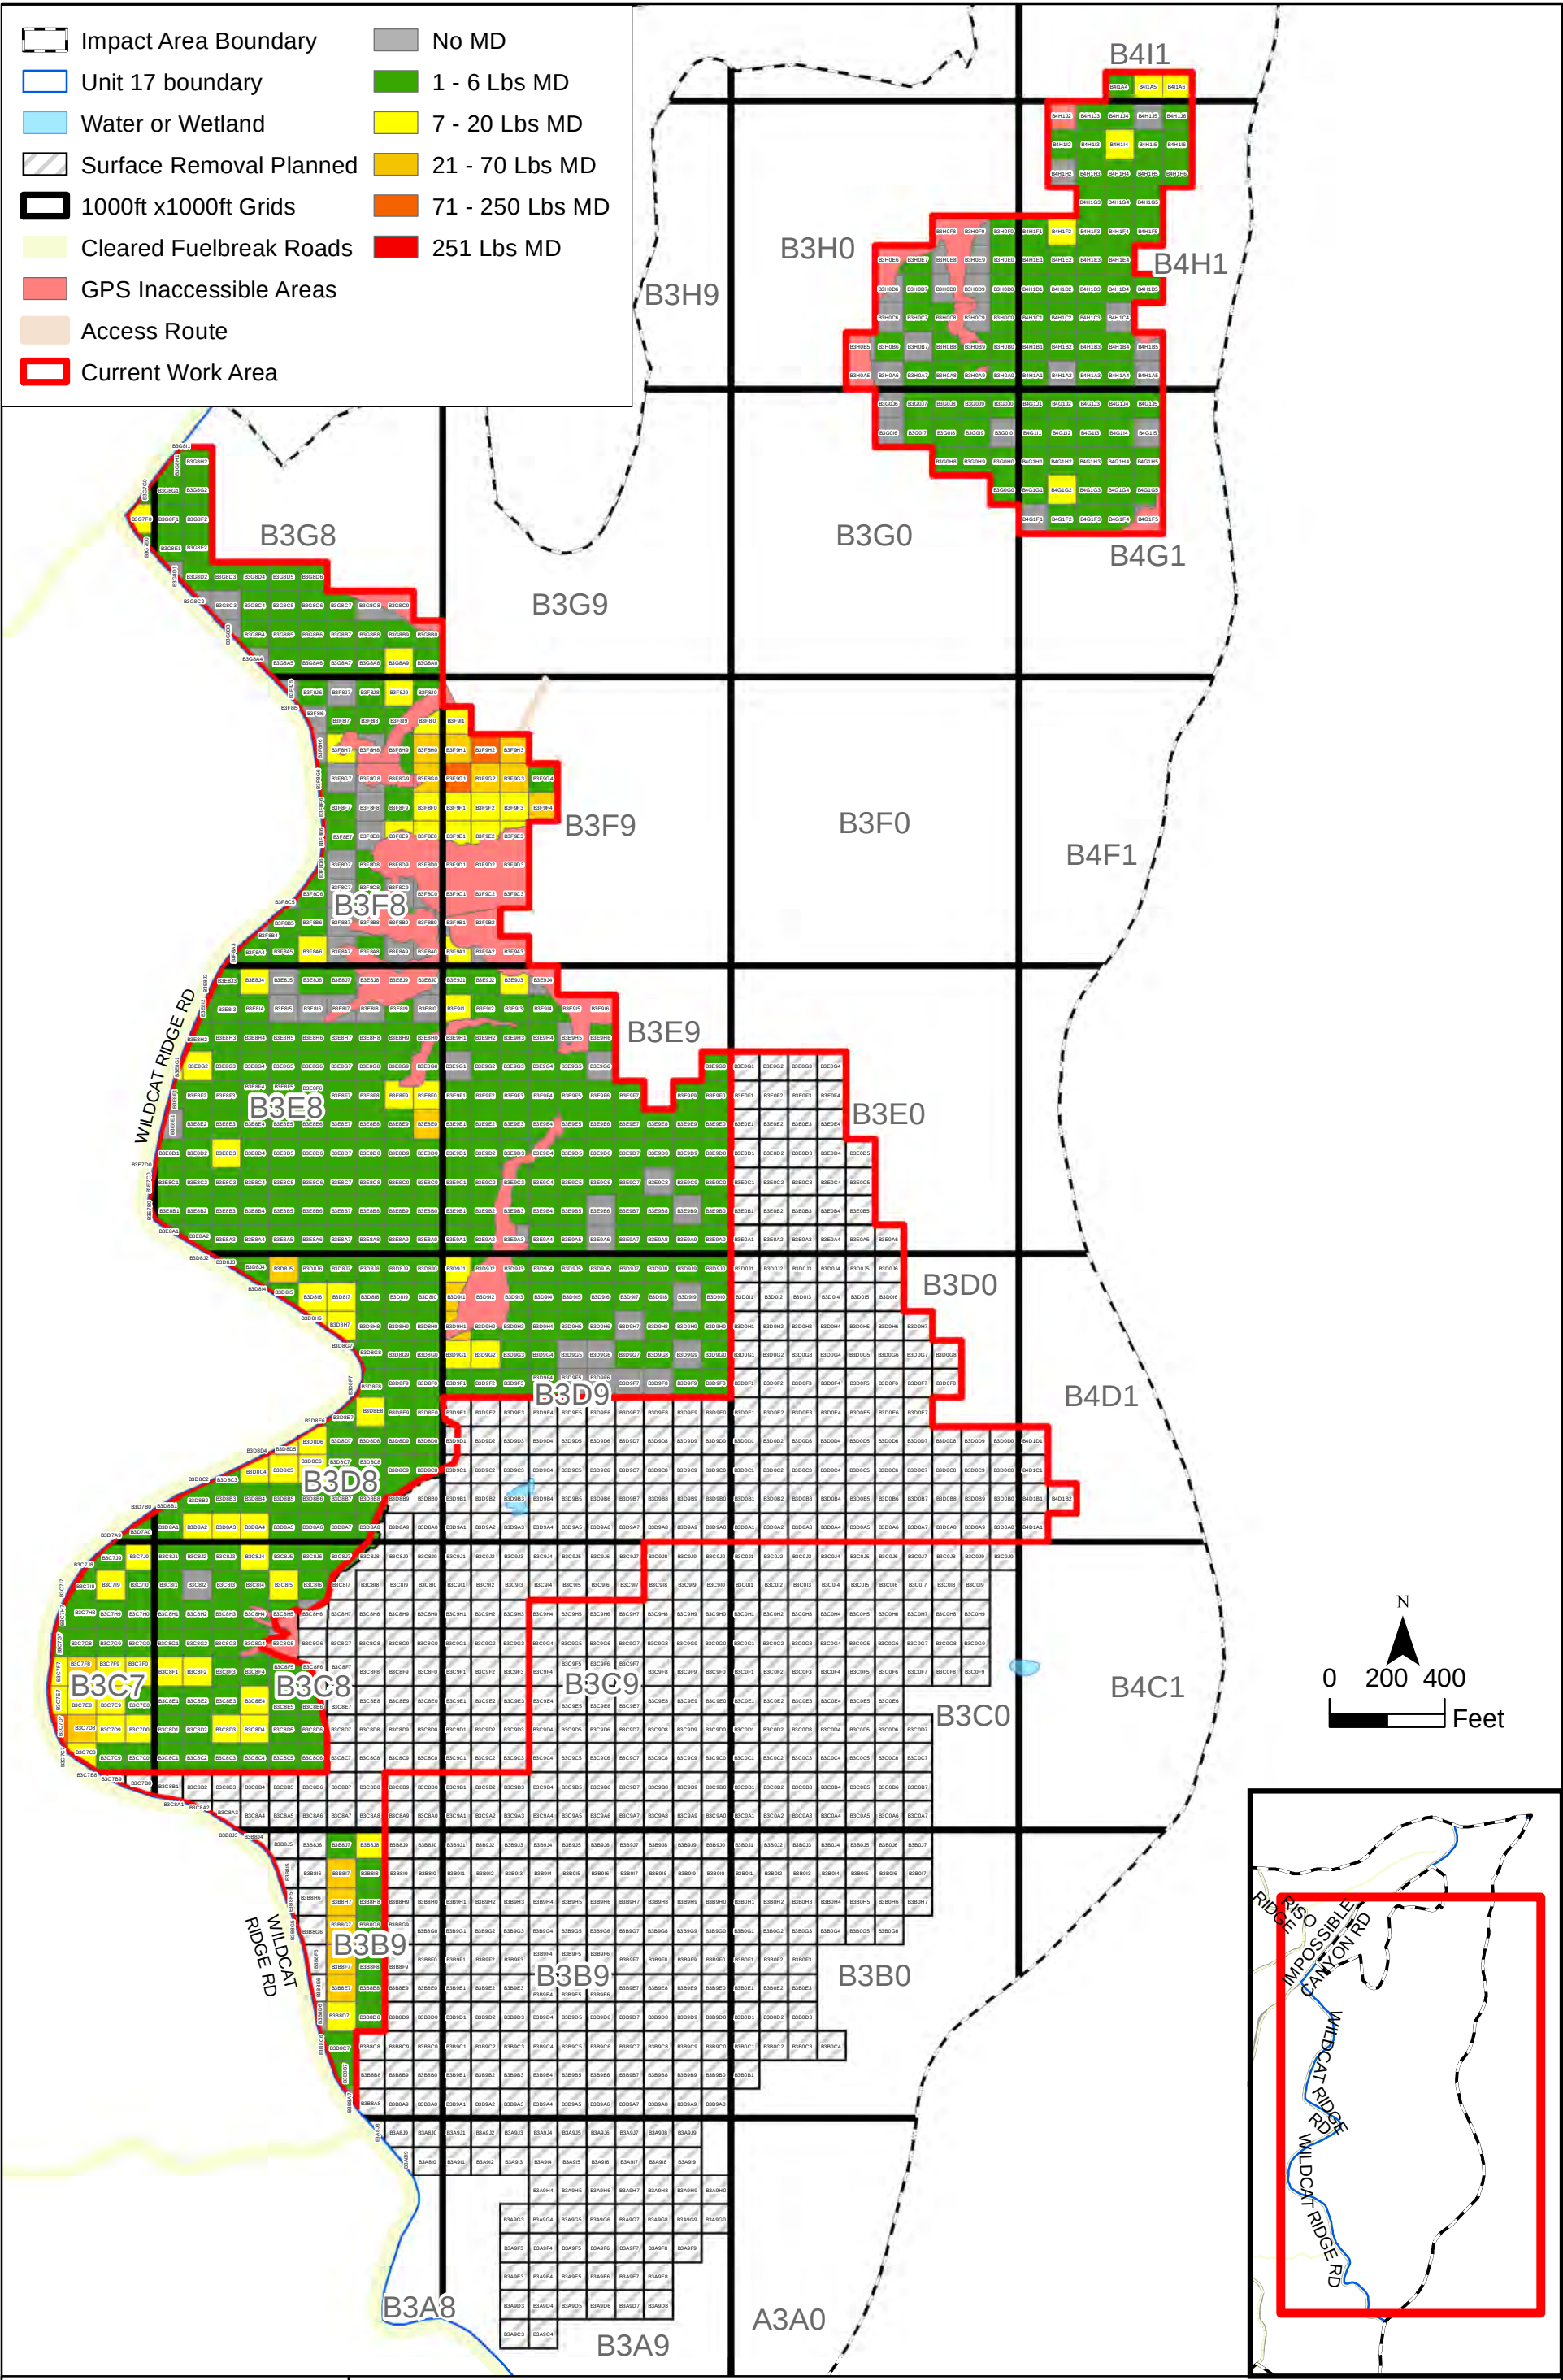

Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations
 - DGM Survey
 - Started January 28, 2026;
 - Demobilized July 30, 2026;
 - Returning October 2026
 - ~81 acres completed to date.
 - Evaluating inaccessible terrain
 - o ~27 acres inaccessible



- Impact Area Boundary

Unit 17 boundary

Water or Wetland

1000ft x1000ft Grids

Cleared Fuelbreak Roads

Surface Removal Planned

GPS Inaccessible Areas

Access Route




Current Work Area

IVS Location
- DGM Survey Status

Field Collection Complete

Data Processing Complete

DGM Inaccessible Areas

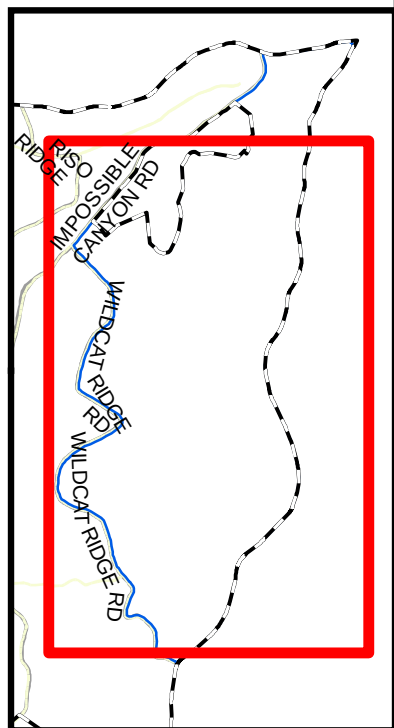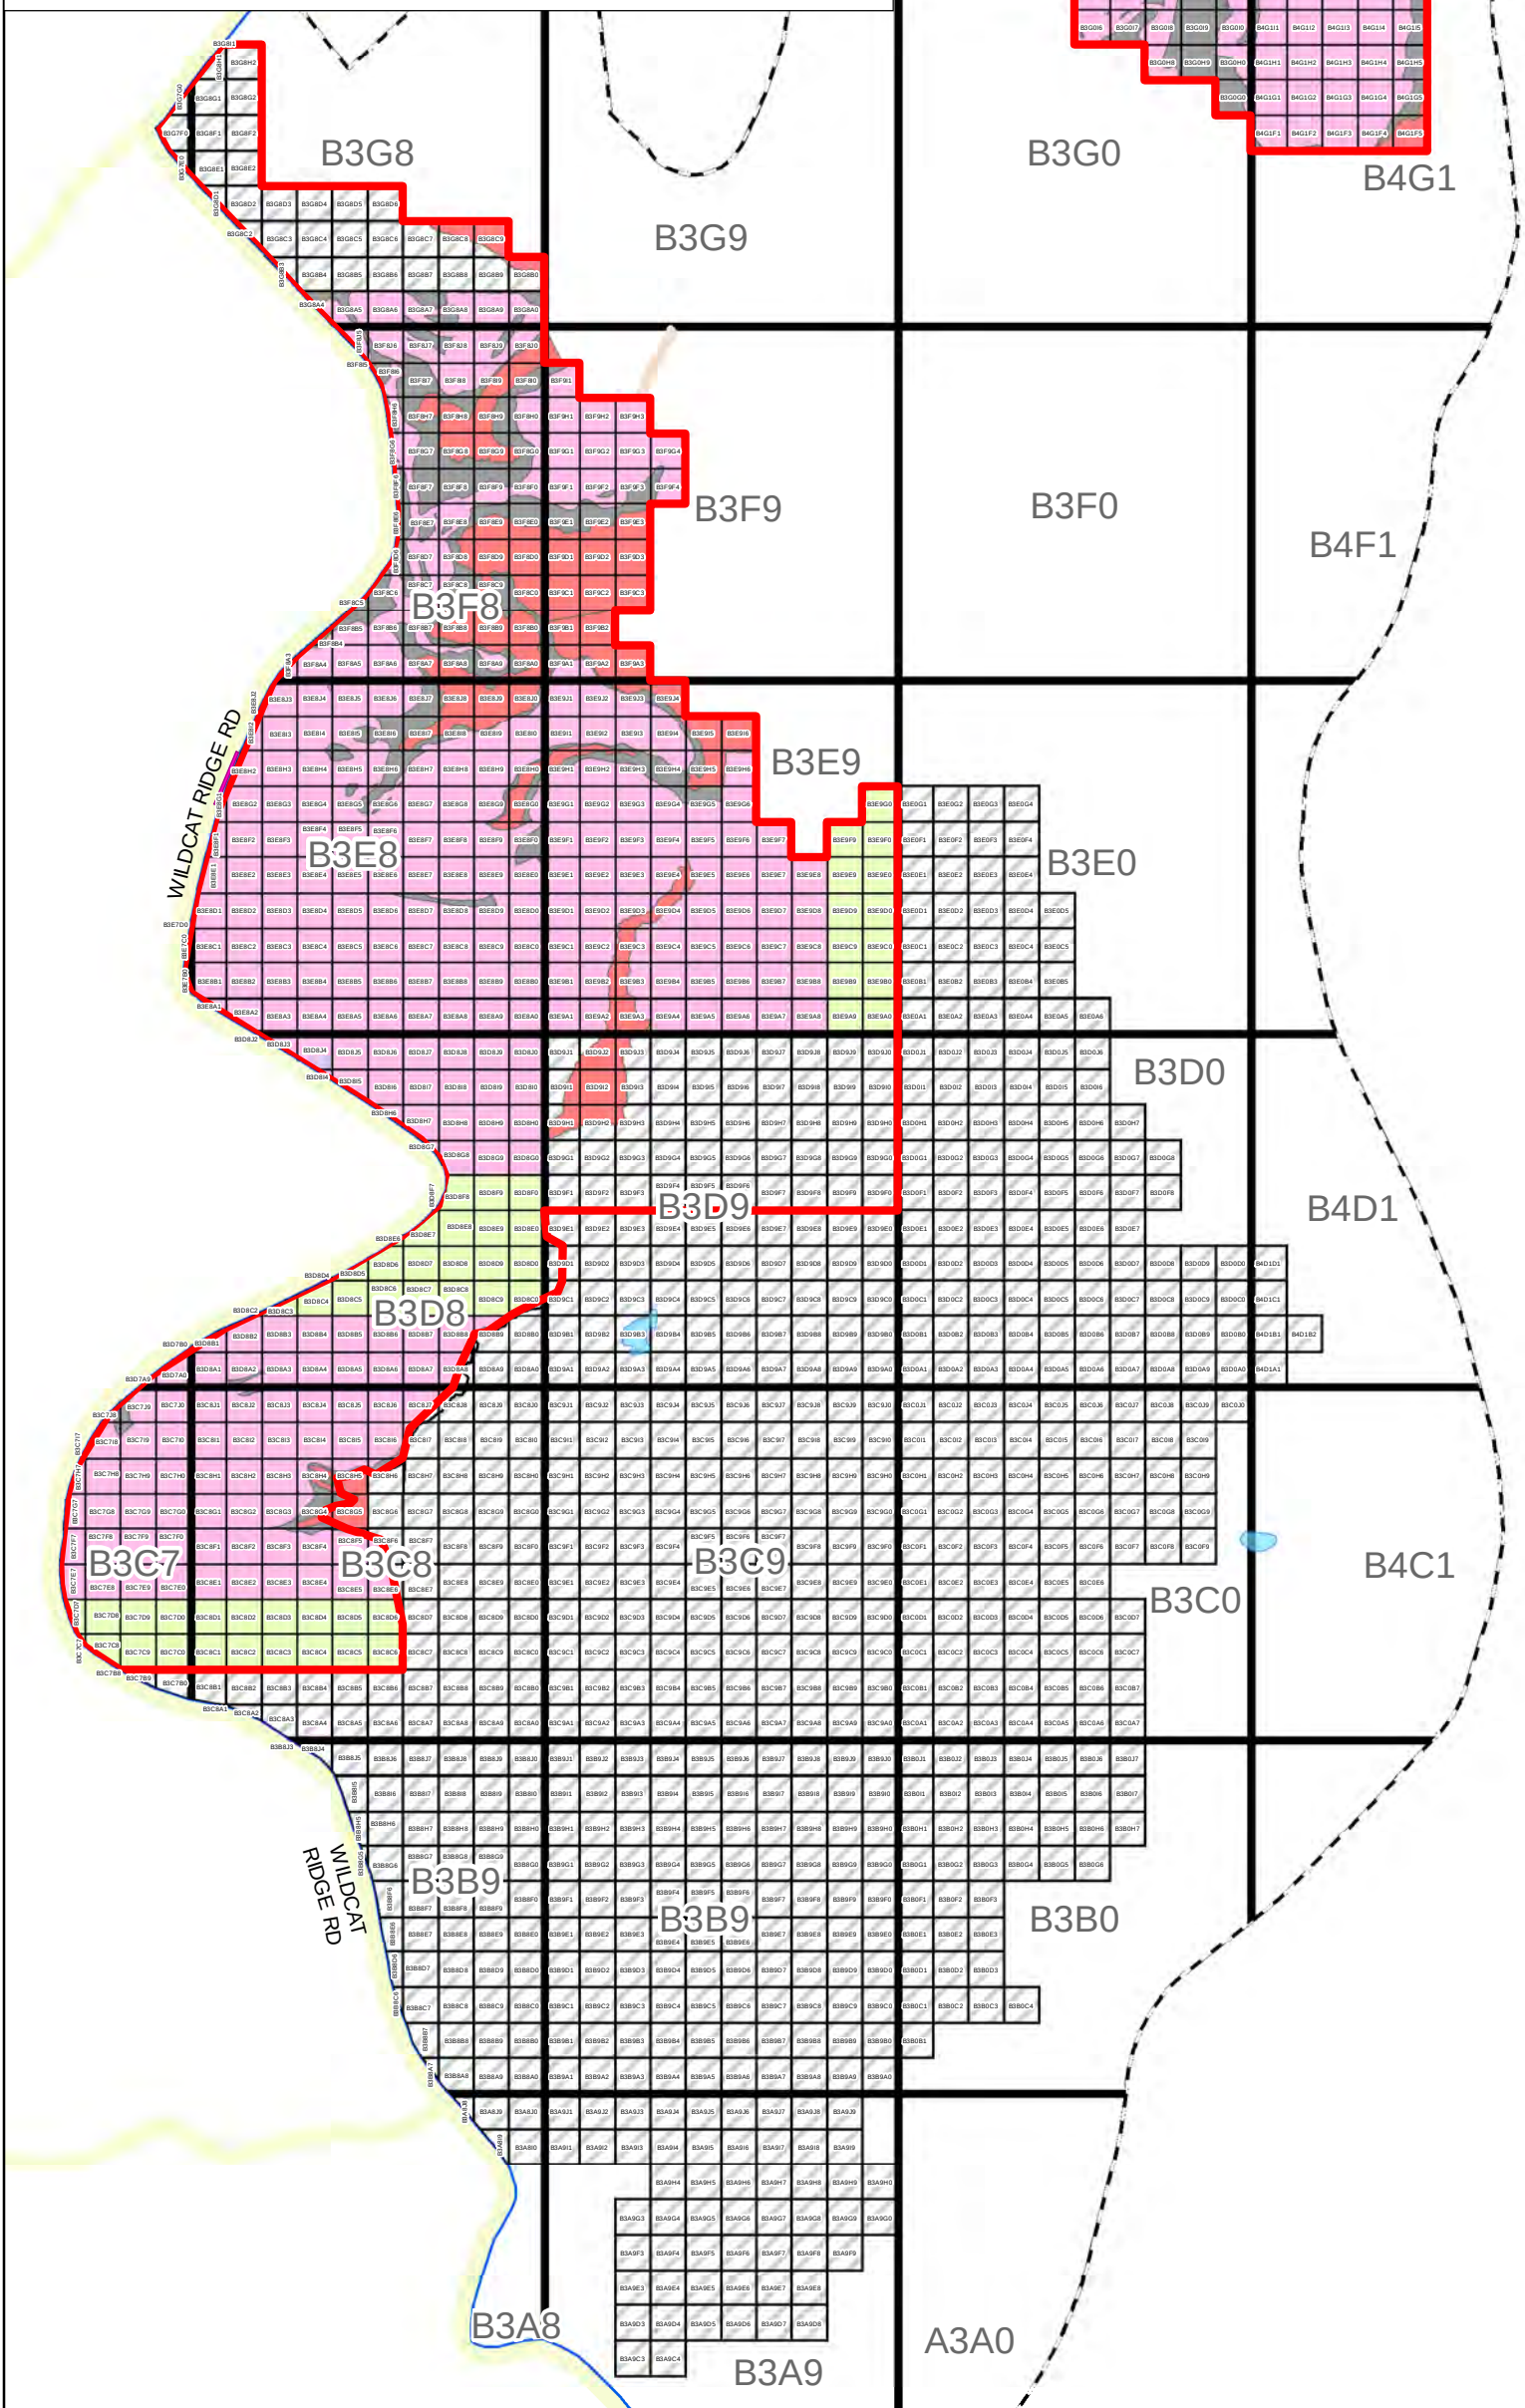

Unit 17 MEC Remedial Actions – Task Orders 2/3

- Field Operations Schedule
 - Technology Aided Surface MEC removal
 - Started October 15, 2025, expected completion in January 2027
 - DGM Survey
 - Started January 28, 2026, expected completion in January 2027
 - Basewide Range Assessment Reconnaissance Survey
 - January – February 2027

