


Fort Ord Military Munitions Response Program Update

July 2022

1. Field Activities

- Unit 5:
 - Vegetation cutting: completed in Nov-Dec 2021. Two MPPEH items (projectiles, 75mm and 8-in.) were placed in the explosives storage location.
 - Grid staking: 97% completed in Dec 2021. Remaining stakes placed week of 7/11/2022.
 - Surface removal: began 7/18/2022.
 - Digital geophysical mapping: pending.
- 2022 surface monitoring of Impact Area units:
 - Not yet scheduled.

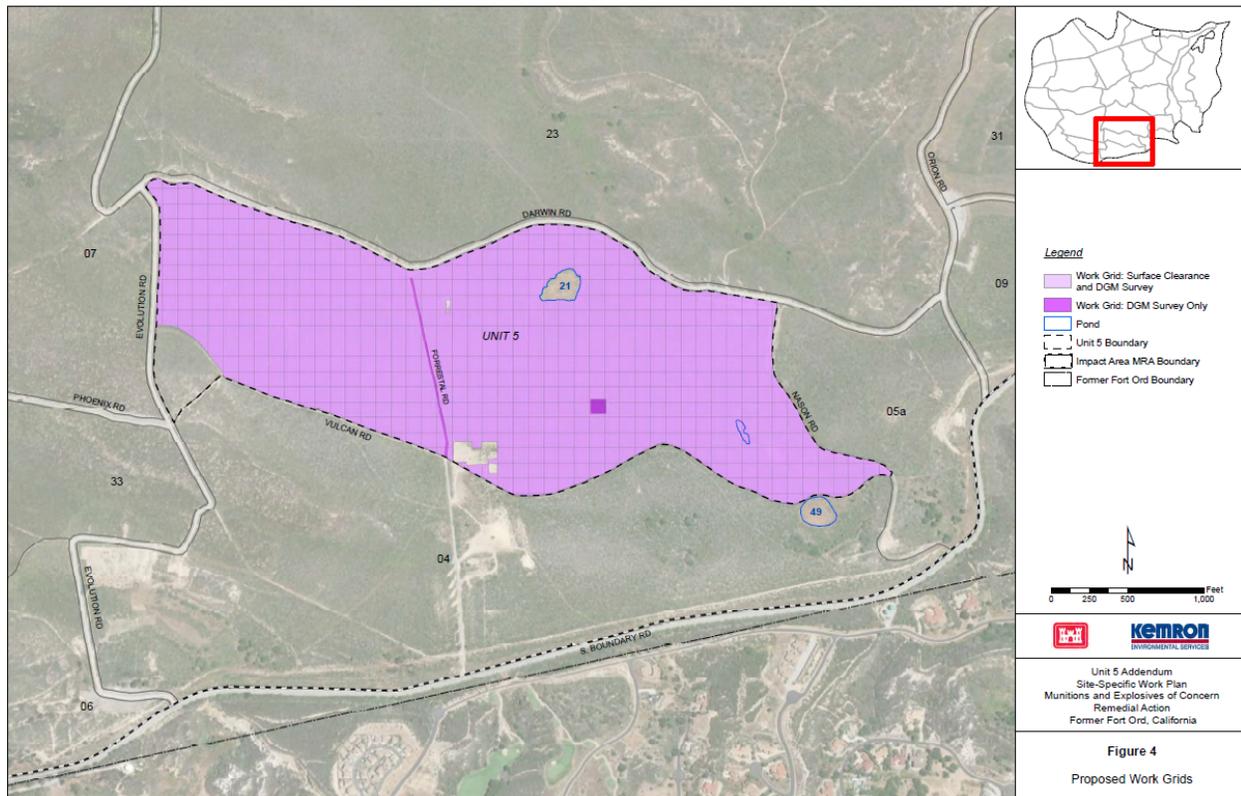

OE-0626U

Acronyms

MMRP: Military Munitions Response Program
 MPPEH: material potentially presenting an explosive hazard
